

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, Ky.	




Slack: 0"

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- FRAME & GRATE BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.


P2) 24" x 30" - CASTING HEIGHT - 4"
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 38"
1) 24" x 30" - Conseal CS-102 1.00"
1) Hole - 18
1) Hole - 20

0 lb
4425 lb
0 lb
0 lb
0 lb


Structure Total: 4425 lb

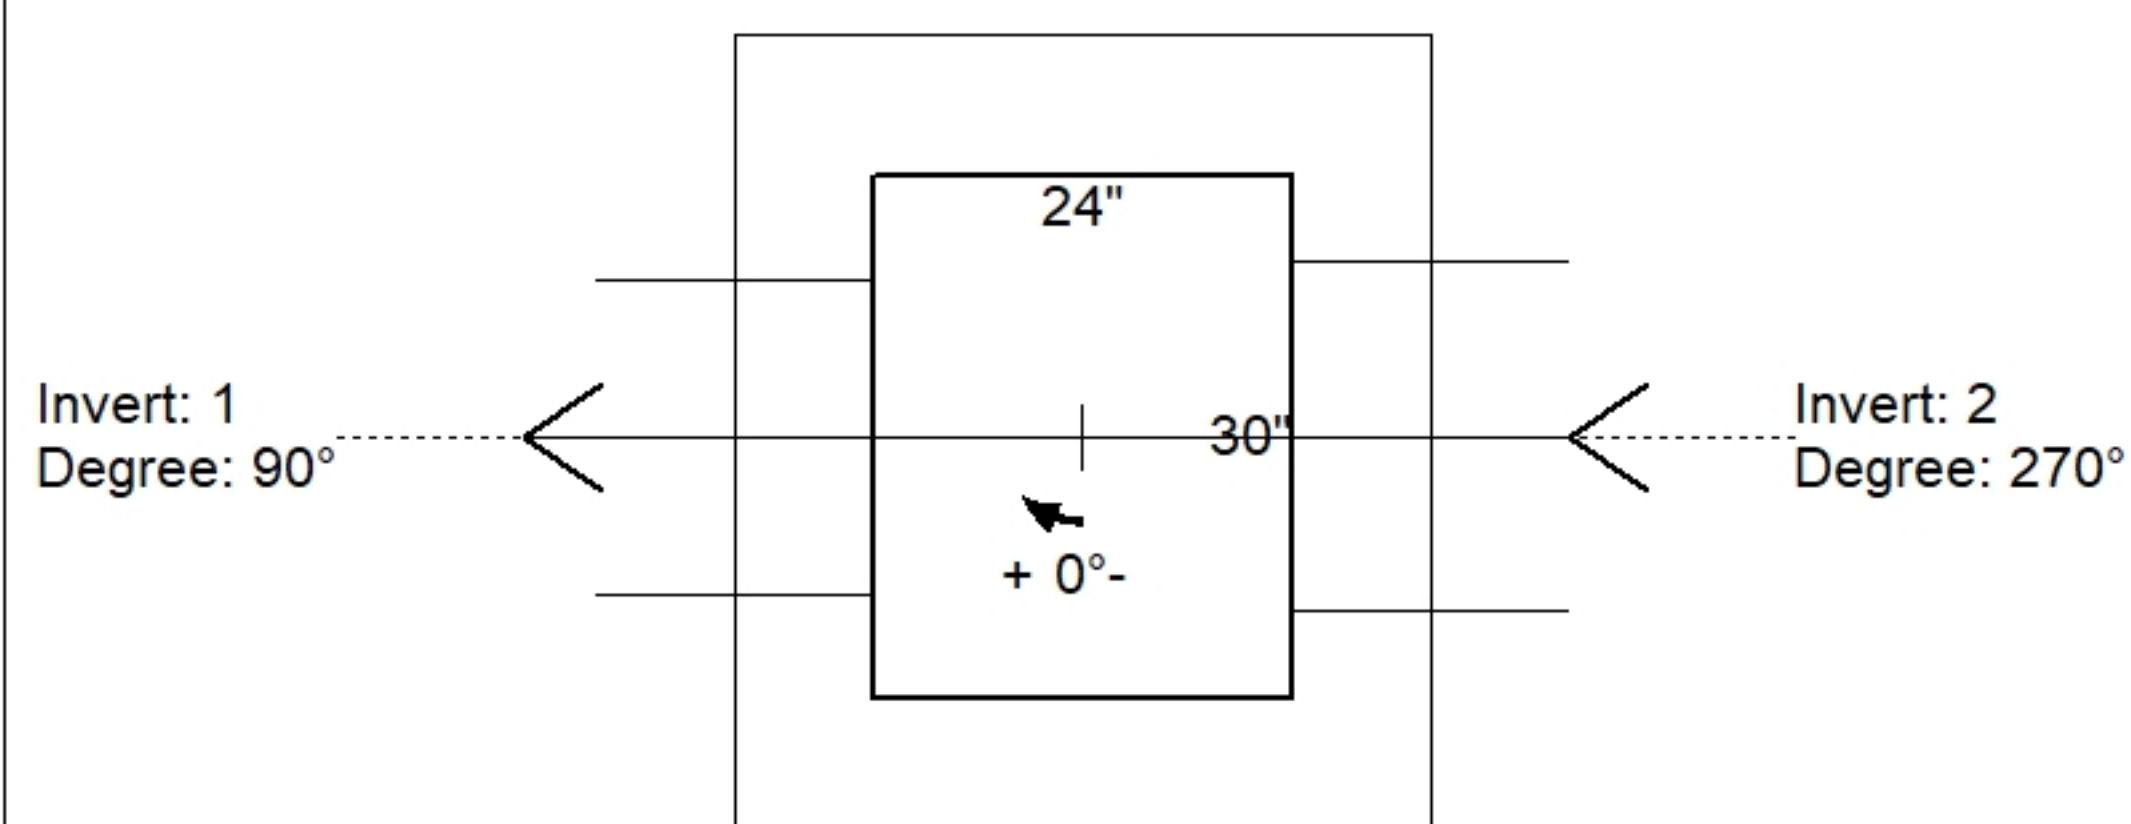

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	587.35'							
Reducer								
Invert 1	583.85'	90°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2	583.85'	270°	12" RCP B WALL	16"	20"	Hole 20	-4"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

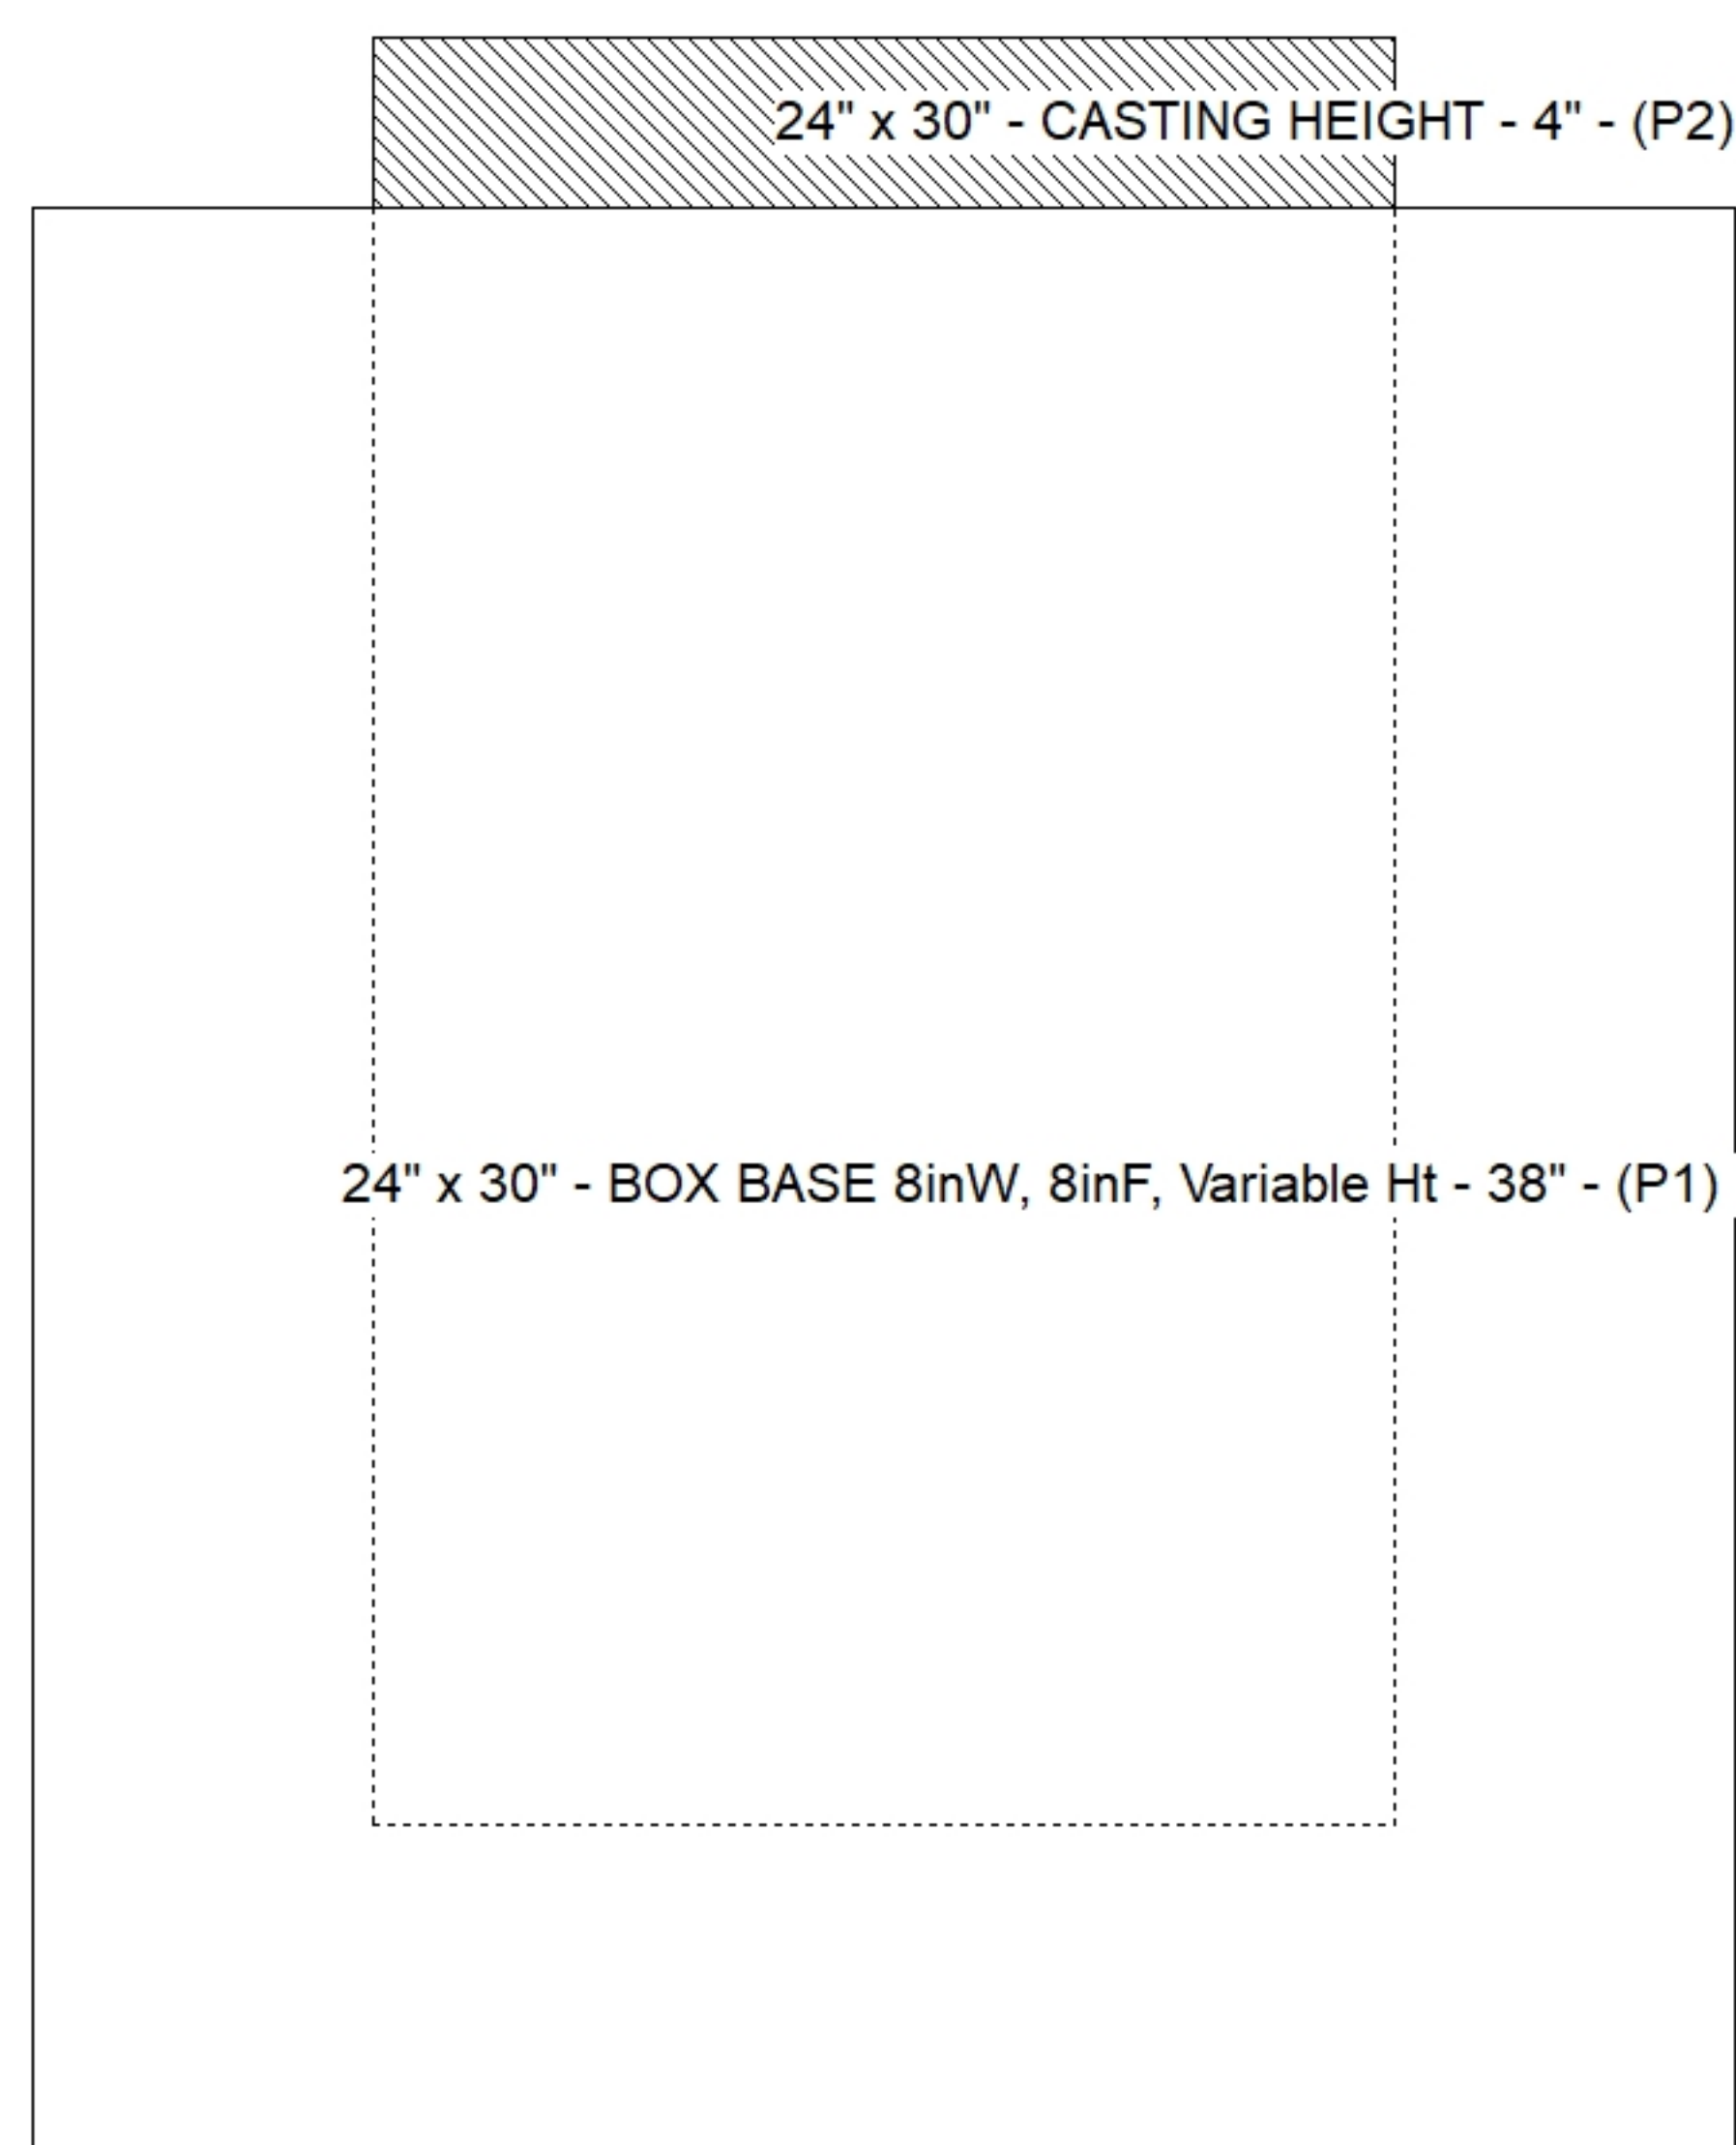

Default - Interior Dimensions

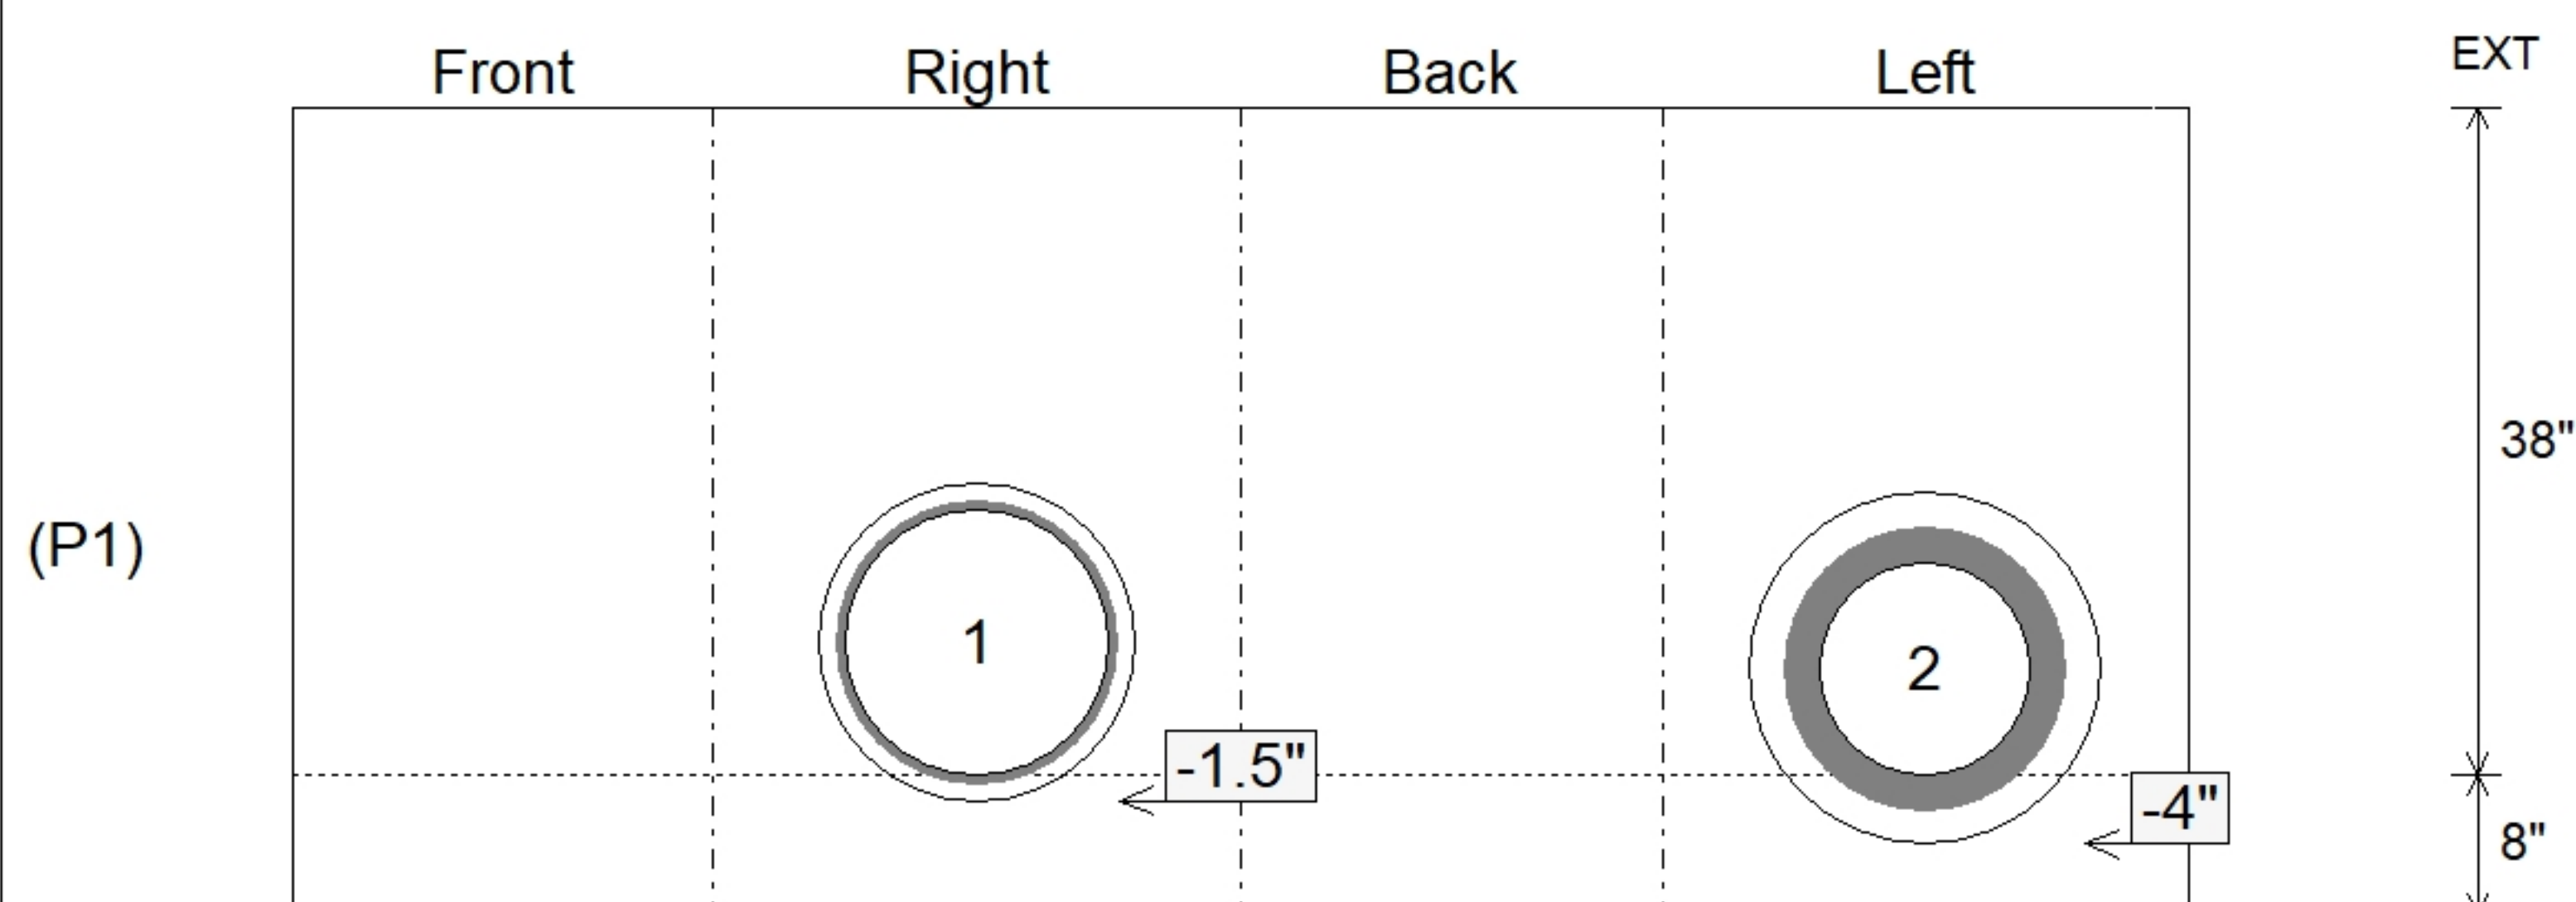

Submittal Drawing
8/18/2026 9:55:14 AM

SUBMITTAL
APPROVED BY:
