

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, Ky.	



Spec: KYTC
Type: CBI TYPE A (10')
Size: 24" x 36"

Rim: 590.08'
Invert: 583.72'
Rim to Invert: 6.36'

Sump: 0"
Floor (Top): 583.72'
Floor Height: 8"


Floor (Bot): 583.053'
Overall Height: 6.667'
Slack: 4.32"

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10"
P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 44"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 26
1) Hole - 22
2) Hole - 18


3398 lb
5270 lb
4881 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 13548 lb

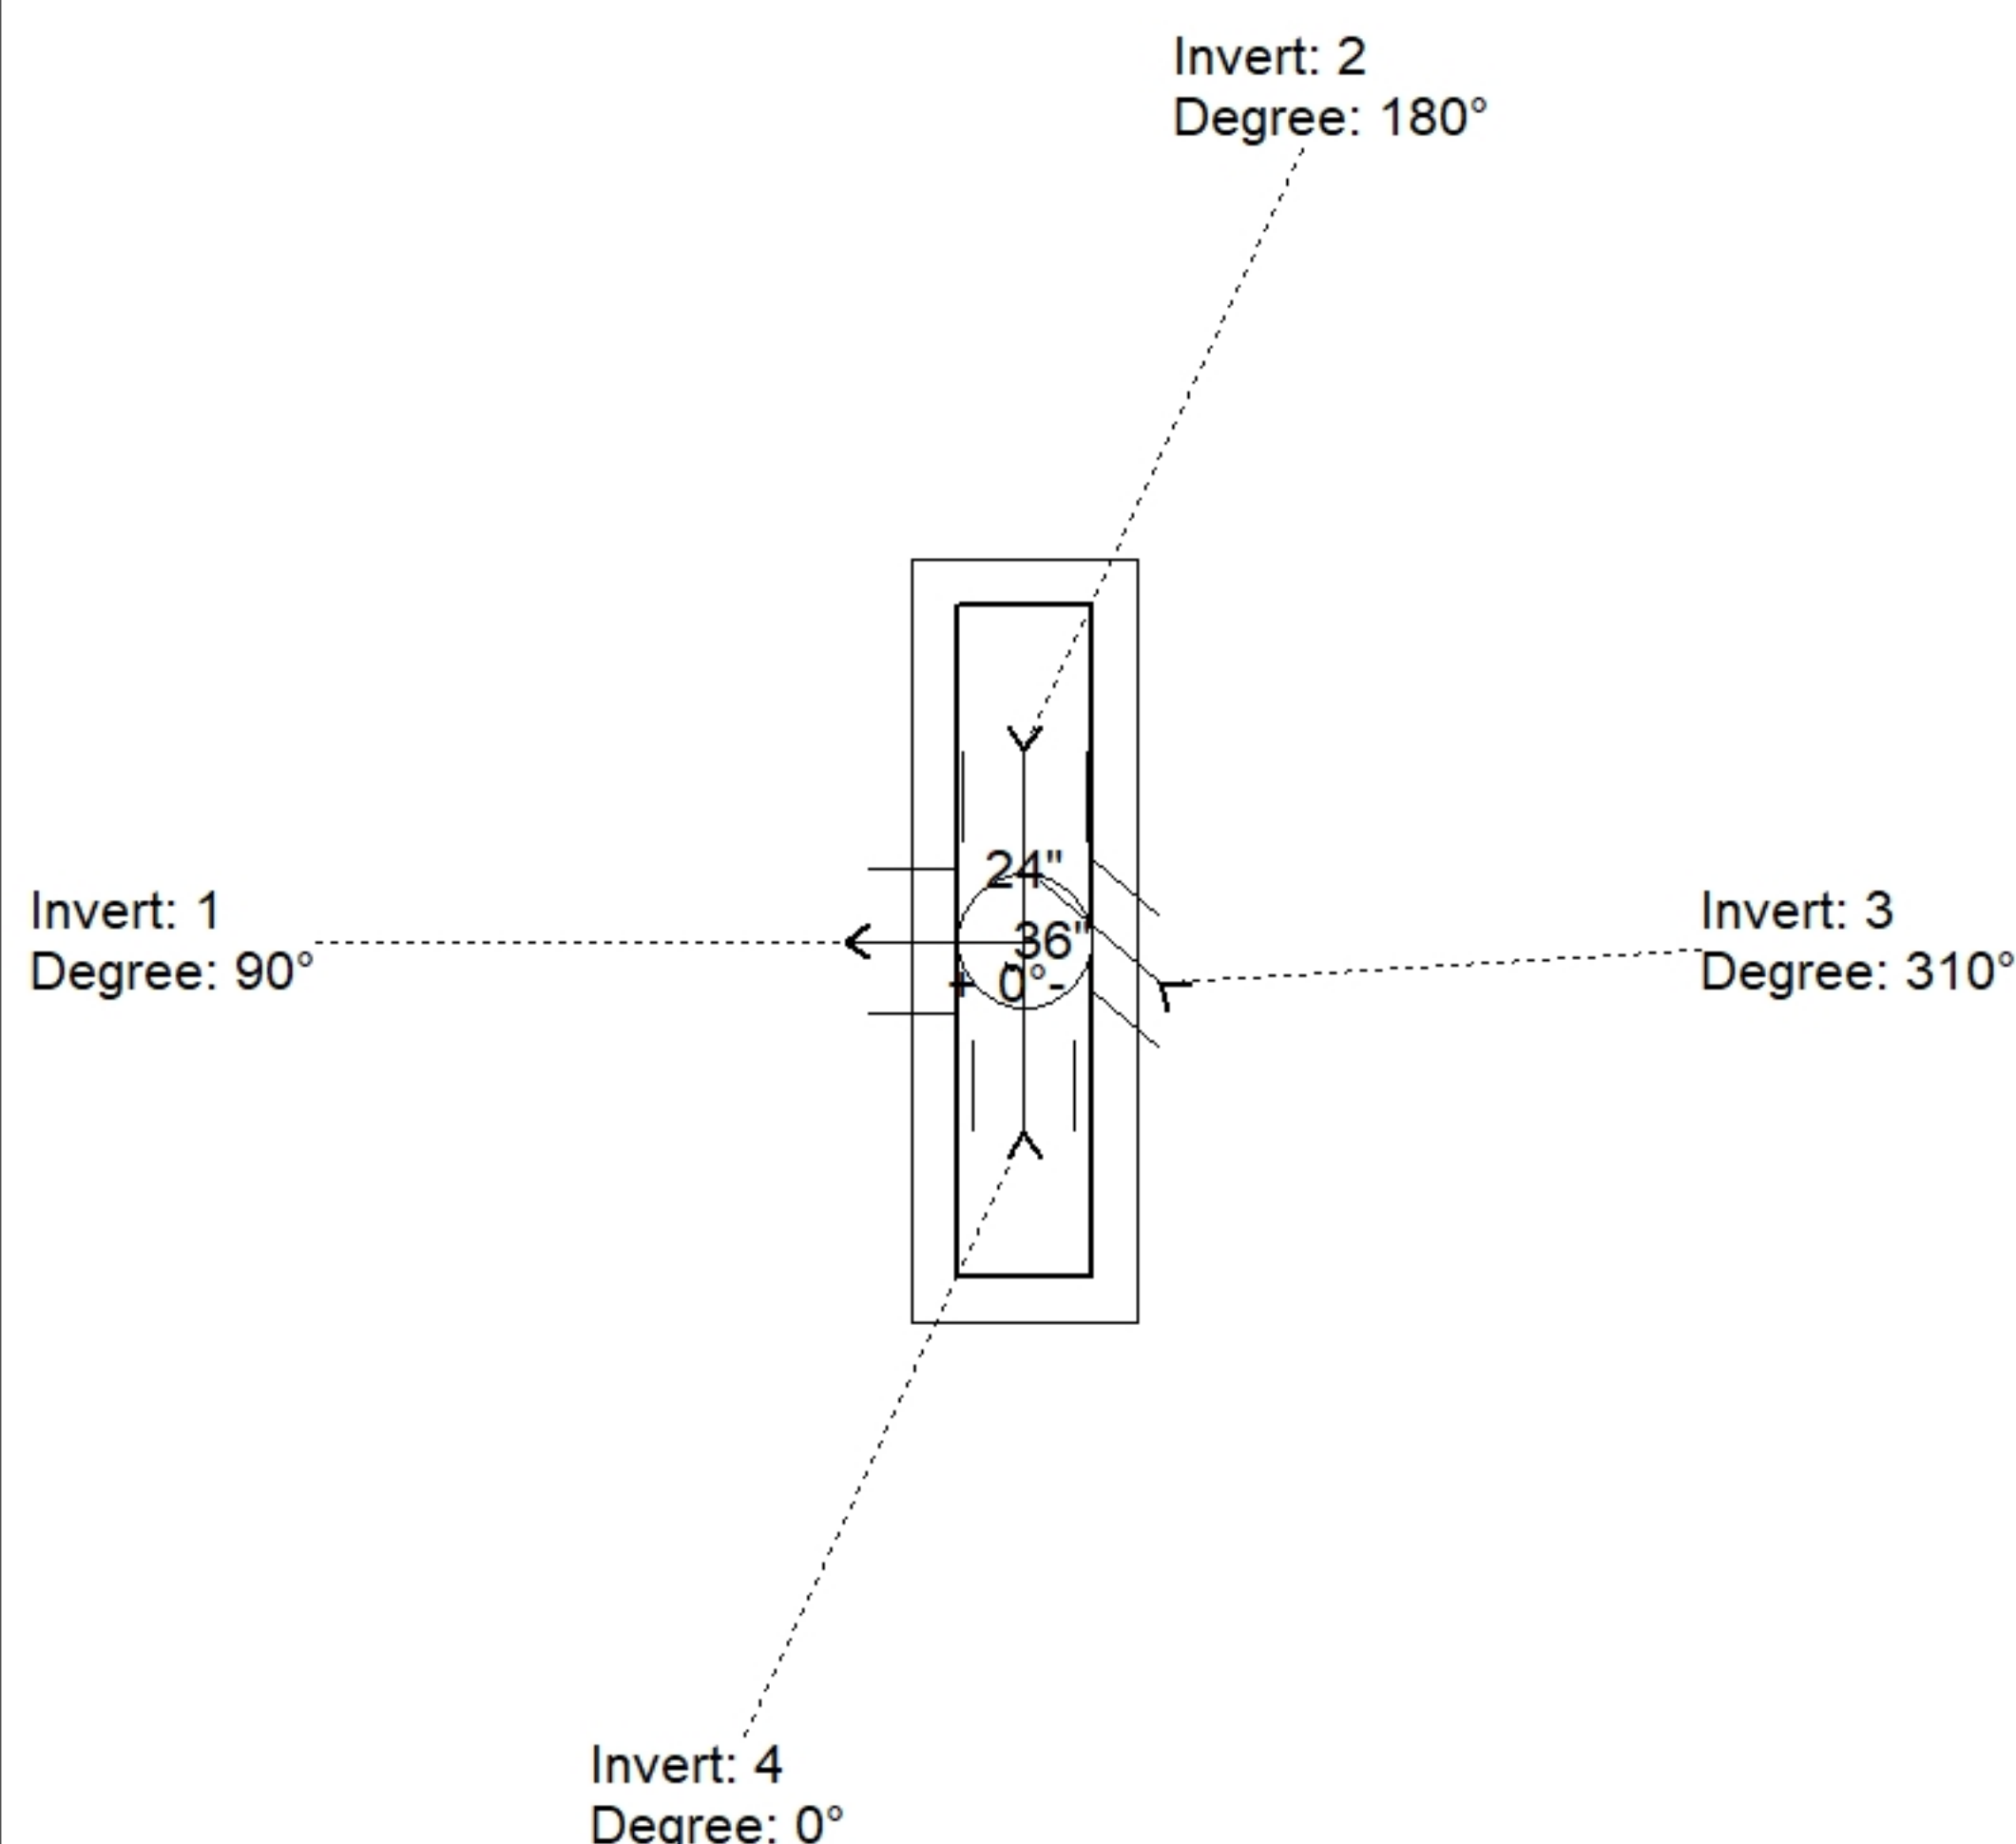

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	590.08'							
Reducer								
Invert 1	583.72'	90°	18" RCP B WALL	23"	26"	Hole 26	-4"	P1
Invert 2	583.72'	180°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 3	583.72'	310°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 4	583.72'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

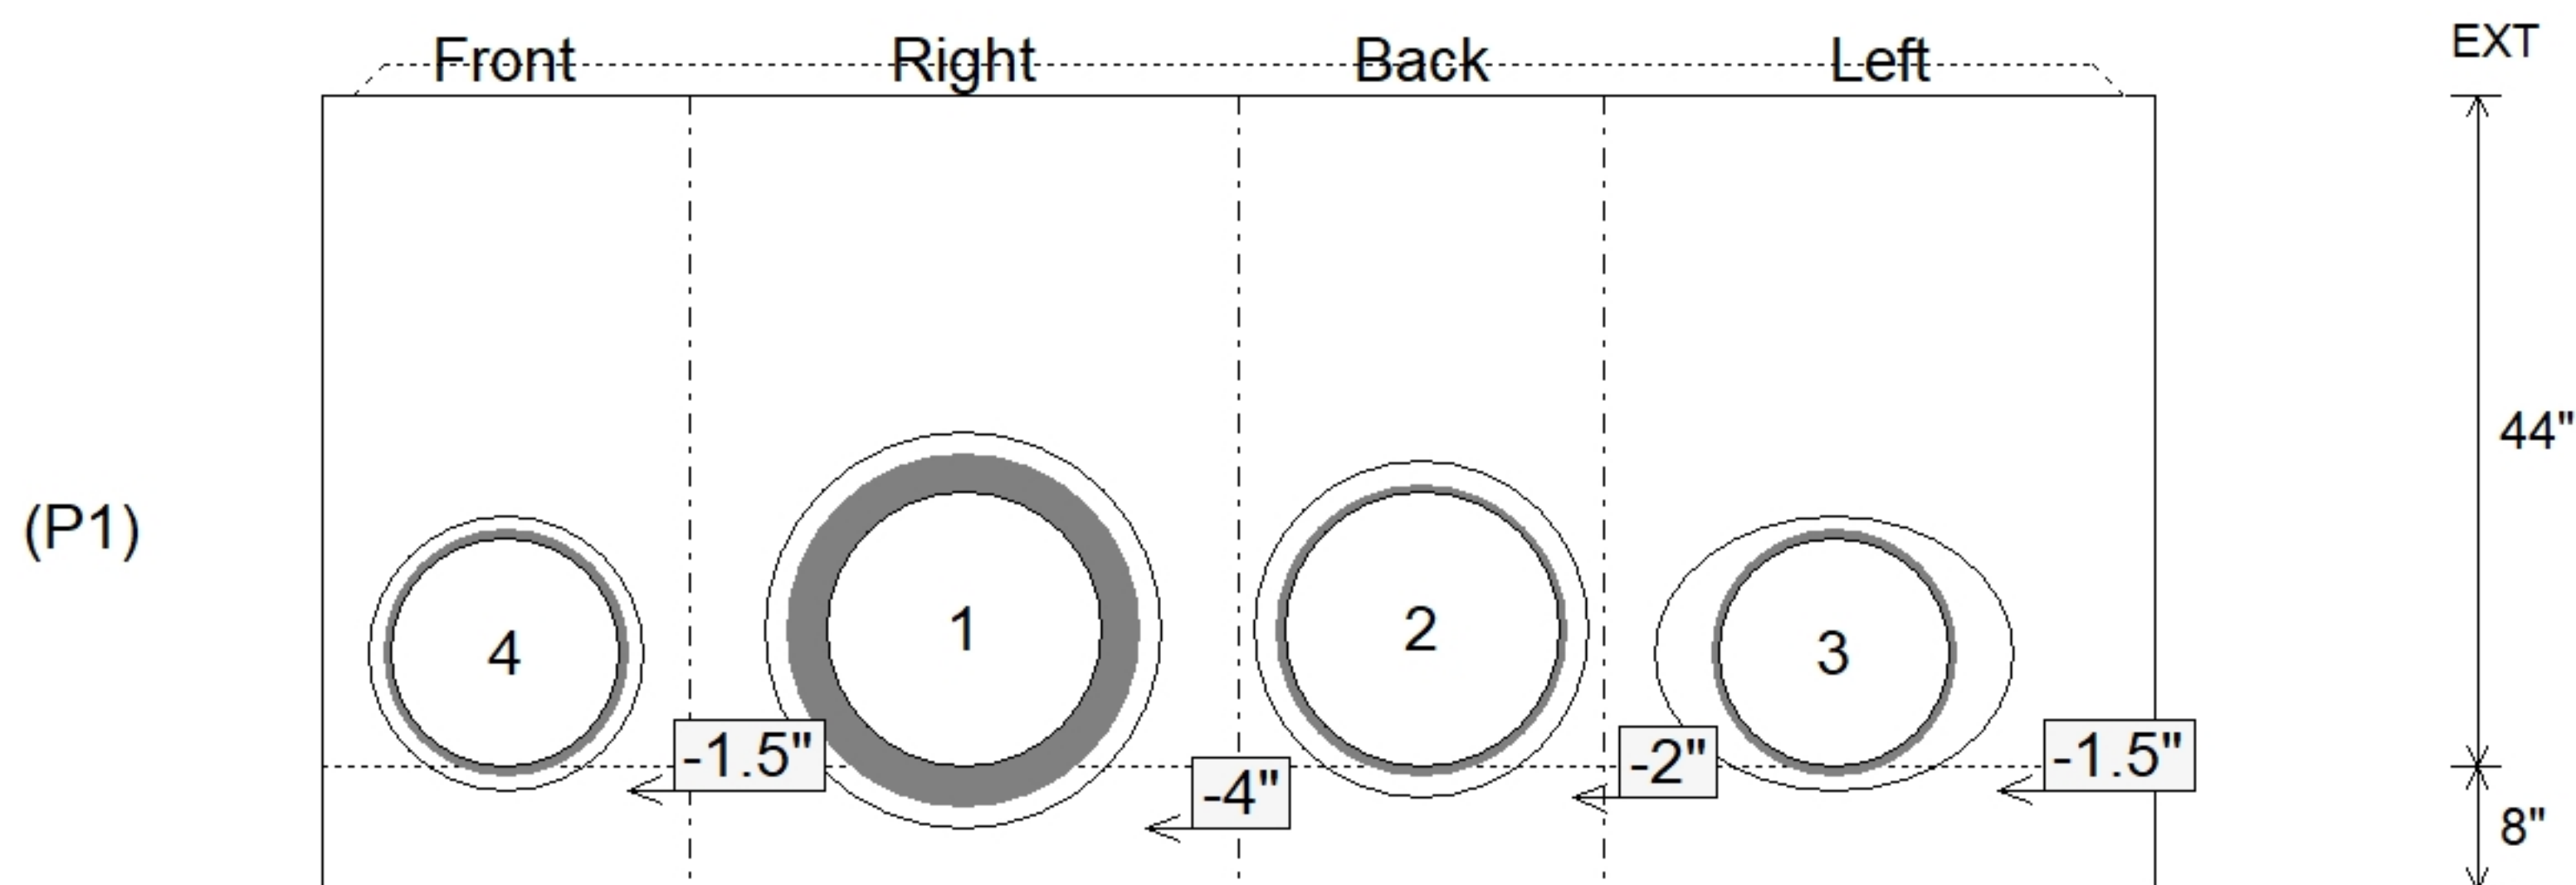

Submittal Drawing
8/18/2026 9:55:14 AM

SUBMITTAL
APPROVED BY:
