

Contractor: Cleary Construction, Inc.

PC: T. Ryan

TECH: J. Coppage

Plant: Beaver Dam, Ky.




Structure ID: 118+97 RT CBIA INLET 15			
Spec: KYTC	Rim: 591.16'	Sump: 0"	Floor (Bot): 585.283'
Type: CBI TYPE A (10')	Invert: 585.95'	Floor (Top): 585.95'	Overall Height: 5.5'
Size: 24" x 36"	Rim to Invert: 5.21'	Floor Height: 8"	Slack: 4.52"


Structure Notes: .
 -KYTC STATE PROJECT 251007
 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
 -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
 -KYTC CERTIFICATIONS REQUIRED.

STRUCTURE SUMMARY:	
P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10"	3398 lb
P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18"	5270 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF - 30"	4202 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 22	0 lb


Structure Total:	12870 lb

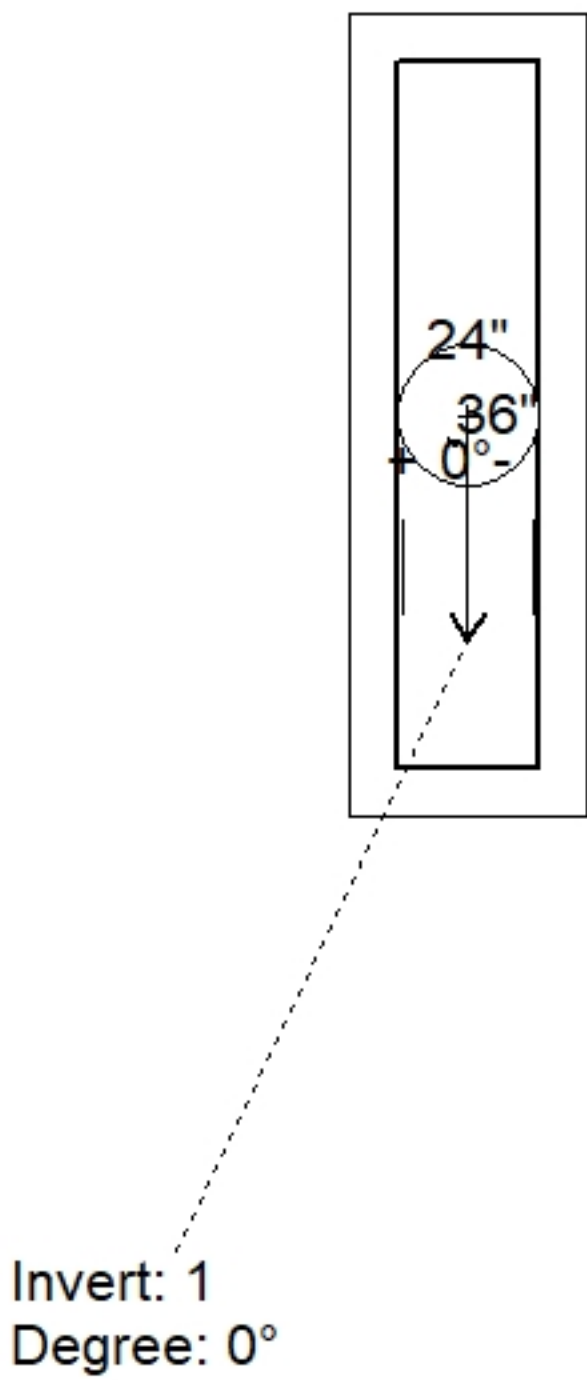

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	591.16'							
Reducer								
Invert 1	585.95'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

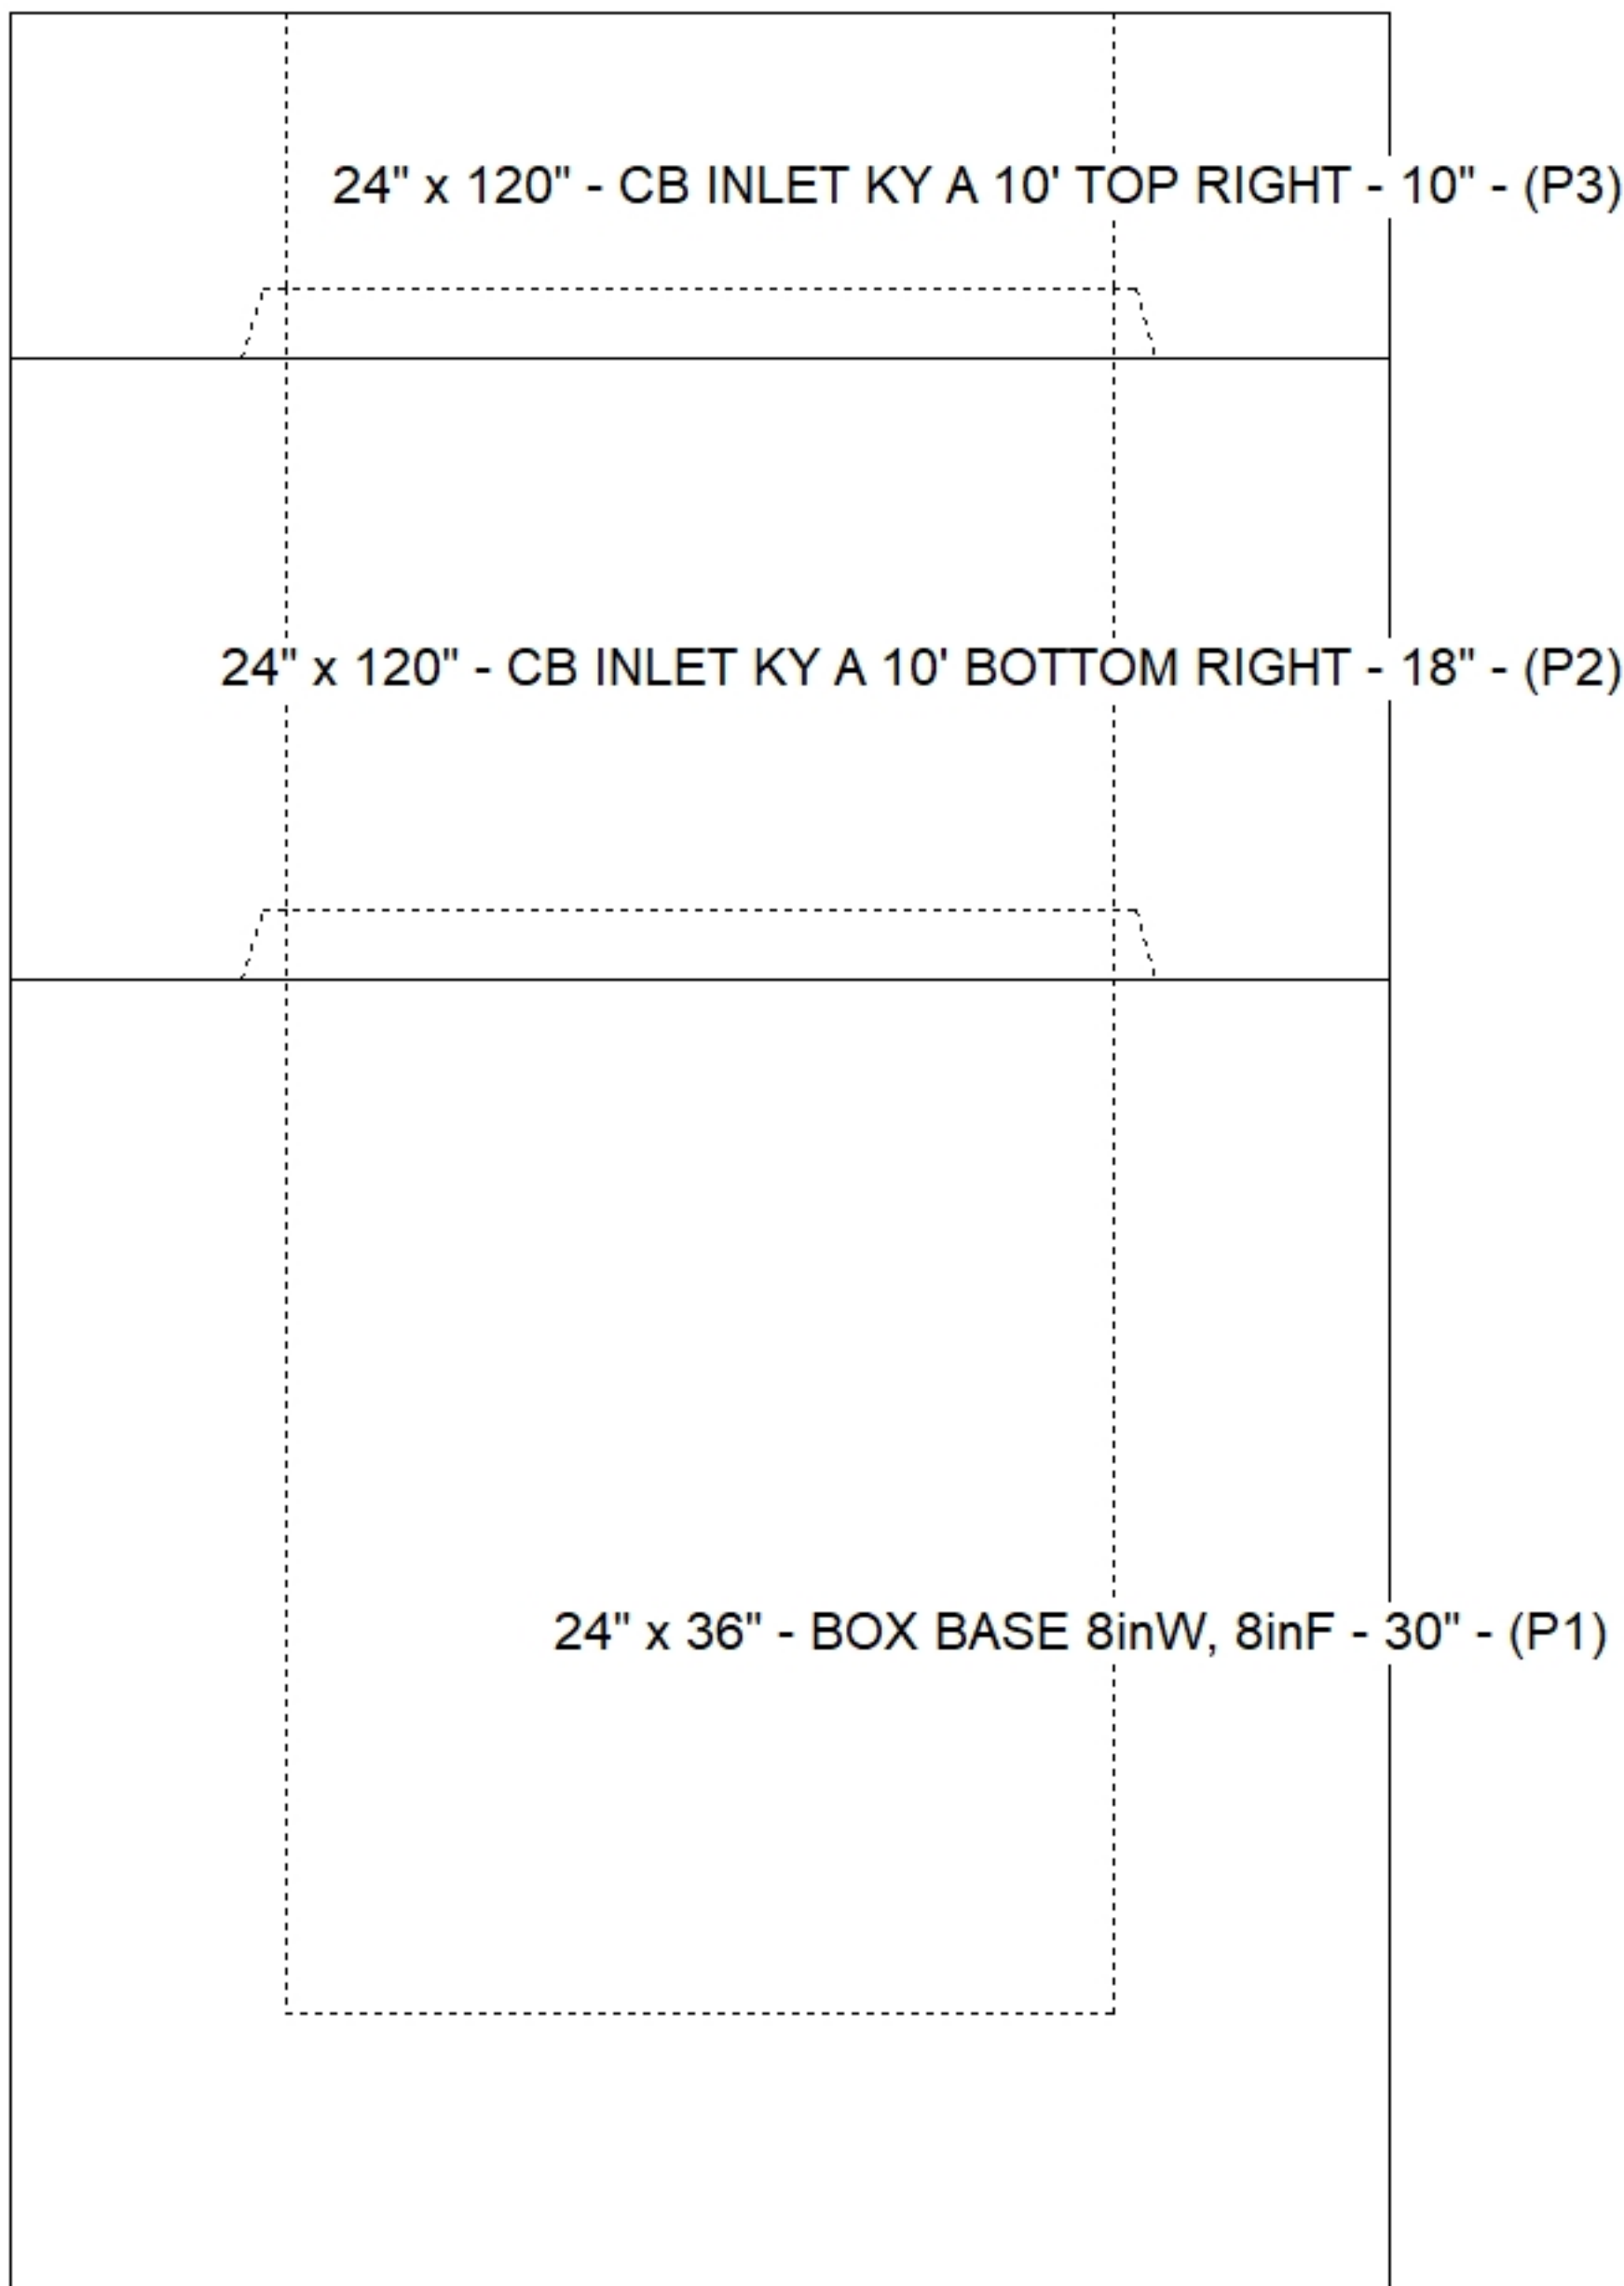

Default - Interior Dimensions

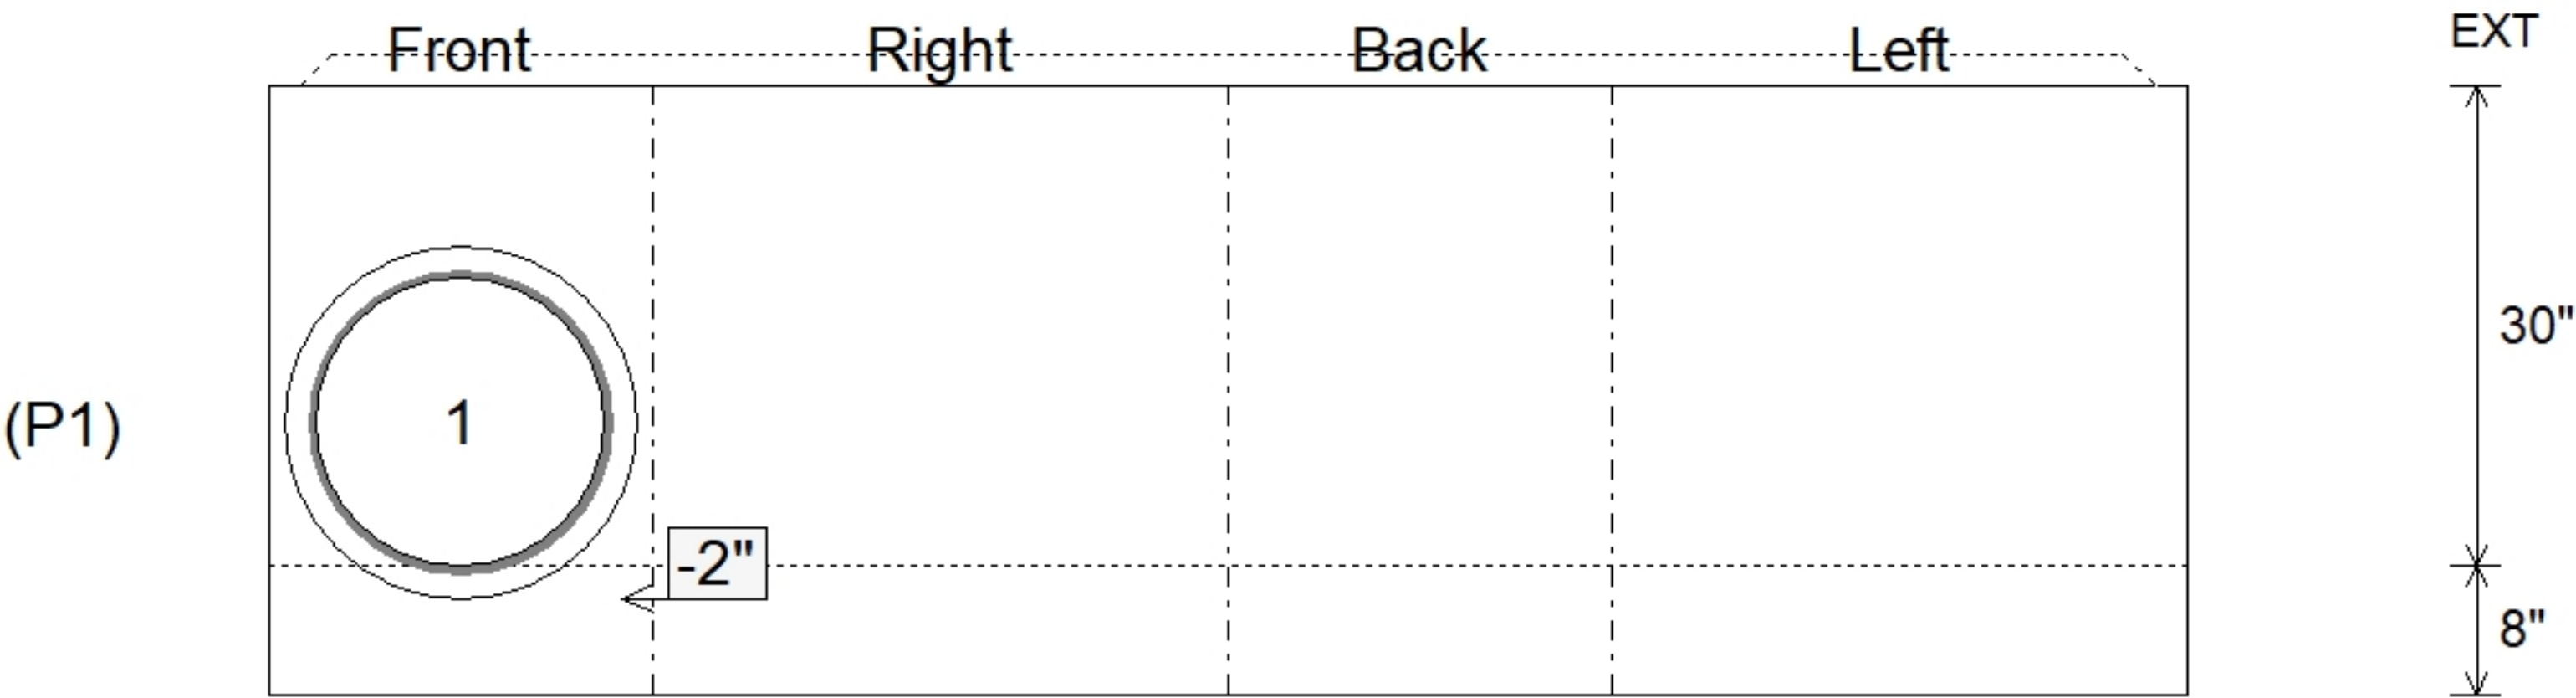

Submittal Drawing
8/18/2026 9:55:15 AM

SUBMITTAL
APPROVED BY:
