



Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, Ky. 8/17/2026 10:44:09 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 123+90 RT CBIA INLET 29											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht							
P3) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 36" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22 1) Hole - 18					3400 lb 5270 lb 4604 lb 0 lb 0 lb 0 lb Structure Total: 13274 lb		Structure Notes: -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.				
Rim: 593.13' Rim to Invert: 5.68' Slack: 4.16" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	587.45'	60°	23.691"	18" CMP	19"	Hole 22	22"	25.403"	-2"	8"	
Invert 2	587.45'	180°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

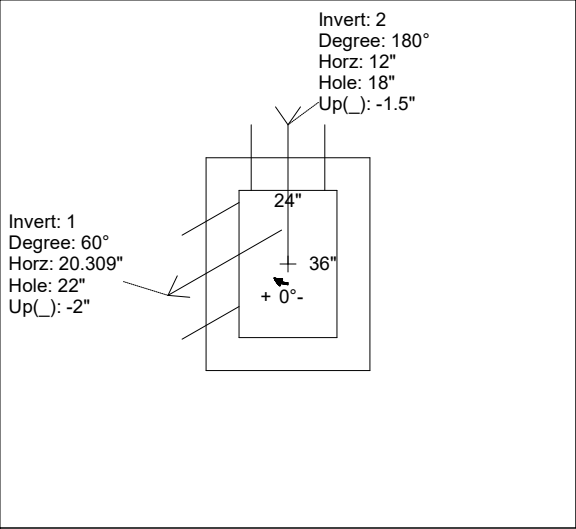

UPSIDE-DOWN VIEW (int. dimensions)

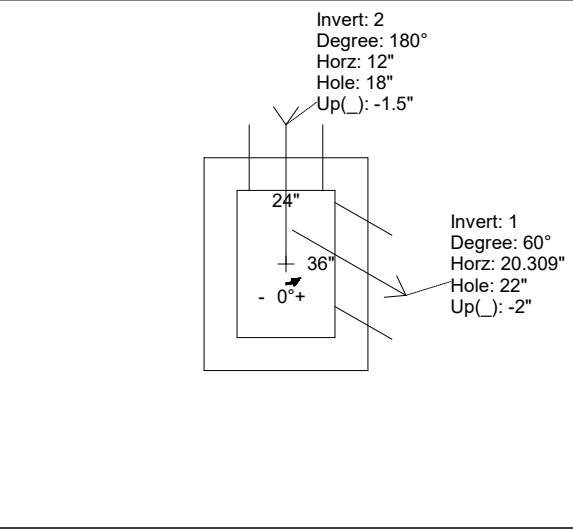

INSIDE WALL DIMENSIONS

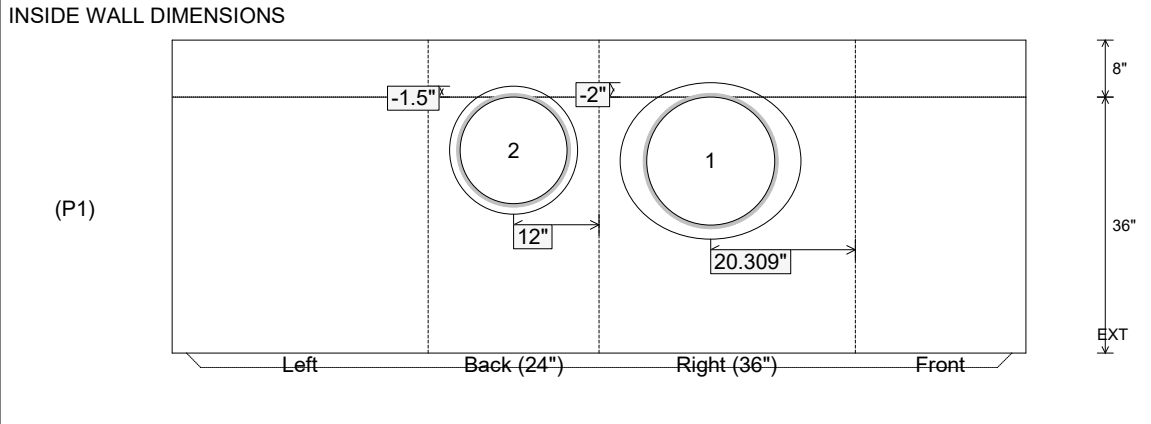

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 36" Height (Ext): 44"	Weight (Net): 4604 lb Volume (Net): 1.18cu.yd
----------------------------------	---------------------------------	--	--	--
