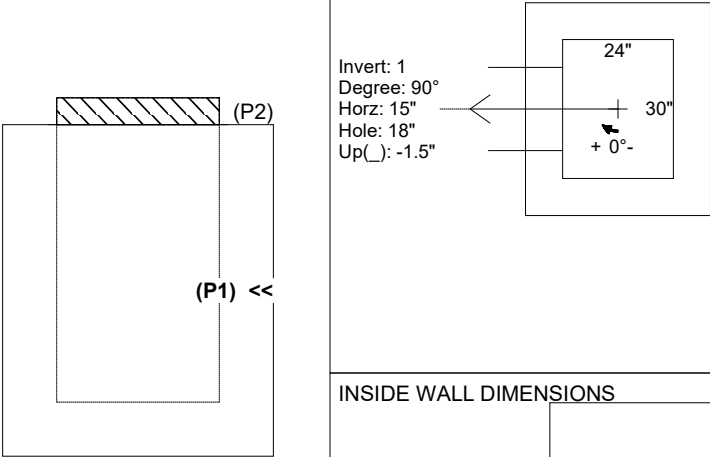

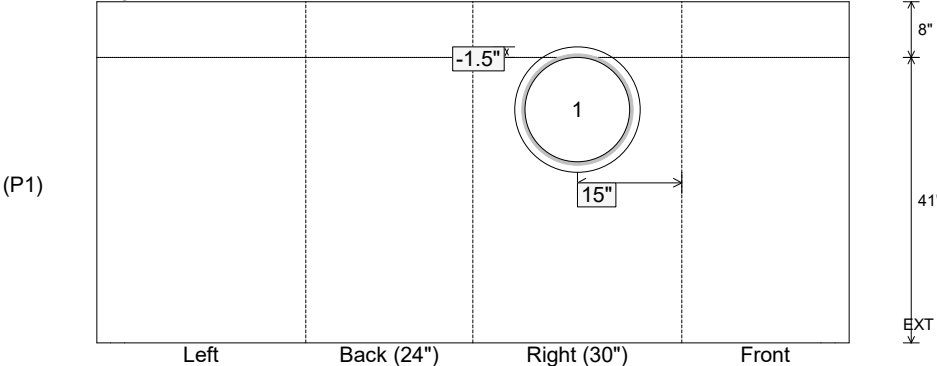


Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, Ky. 8/17/2026 10:43:45 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 125+10 RT DBI-11 INLET 30											
P1		BX24300808VF		BOX BASE 8inW, 8inF, Variable Ht							
P2) 24" x 30" - CASTING HEIGHT - 4" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 41" 1) 24" x 30" - Conseal CS-102 1.00" 1) Hole - 18"					0 lb 4918 lb 0 lb 0 lb ----- 4918 lb Structure Total:		Structure Notes: -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -FRAME & GRATE BY OTHERS. -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.				
Rim: 589.75'		Rim to Invert: 3.75'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	586'	90°	23"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions) 											
INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 41" Height (Ext): 49"		Weight (Net): 4918 lb Volume (Net): 1.26cu.yd	
