

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, Ky.	



Spec: KYTC
Type: DBI TYPE 11
Size: 24" x 30"

Rim: 589.75'
Invert: 586'
Rim to Invert: 3.75'

Sump: 0"
Floor (Top): 586'
Floor Height: 8"


Floor (Bot): 585.333'
Overall Height: 4.417'
Slack: 0"

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- FRAME & GRATE BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.


P2) 24" x 30" - CASTING HEIGHT - 4"
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 41"
1) 24" x 30" - Conseal CS-102 1.00"
1) Hole - 18

0 lb
4918 lb
0 lb
0 lb


Structure Total: 4918 lb

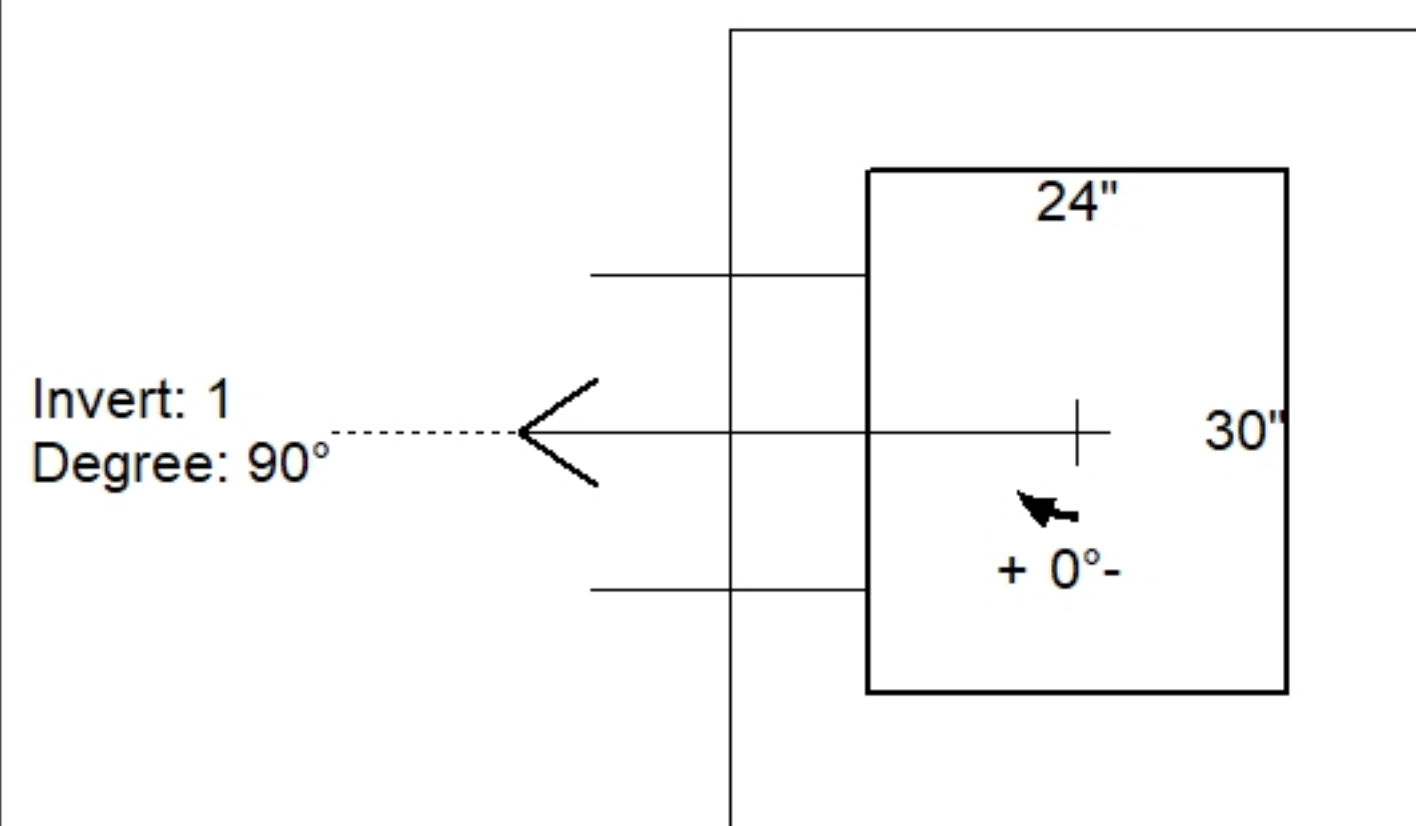

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	589.75'							
Reducer								
Invert 1	586'	90°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

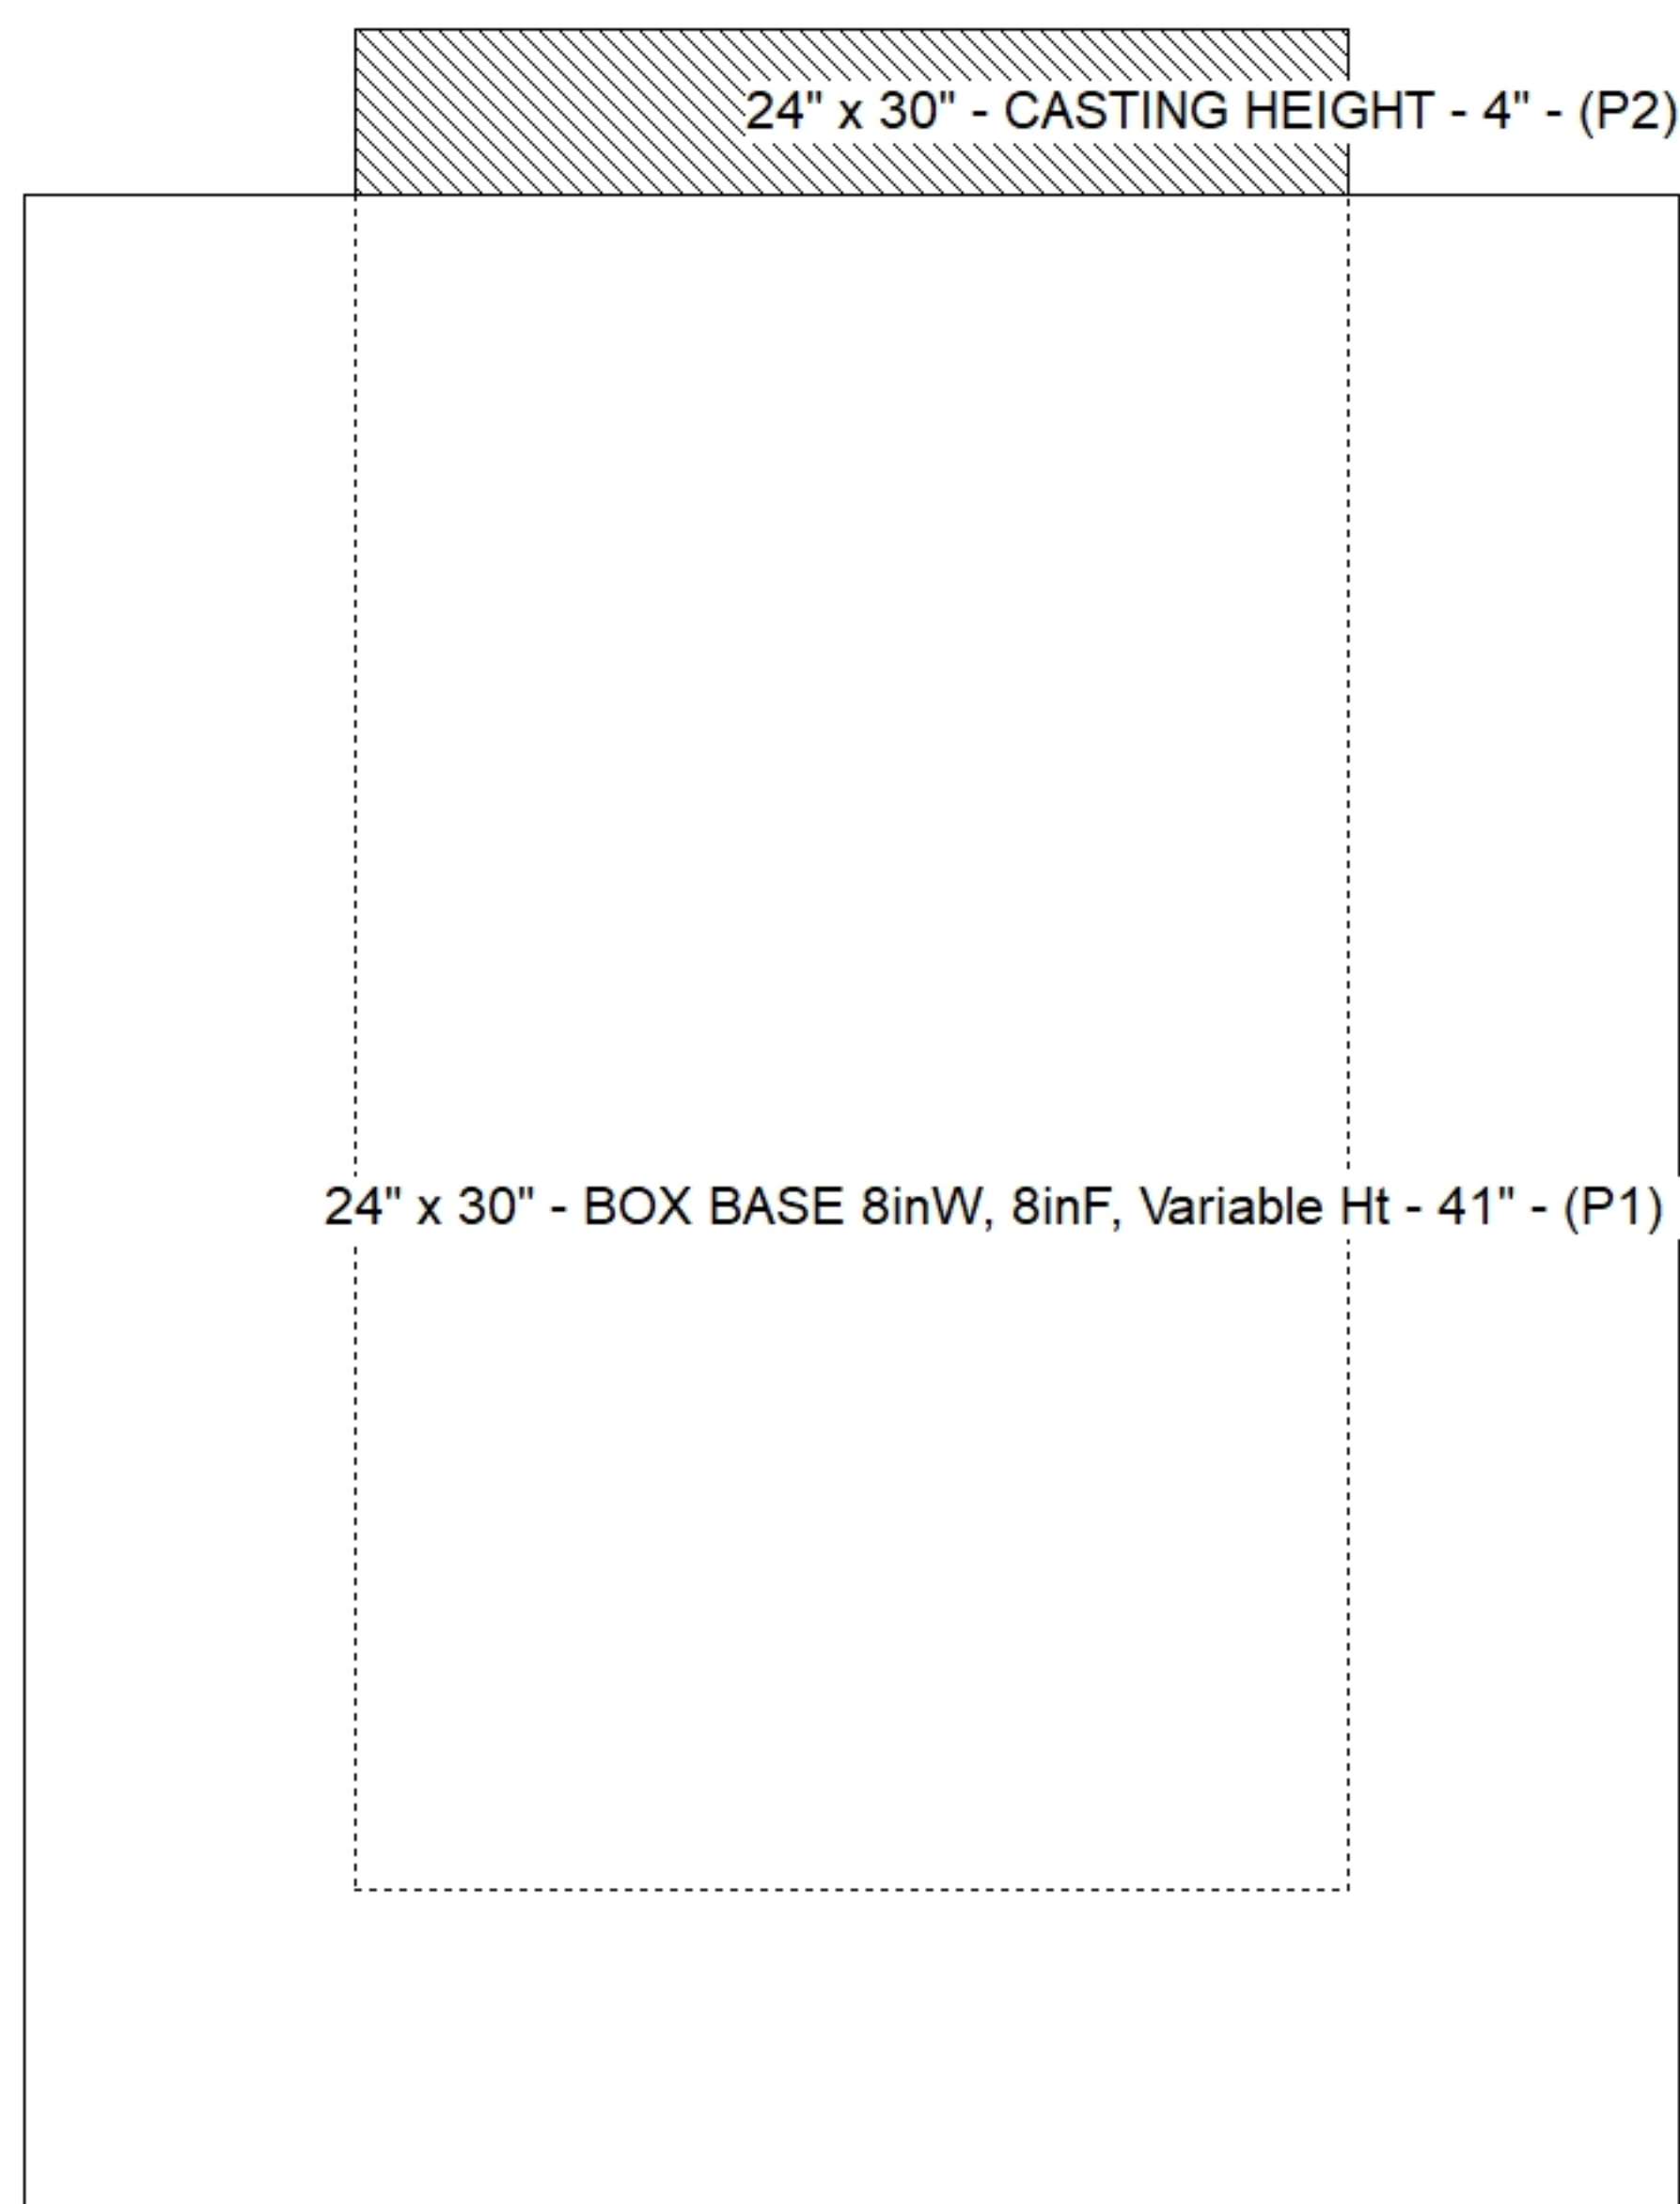

Default - Interior Dimensions

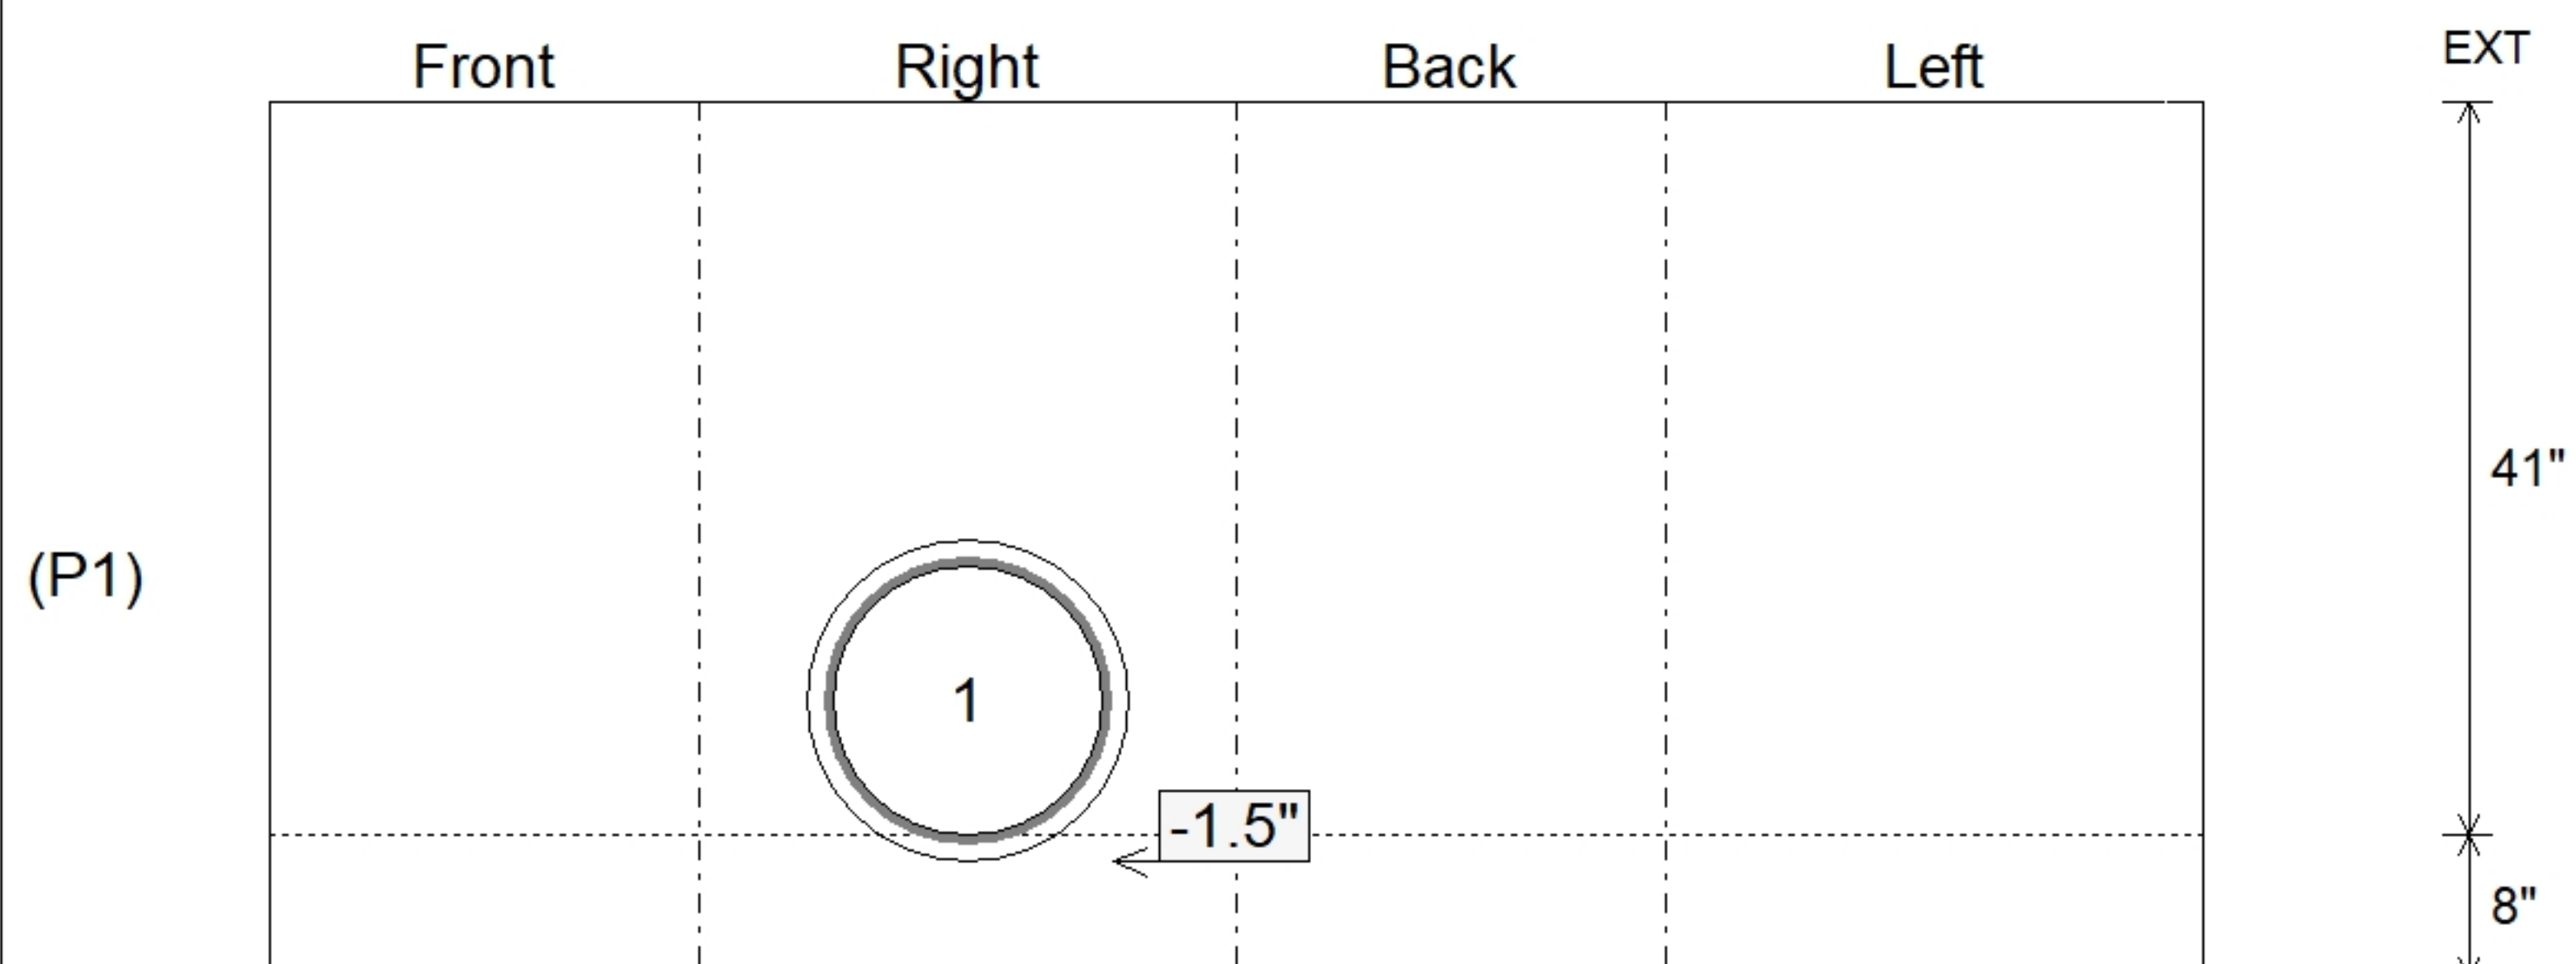

Submittal Drawing
8/18/2026 9:55:15 AM

SUBMITTAL
APPROVED BY:
