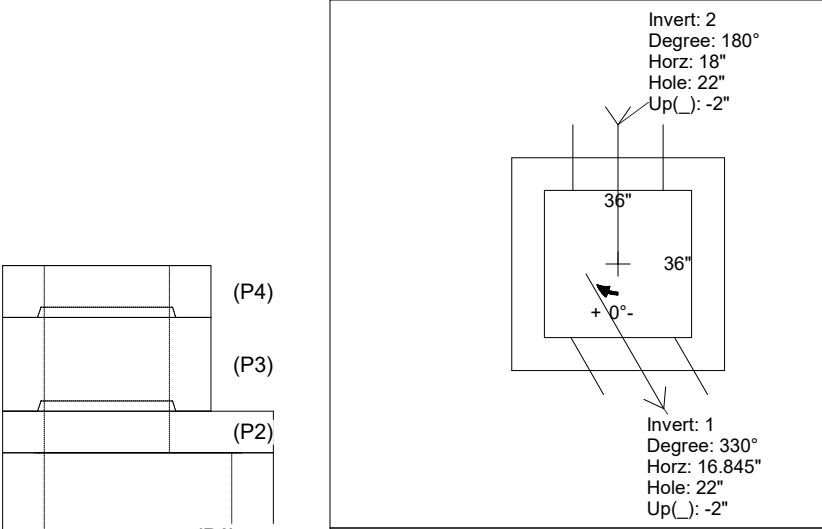
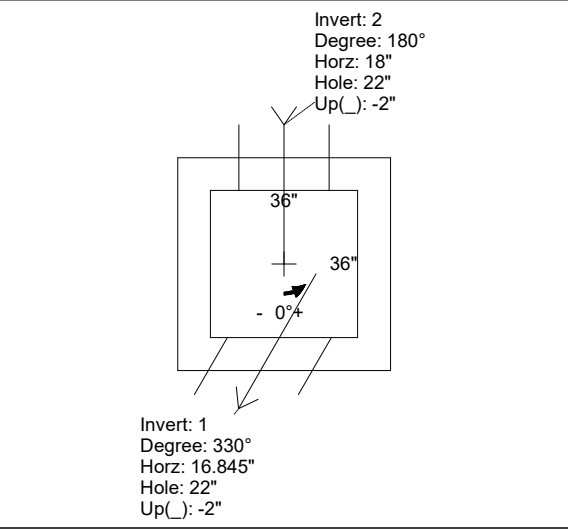



Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, Ky. 8/17/2026 10:43:47 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 126+35 RT CBIA INLET 32											
P1		BX3636-08BA24		BOX BASE 8inW, 8inF							
P4) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18" P2) 36" x 36" - CB TRANSITION SLAB 24"X36" HOLE - 8" P1) 36" x 36" - BOX BASE 8inW, 8inF - 24" 1) 36" x 36" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 22"						3400 lb 5270 lb 1235 lb 4101 lb 0 lb 0 lb 0 lb ----- Structure Total: 14006 lb		Structure Notes: . -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.			
Rim: 591.66' Rim to Invert: 5.36' Slack: 4.32" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	586.3'	330°	20.227"	18" CMP	19"	Hole 22	22"	25.403"	-2"	8"	
Invert 2	586.3'	180°	26"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions)   INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 24" Height (Ext): 32"		Weight (Net): 4101 lb Volume (Net): 1.05cu.yd		
