

Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.
8/17/2026 10:44:54 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 126+35 RT CBIA INLET 32

P2 BX036036-08TS024036


CB TRANSITION SLAB 24"X36" HOLE

- P4) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10"
P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18"
P2) 36" x 36" - CB TRANSITION SLAB 24"X36" HOLE - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF - 24"
1) 36" x 36" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 22

3400 lb
5270 lb
1235 lb
4101 lb
0 lb
0 lb
0 lb

Structure Total: 14006 lb

Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

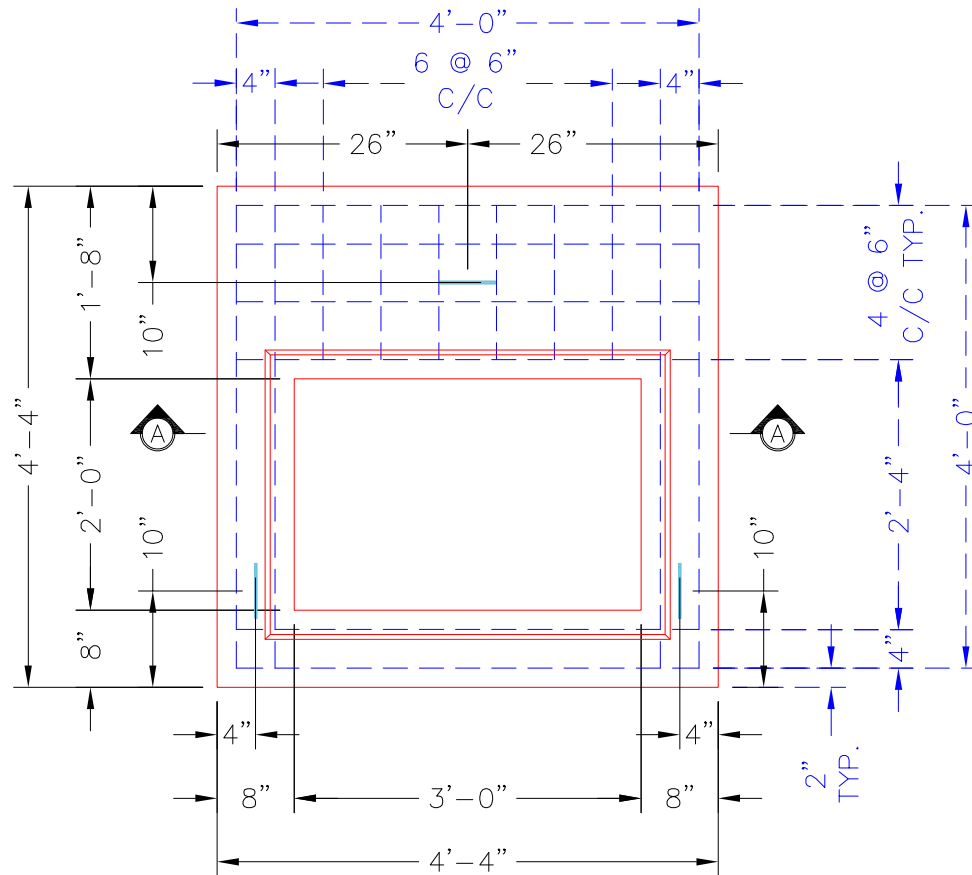


PLAN VIEW

24" X 36" OPENING
OFFSET IN SLAB

3 EA. CONAC .8 TON 8¹/₁₆"
(6MM) WIRE ROPE ANCHORS
REQUIRED—MINIMUM.

#5 BAR @ 4" C/C TYP.
(TOP & BOTTOM)

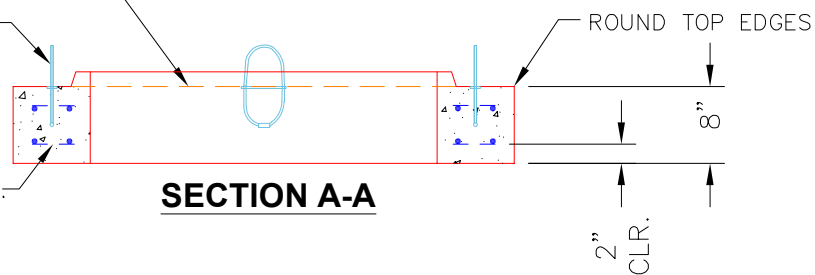

SECTION A-A

NOTES:

- CONCRETE: 4500 PSI @ 28 DAYS.
- REINFORCING: #5 BAR @ 4" & 6" C/C—GRADE 60.
(TOP & BOTTOM LAYERS).
- 3 EA. CONAC WIRE LOOP LIFTERS REQUIRED.

#5 BAR CUT LIST
20 EA. @ 48" LG.
12 EA. @ 16" LG.

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1235 lb
Volume (Net): 0.32cu.yd
