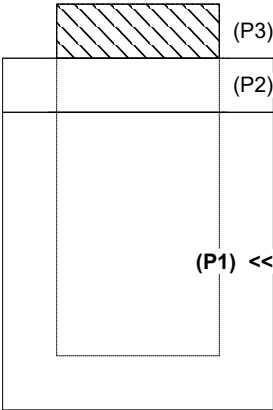
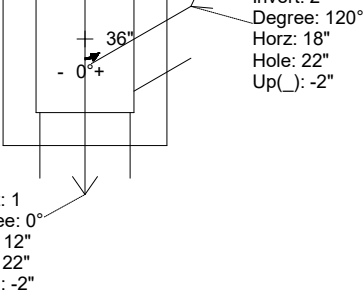
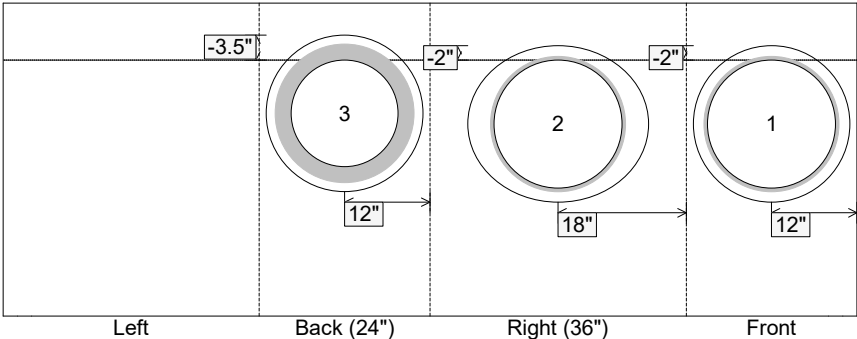


Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, Ky. 8/17/2026 10:43:48 AM		Tech: J. Coppage PC: T. Ryan					
Structure ID: 126+69 RT JB-B2 INLET 32A												
P1		BX2436-08BA36		BOX BASE 8inW, 8inF								
P3) 24" - CASTING HEIGHT - 8" P2) 24" x 36" - BX FLAT LID 8inW w/CC 24" HOLE - 8" P1) 24" x 36" - BOX BASE 8inW, 8inF - 36" 1) 24" x 36" - Conseal CS-102 1.00" 3) Hole - 22					0 lb 1093 lb 4265 lb 0 lb 0 lb ----- 5357 lb Structure Total:		Structure Notes: -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.). -TYPE 2 FRAME & COVER BY OTHERS. -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.					
Rim: 591.1'					Rim to Invert: 4.54'		Slack: 2.48"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	586.56'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"		
Invert 2	586.56'	120°	30.619"	18" CMP	19"	Hole 22	22"	25.403"	-2"	-6"		
Invert 3	586.56'	180°	20"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-3.5"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 												
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 36" Height (Ext): 44"		Weight (Net): 4265 lb Volume (Net): 1.09cu.yd			
