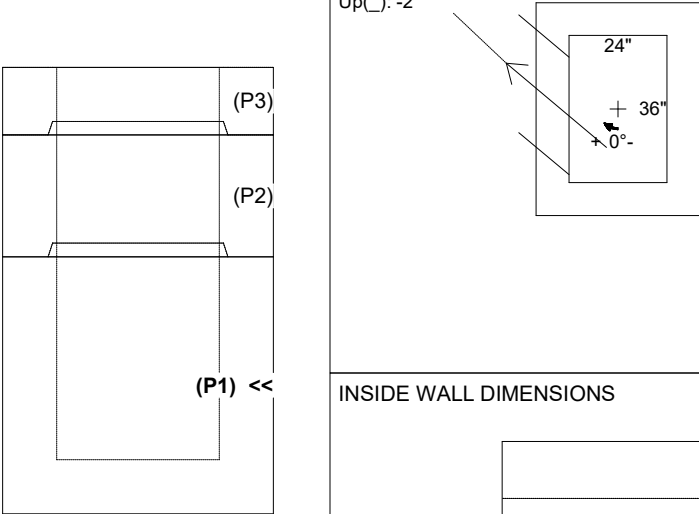

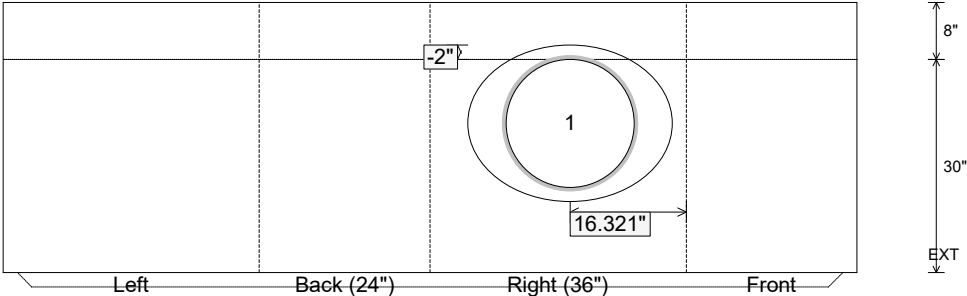


Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, Ky. 8/17/2026 10:43:49 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 126+92 CBIA INLET 33											
P1		BX2436-08BA30		BOX BASE 8inW, 8inF							
P3) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF - 30" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 22"					3400 lb 5270 lb 4124 lb 0 lb 0 lb ----- Structure Total: 12794 lb		Structure Notes: . -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.				
Rim: 592.31' Rim to Invert: 5.11' Slack: 3.32" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	587.2'	130°	31.033"	18" CMP	19"	Hole 22	22"	28.719"	-2"	-9"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) Invert: 1 Degree: 130° Horz: 16.321" Hole: 22" Up(): -2"  UPSIDE-DOWN VIEW (int. dimensions) Invert: 1 Degree: 130° Horz: 16.321" Hole: 22" Up(): -2"  INSIDE WALL DIMENSIONS (P1) 											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 30" Height (Ext): 38"		Weight (Net): 4124 lb Volume (Net): 1.05cu.yd		
