

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, Ky.	



Spec: KYTC
Type: CBI TYPE A (10')
Size: 24" x 36"


Rim: 592.31'	Sump: 0"
Invert: 587.2'	Floor (Top): 587.2'
Rim to Invert: 5.11'	Floor Height: 8"

Floor (Bot): 586.533'
Overall Height: 5.5'
Slack: 3.32"

-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

P3) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10"	3400 lb
P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18"	5270 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF - 30"	4124 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 22	0 lb
Structure Total:	12794 lb


Invert: 1
Degree: 130°

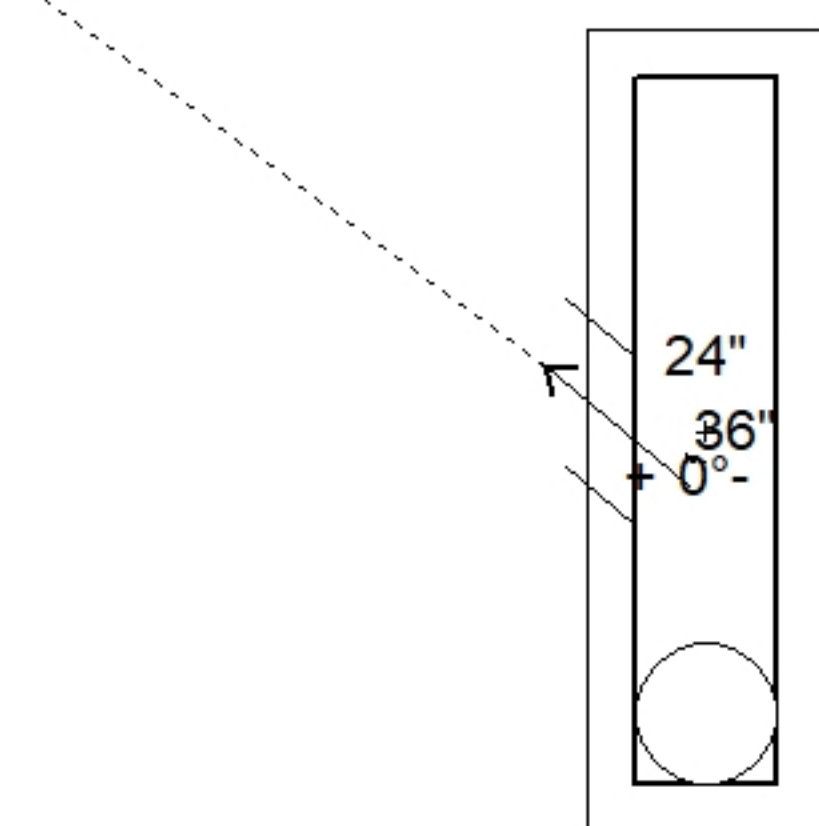

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	592.31'							
Reducer								
Invert 1	587.2'	130°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - BOX BASE 8inW, 8inF - 30" - (P1)

Default - Interior Dimensions

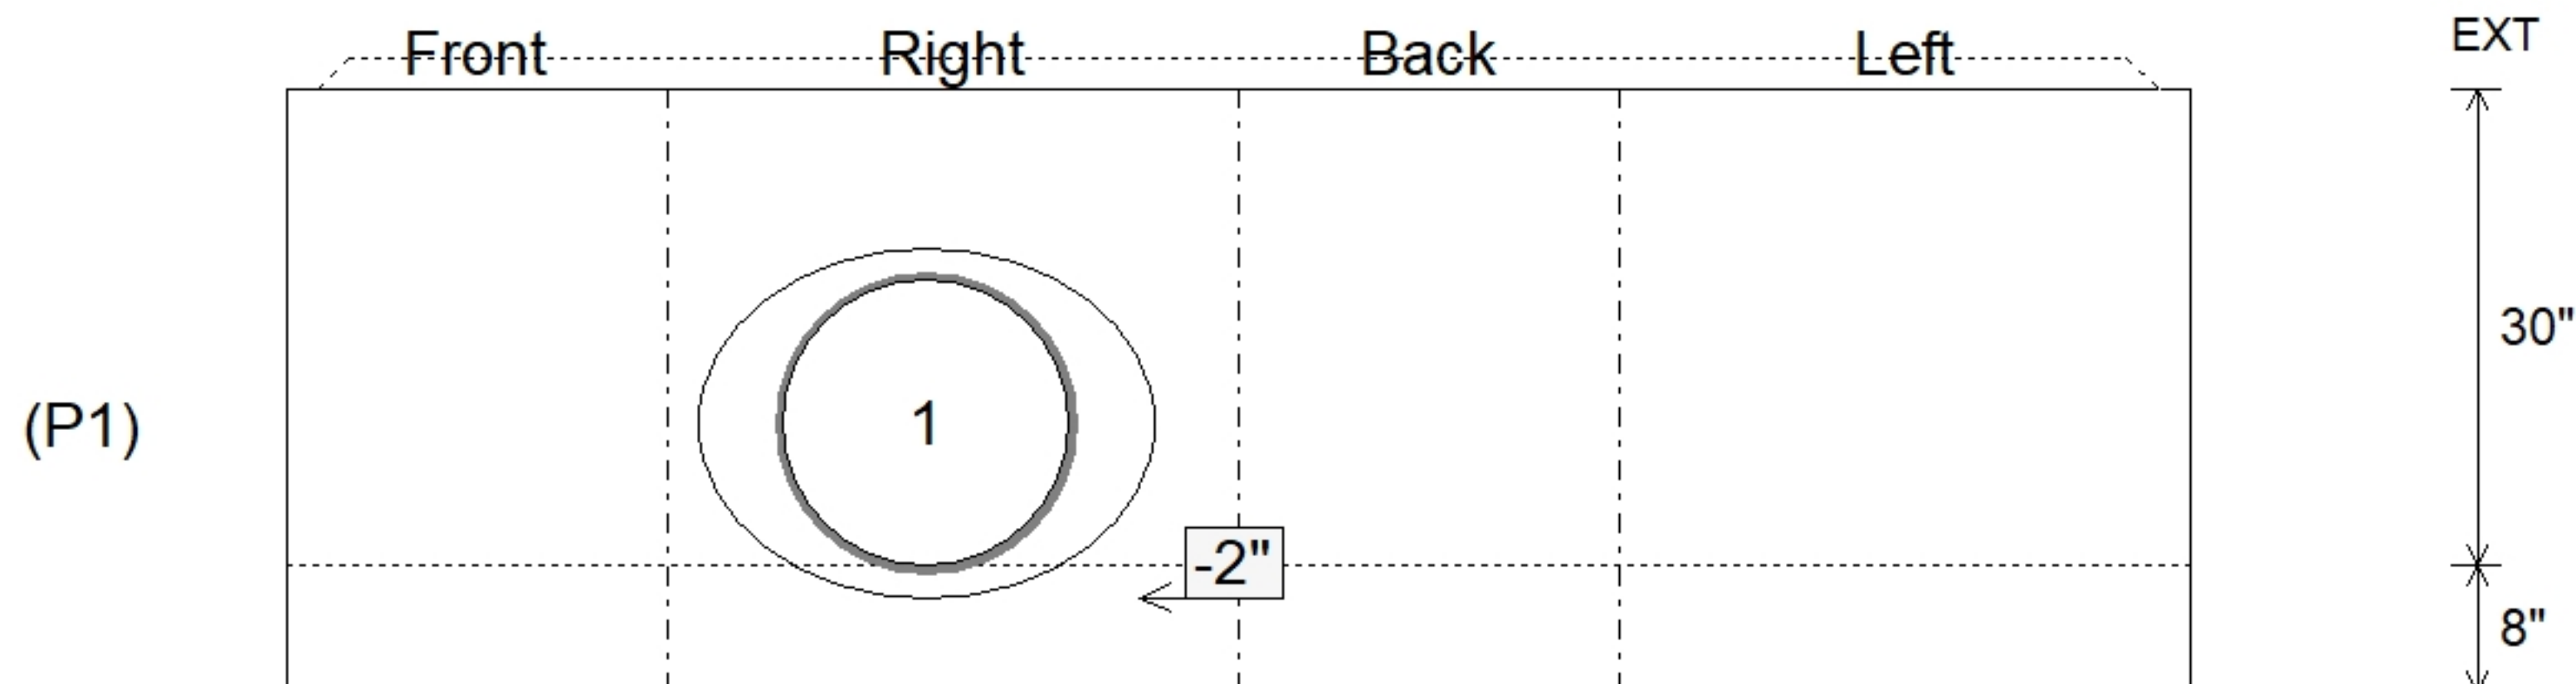

Submittal Drawing
8/18/2026 9:55:17 AM

SUBMITTAL
APPROVED BY:
