



Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, Ky. 8/17/2026 10:43:52 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 127+07 RT DBI-13G INLET 80											
P1 BX24300808VF BOX BASE 8inW, 8inF, Variable Ht											
P3) 15" x 27" - P.I.P. - BY OTHERS - 3" P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE - 8" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 20" 1) 24" x 30" - Conseal CS-102 1.00" 1) Hole - 18 2) Hole - 4					0 lb 963 lb 2919 lb 0 lb 0 lb 0 lb ----- Structure Total: 3882 lb		Structure Notes: . -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -DBI 13G FRAME & GRATE BY OTHERS. -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -#5 BAR STUBBED OUT OF TOP OF TRANSITION SLAB 6" AT 12" C/C FOR FIELD POURED CURB & GUTTER. -KYTC CERTIFICATIONS REQUIRED.				
Rim: 590.75' Rim to Invert: 3' Slack: 5" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	587.75'	125°	29.68"	15" CMP	16"	Hole 18	18"	21.974"	-1.5"	-6"	
Invert 2	588.76'	90°	10"	4" WEEP HOLE	4"	Hole 4	4"	4"	12.12"	-13"	
Invert 3	588.76'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	12.12"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

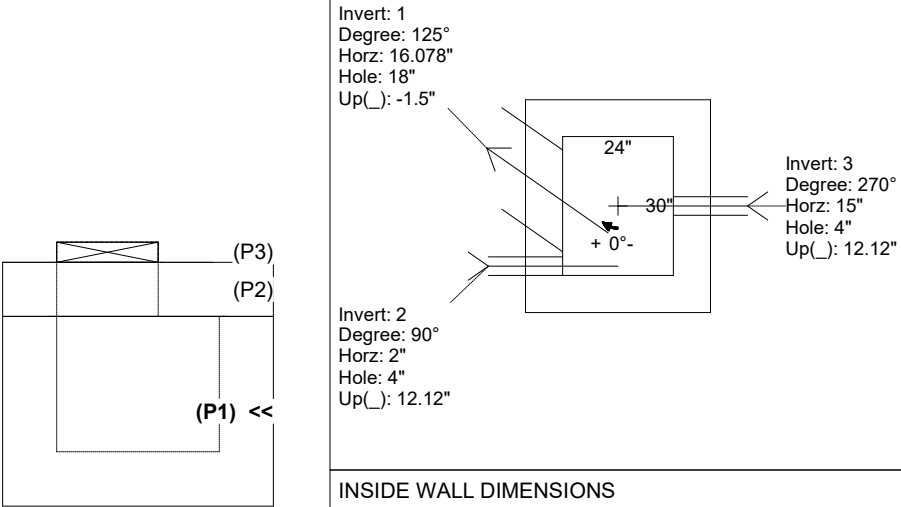

UPSIDE-DOWN VIEW (int. dimensions)

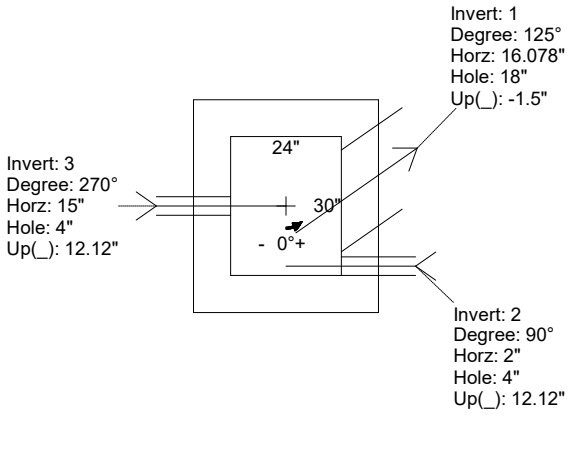

INSIDE WALL DIMENSIONS

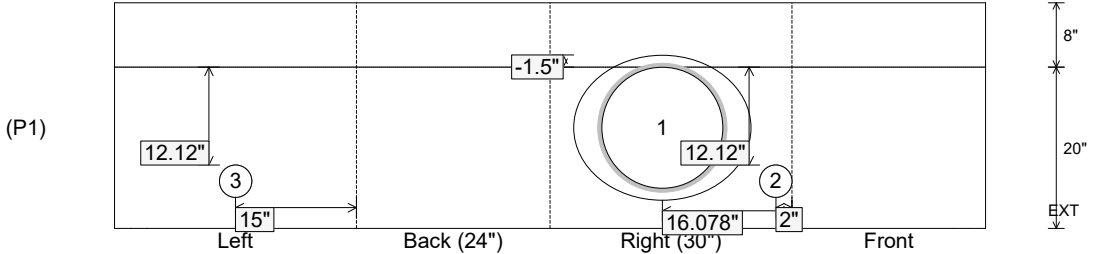

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 20" Height (Ext): 28"	Weight (Net): 2919 lb Volume (Net): 0.75cu.yd
----------------------------------	-------------------------------	--	--	--
