




Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, Ky. 8/17/2026 10:43:50 AM		Tech: J. Coppage PC: T. Ryan					
Structure ID: 127+07 RT JB-B2 INLET 34												
P1		BX2424-08BAVF		BOX BASE 8inW, 8inF, Variable Ht								
P3) 24" - CASTING HEIGHT - 8" P2) 24" x 24" - BX FLAT LID 8inW w/CC 24" HOLE - 8" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht - 28" 1) 24" x 24" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 1) Hole - 22 2) Hole - 18					0 lb 770 lb 2883 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 3654 lb		Structure Notes: -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.). -TYPE 2 FRAME & COVER BY OTHERS. -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.					
Rim: 590.92'					Rim to Invert: 3.81'		Slack: 1.72"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	587.11'	0°	20"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-3.5"	0"		
Invert 2	587.11'	180°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"		
Invert 3	587.11'	270°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

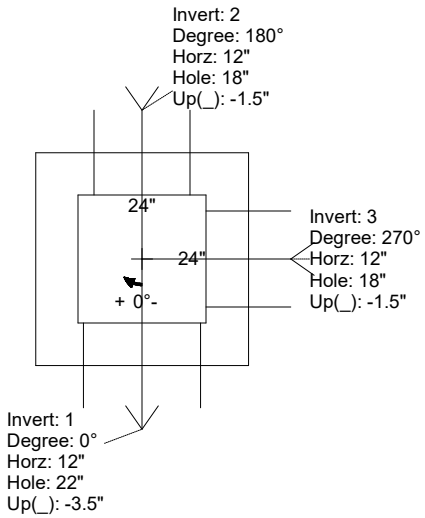

RIGHT-SIDE UP VIEW (int. dimensions)

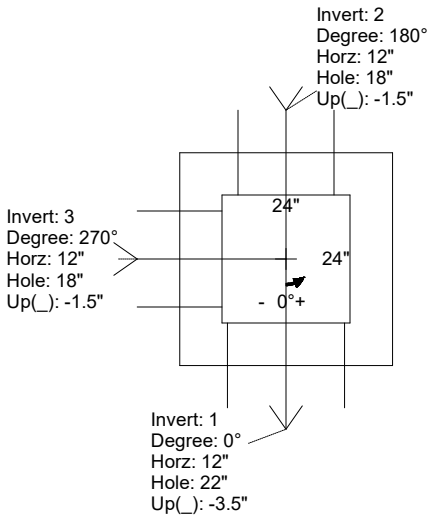

UPSIDE-DOWN VIEW (int. dimensions)

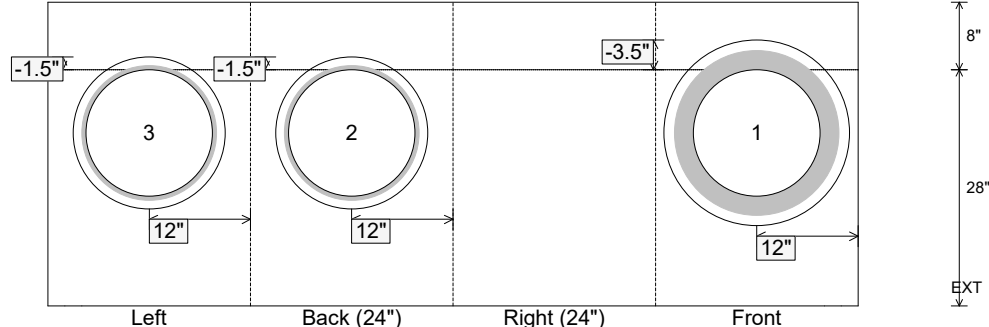

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 28" Height (Ext): 36"	Weight (Net): 2883 lb Volume (Net): 0.74cu.yd
----------------------------------	-------------------------------	--	--	--
