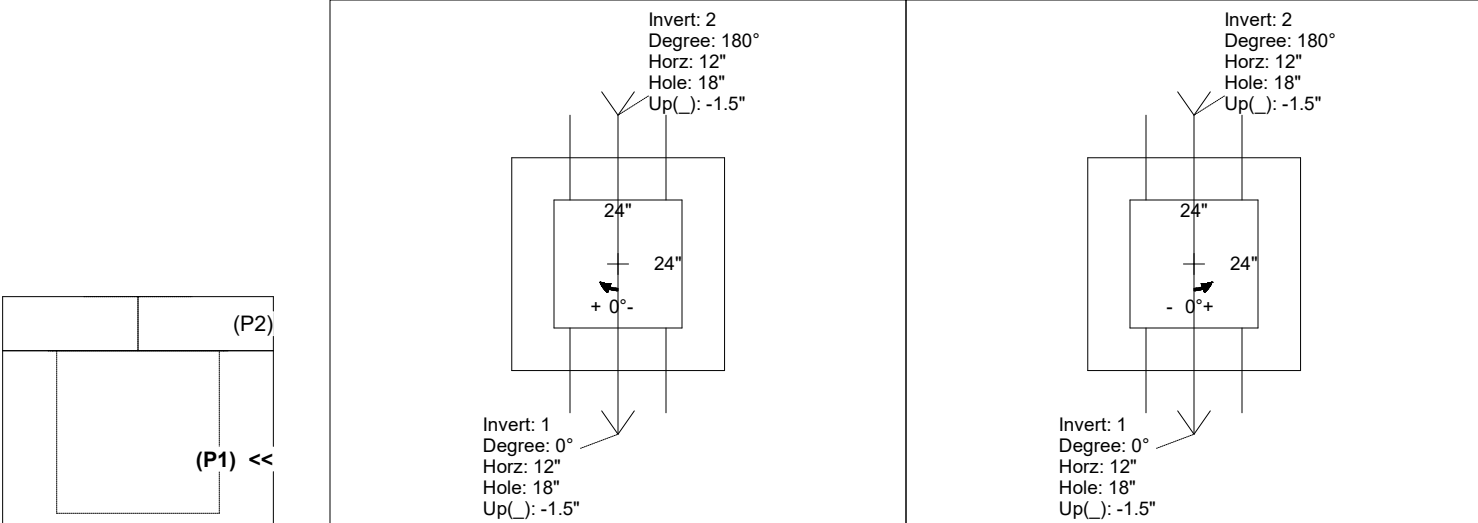
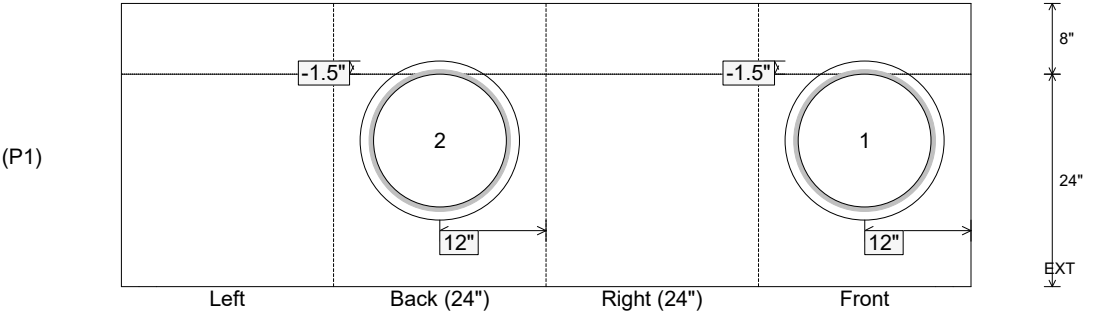


Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, Ky. 8/17/2026 10:43:58 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 130+84 RT JB-A INLET 74											
P1		BX2424-08BA24		BOX BASE 8inW, 8inF							
P2) 24" x 24" - CB FLAT TOP 8"W SOLID - 8" P1) 24" x 24" - BOX BASE 8inW, 8inF - 24" 1) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 18					1074 lb 2795 lb 0 lb 0 lb ----- Structure Total: 3869 lb		<u>Structure Notes:</u> -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.				
Rim: 590.43' Rim to Invert: 3.14' Slack: 5.68" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	587.29'	0°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 2	587.29'	180°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 24" Height (Ext): 32"		Weight (Net): 2795 lb Volume (Net): 0.71cu.yd		
