

Contractor: Cleary Construction, Inc.


PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, Ky.	



Slack: 5.68"



- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

Structure Total: 3869 lb

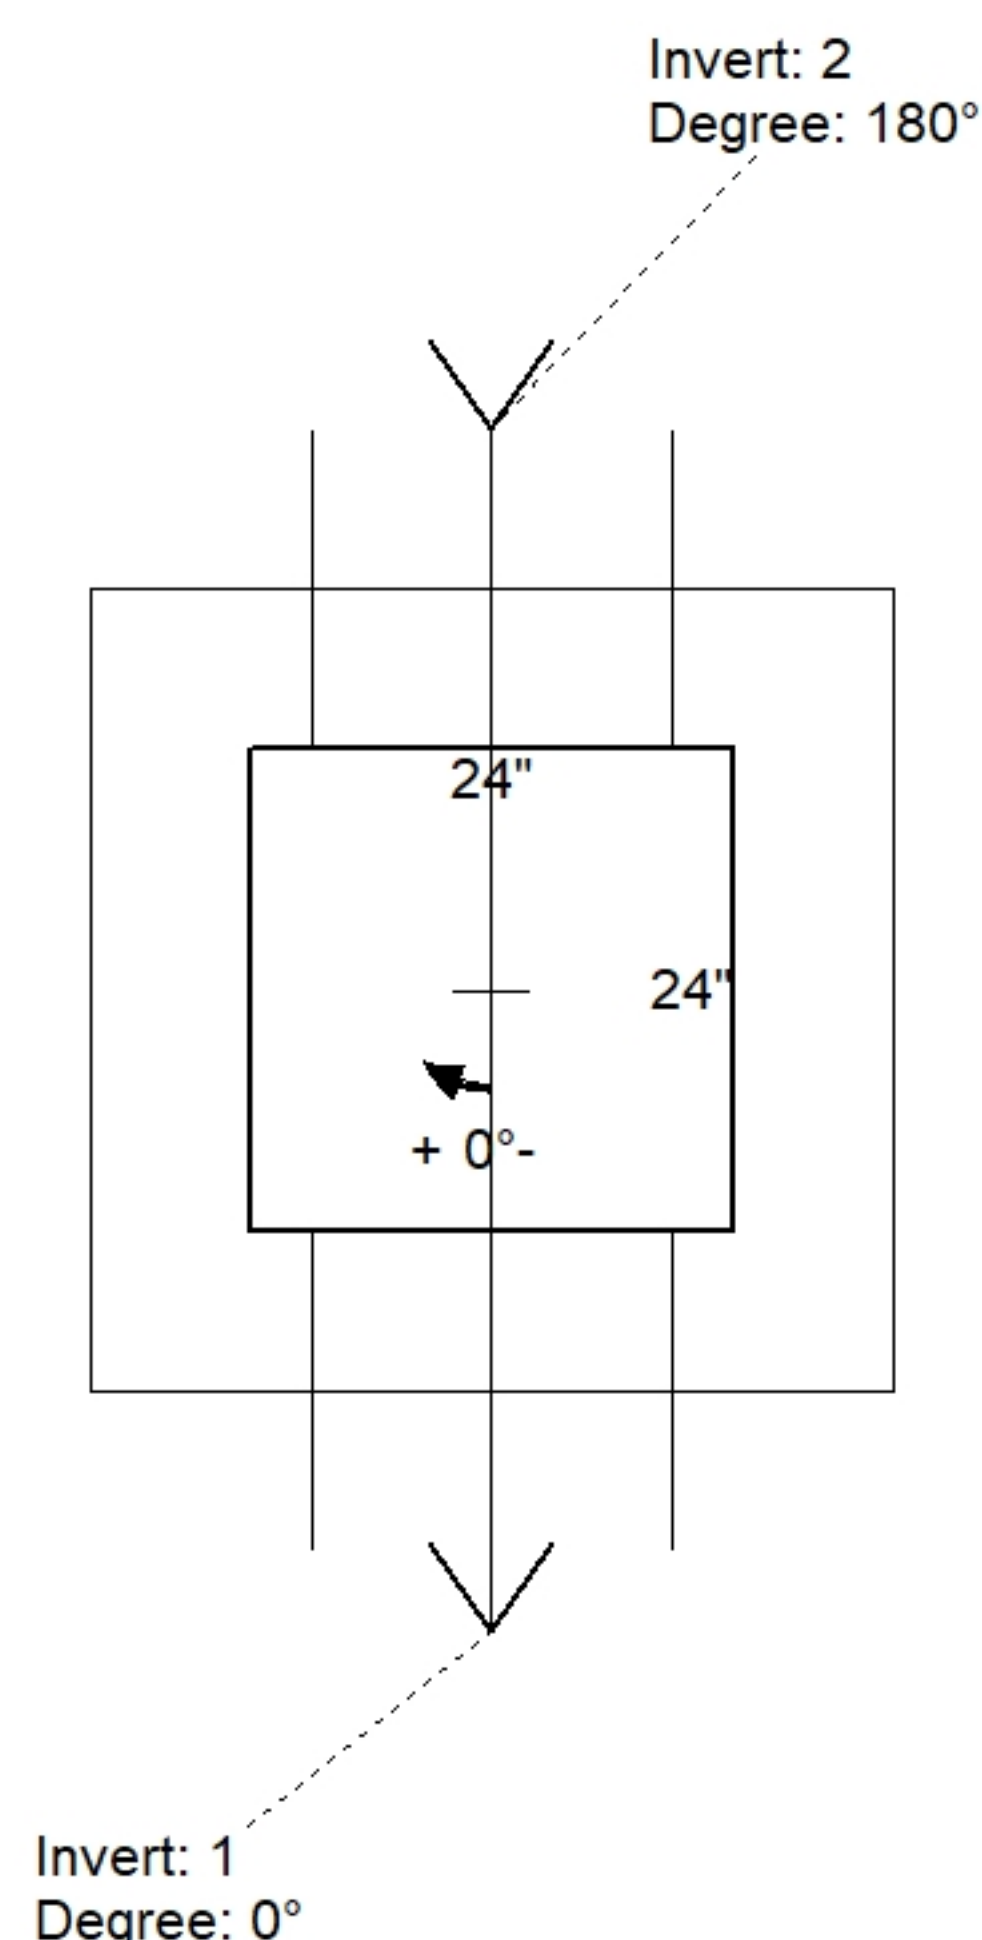

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	590.43'							
Reducer								
Invert 1	587.29'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2	587.29'	180°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

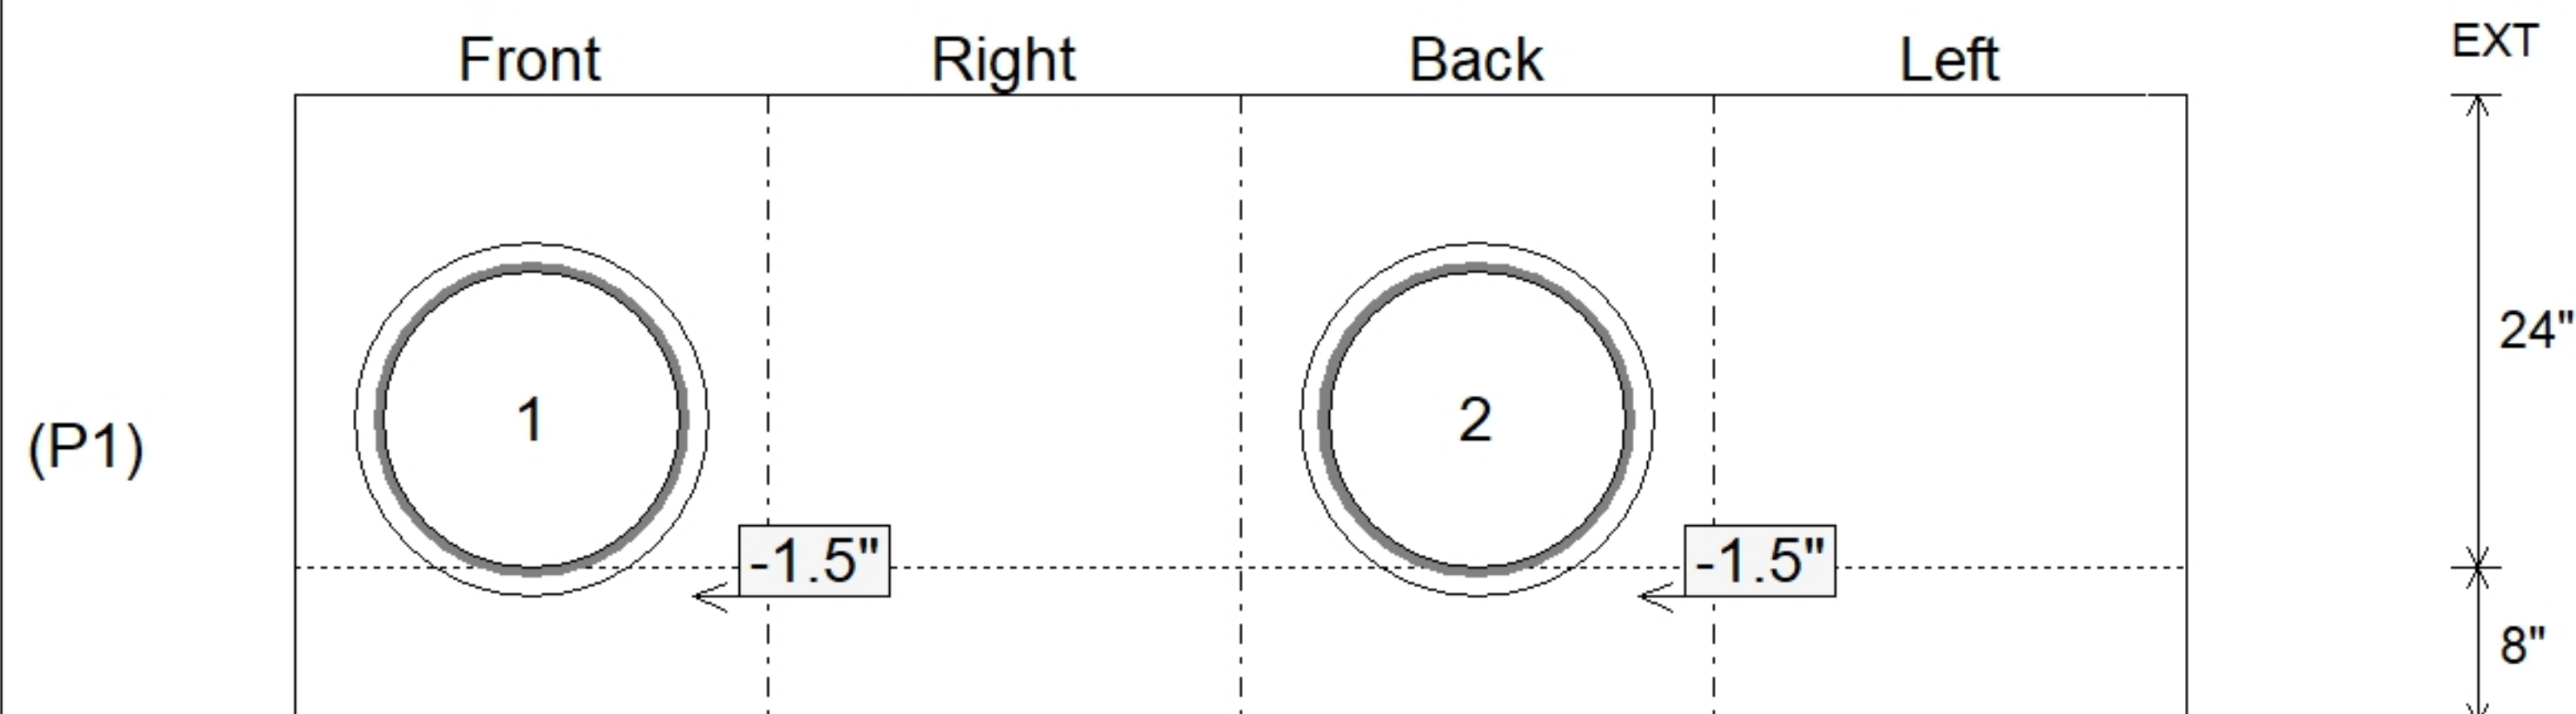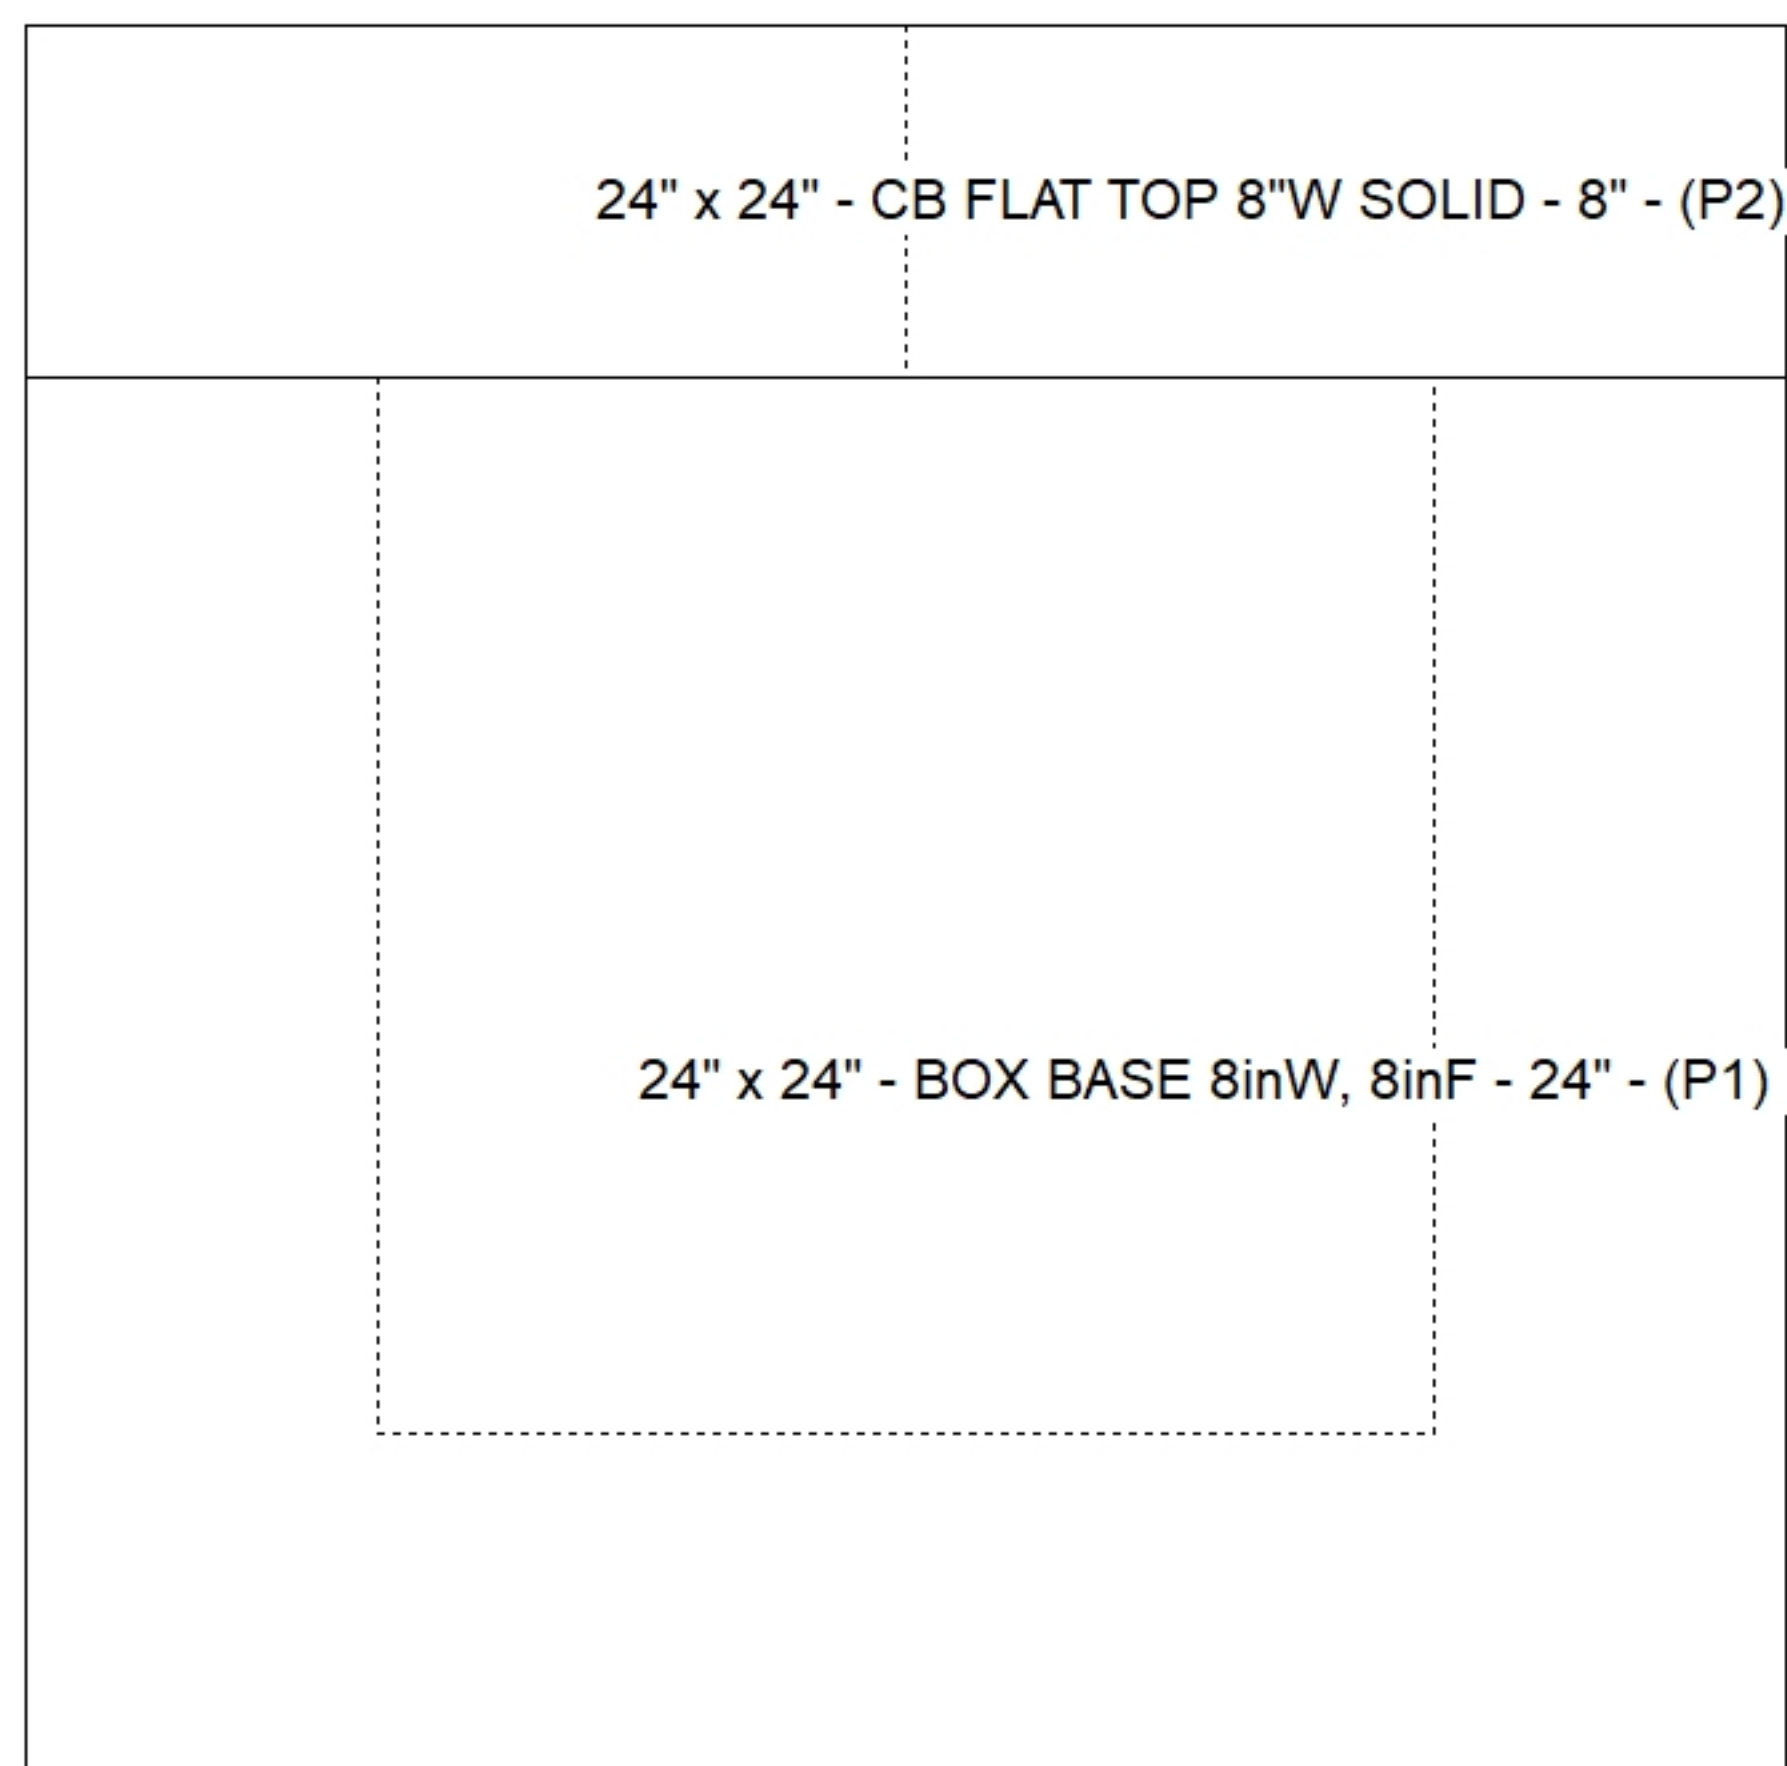

Submittal Drawing
8/18/2026 9:55:22 AM

SUBMITTAL
APPROVED BY:
