

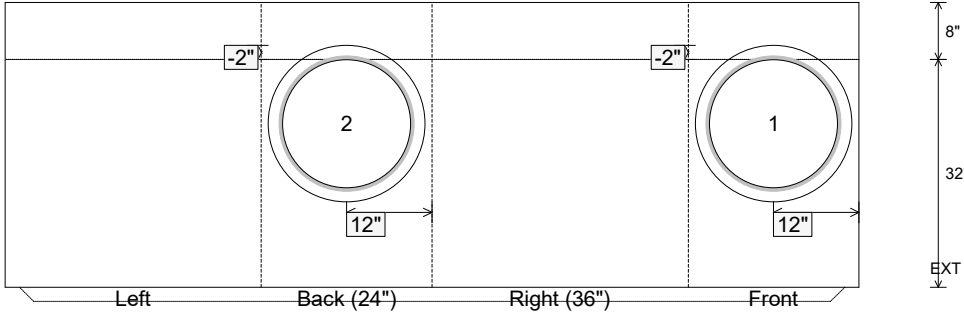
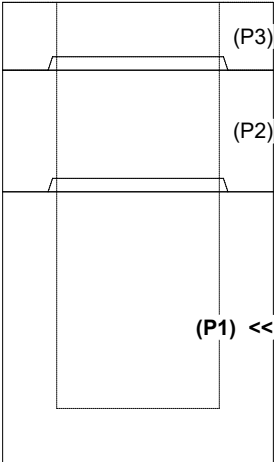


Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, Ky. 8/17/2026 10:44:02 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 14+60 RT CBIA-MOD INLET 78											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht							
P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 32" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 22"					3398 lb 5270 lb 4151 lb 0 lb 0 lb ----- Structure Total: 12819 lb		<u>Structure Notes:</u> -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.				
Rim: 588.39'		Rim to Invert: 5.33'		Slack: 3.96"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	583.06'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 2	583.06'	180°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions)   											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 32" Height (Ext): 40"		Weight (Net): 4151 lb Volume (Net): 1.06cu.yd		
