

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, Ky.	



Spec: KYTC
Type: CBI TYPE A (10')
Size: 24" x 36"

Rim: 588.39'
Invert: 583.06'
Rim to Invert: 5.33'

Sump: 0"
Floor (Top): 583.06'
Floor Height: 8"


Floor (Bot): 582.393'
Overall Height: 5.667'
Slack: 3.96"

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10"
P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 32"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 22

3398 lb
5270 lb
4151 lb
0 lb
0 lb

Structure Total: 12819 lb

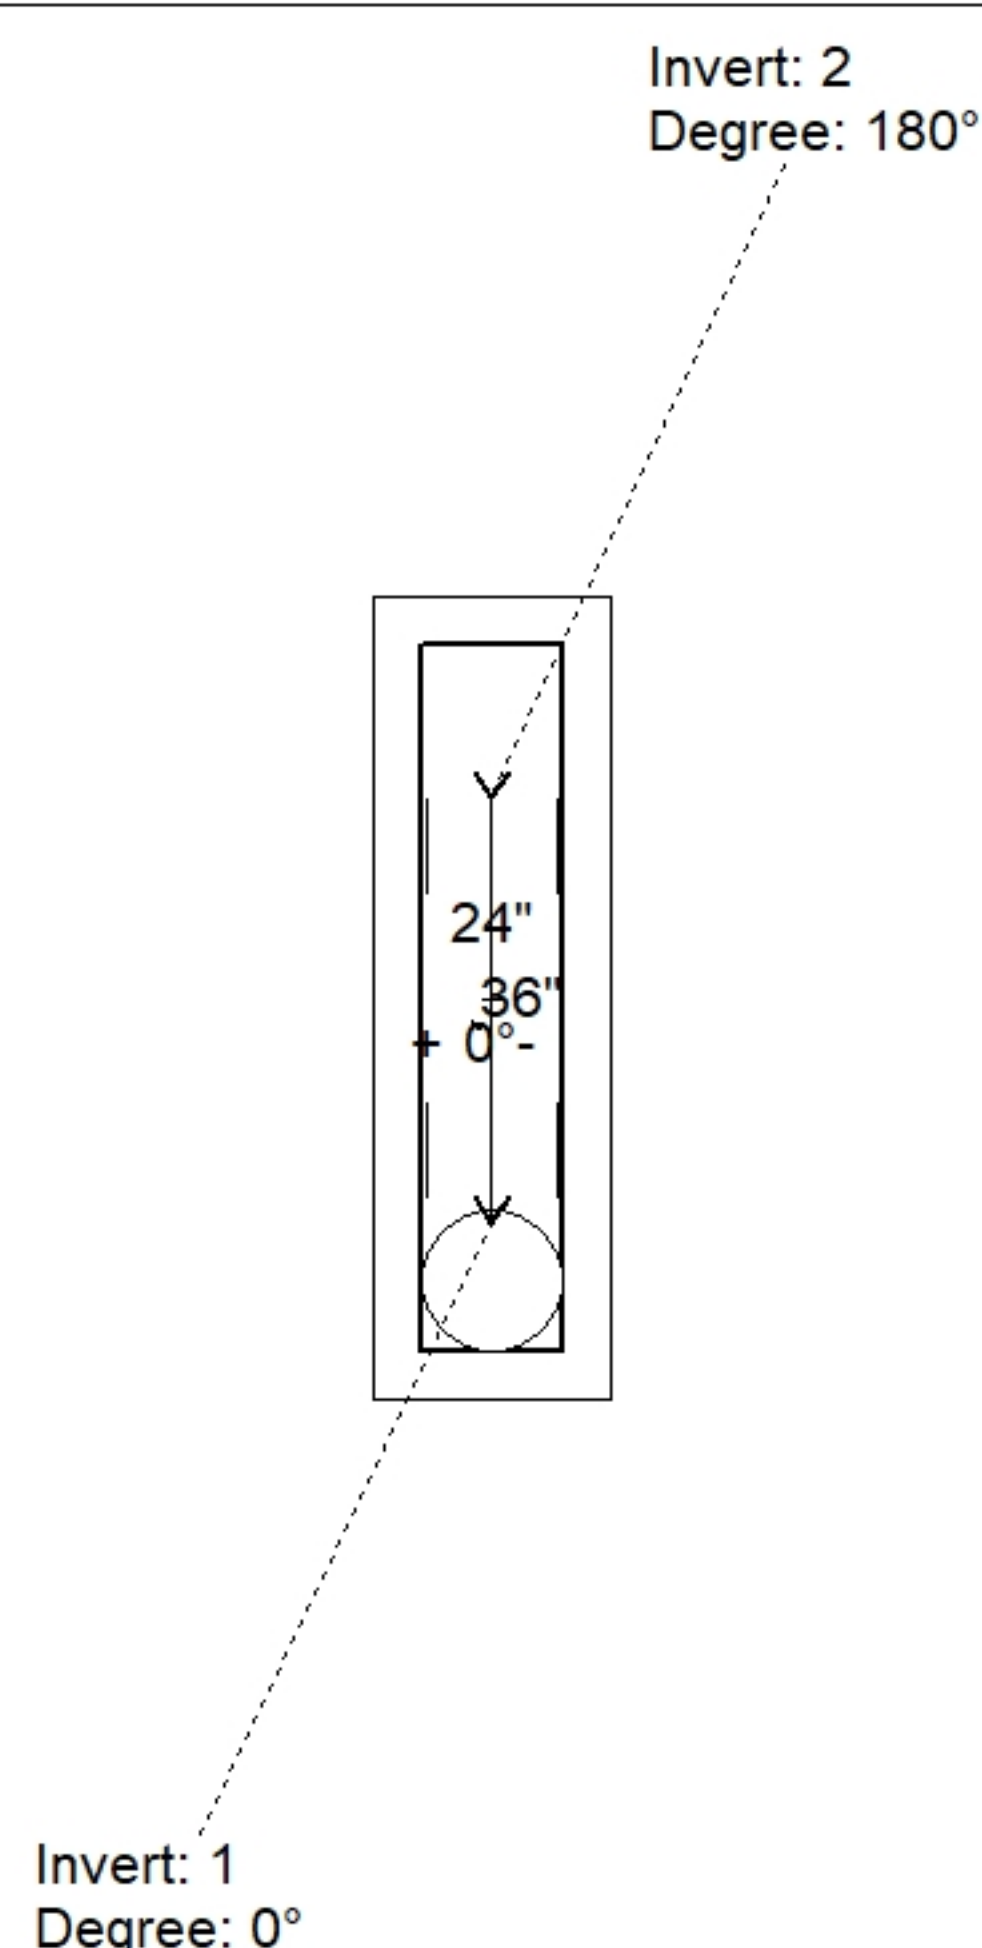


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	588.39'							
Reducer								
Invert 1	583.06'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	583.06'	180°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 120" - CB INLET KY A 10' TOP RIGHT - 10" - (P3)

24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 32" - (P1)

Default - Interior Dimensions

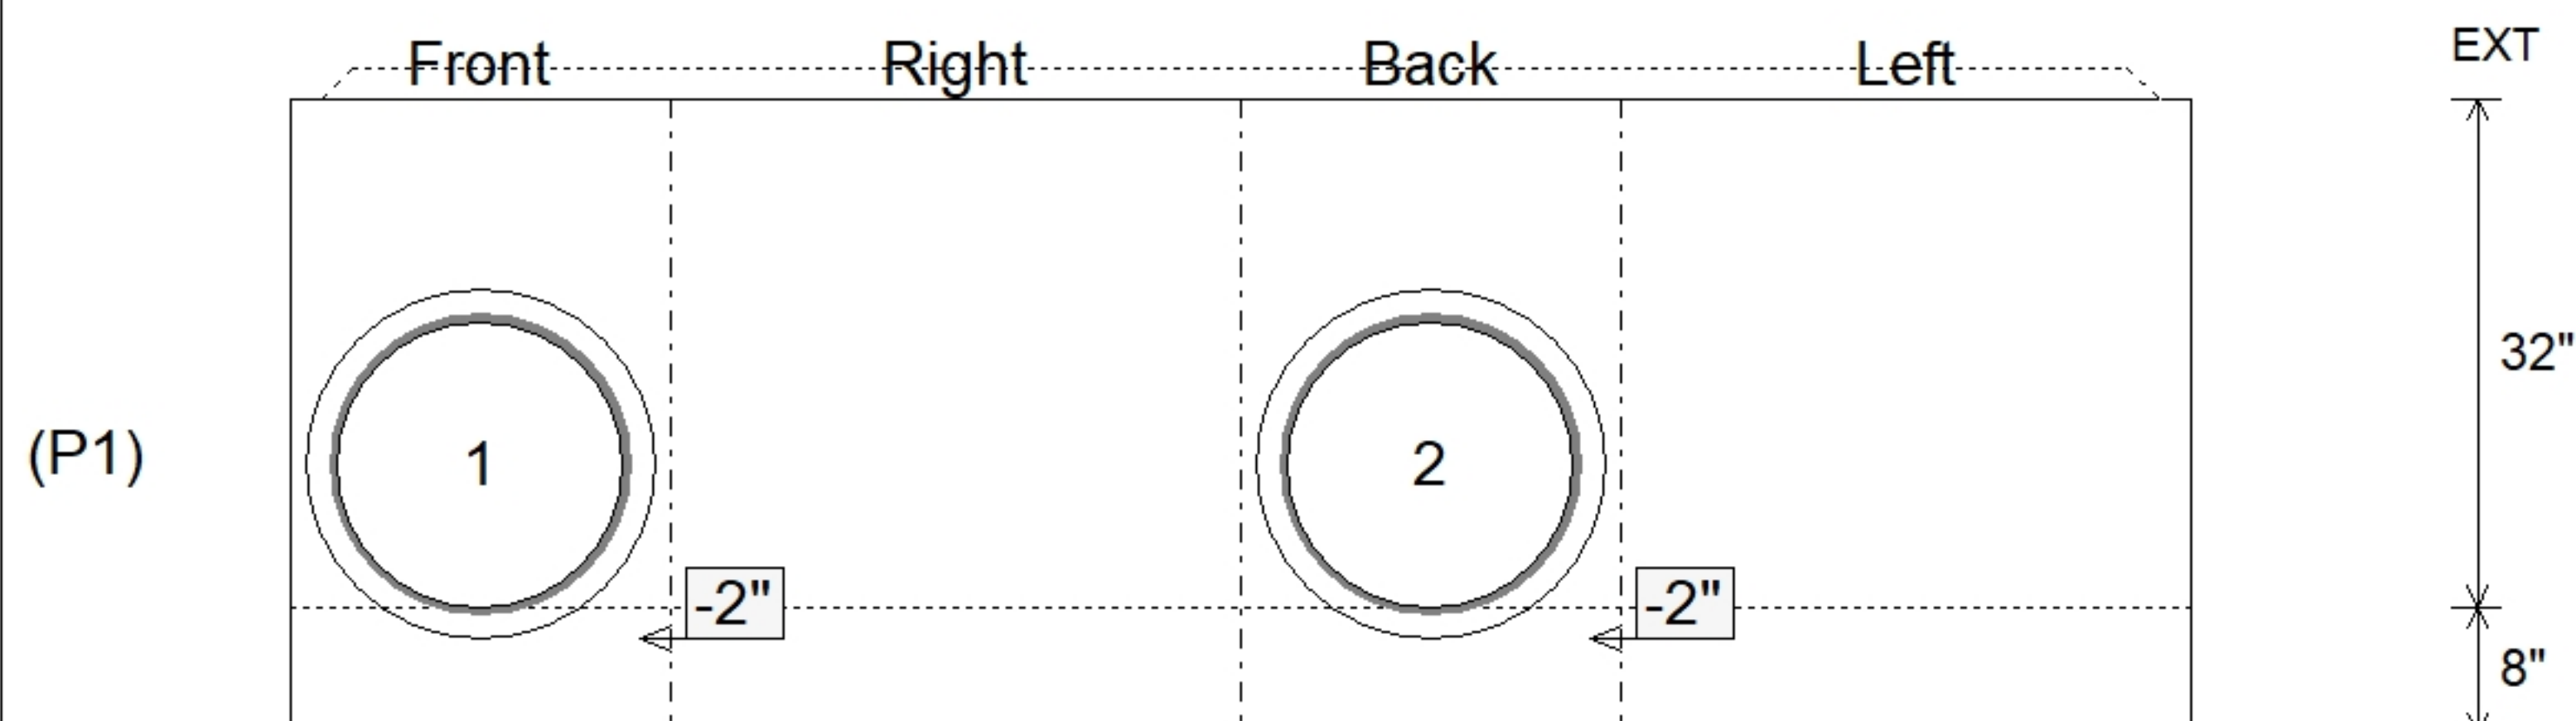

Submittal Drawing
8/18/2026 9:55:23 AM

SUBMITTAL
APPROVED BY:
