

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, Ky.	



Spec: KYTC
Type: CBI TYPE A (10')
Size: 24" x 36"

Rim: 589.18'
Invert: 583.99'
Rim to Invert: 5.19'

Sump: 0"
Floor (Top): 583.99'
Floor Height: 8"


Floor (Bot): 583.323'
Overall Height: 5.5'
Slack: 4.28"

-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.


P3) 24" x 120" - CB INLET KY A 10' TOP SAG - 10"
P2) 24" x 120" - CB INLET KY A 10' BOTTOM SAG - 18"
P1) 24" x 36" - BOX BASE 8inW, 8inF - 30"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 22

3398 lb
5270 lb
3947 lb
0 lb
0 lb


Structure Total: 12615 lb

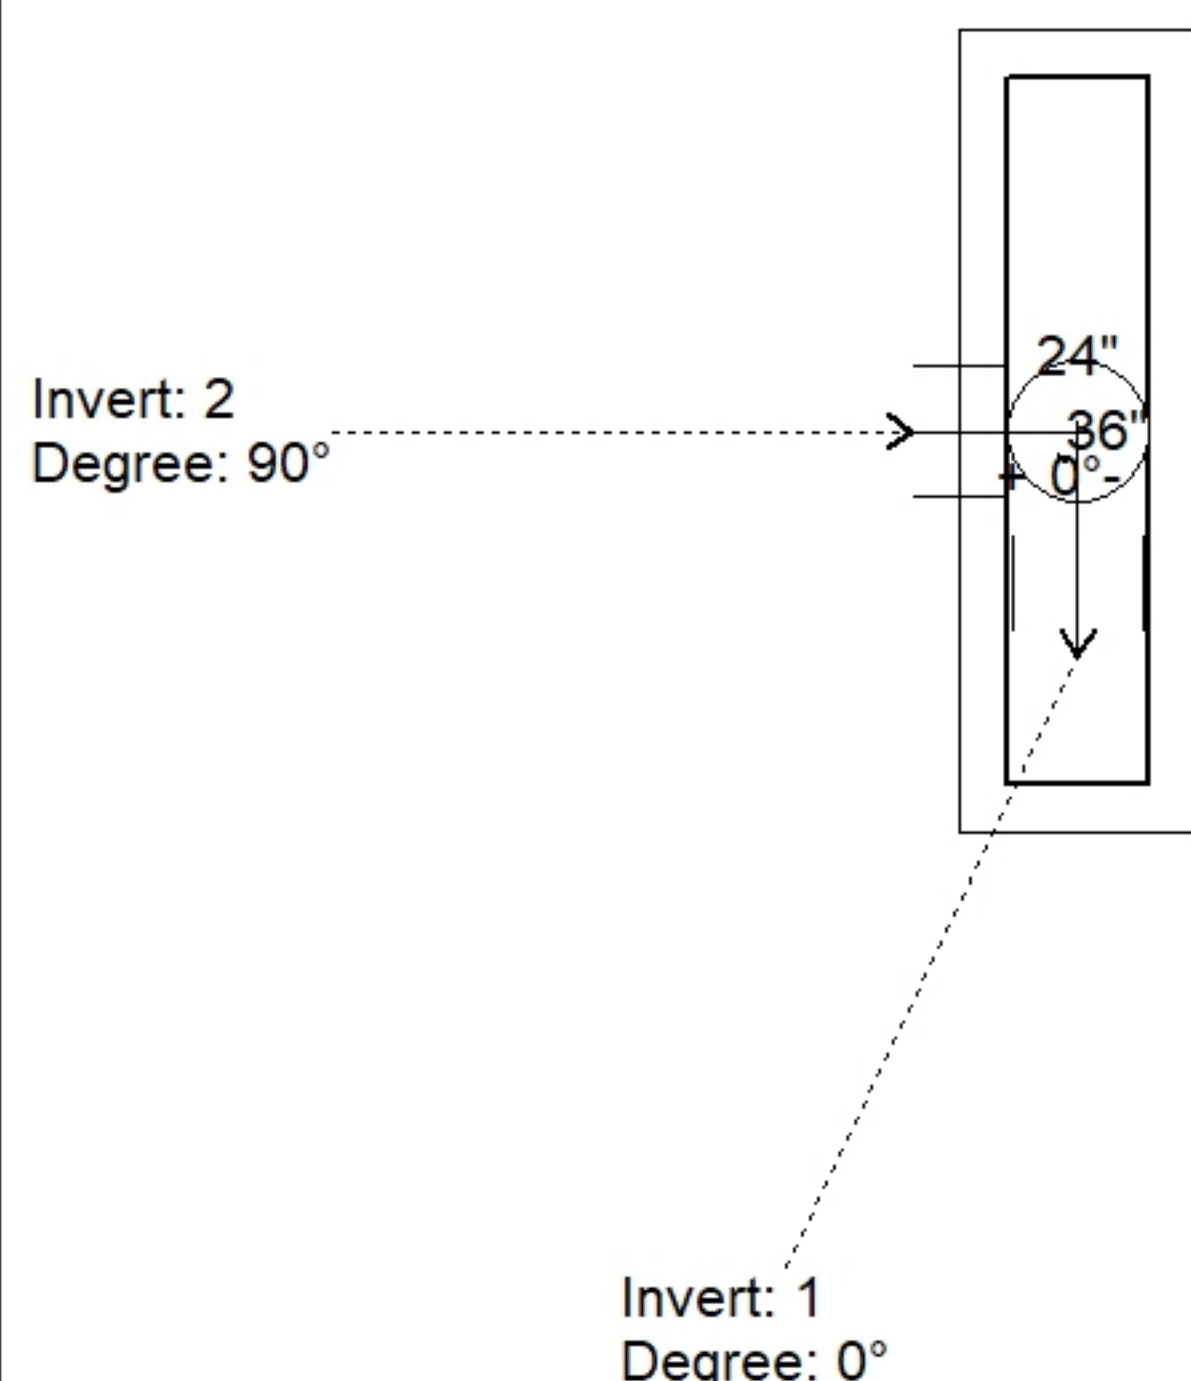

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	589.18'							
Reducer								
Invert 1	583.99'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	583.99'	90°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

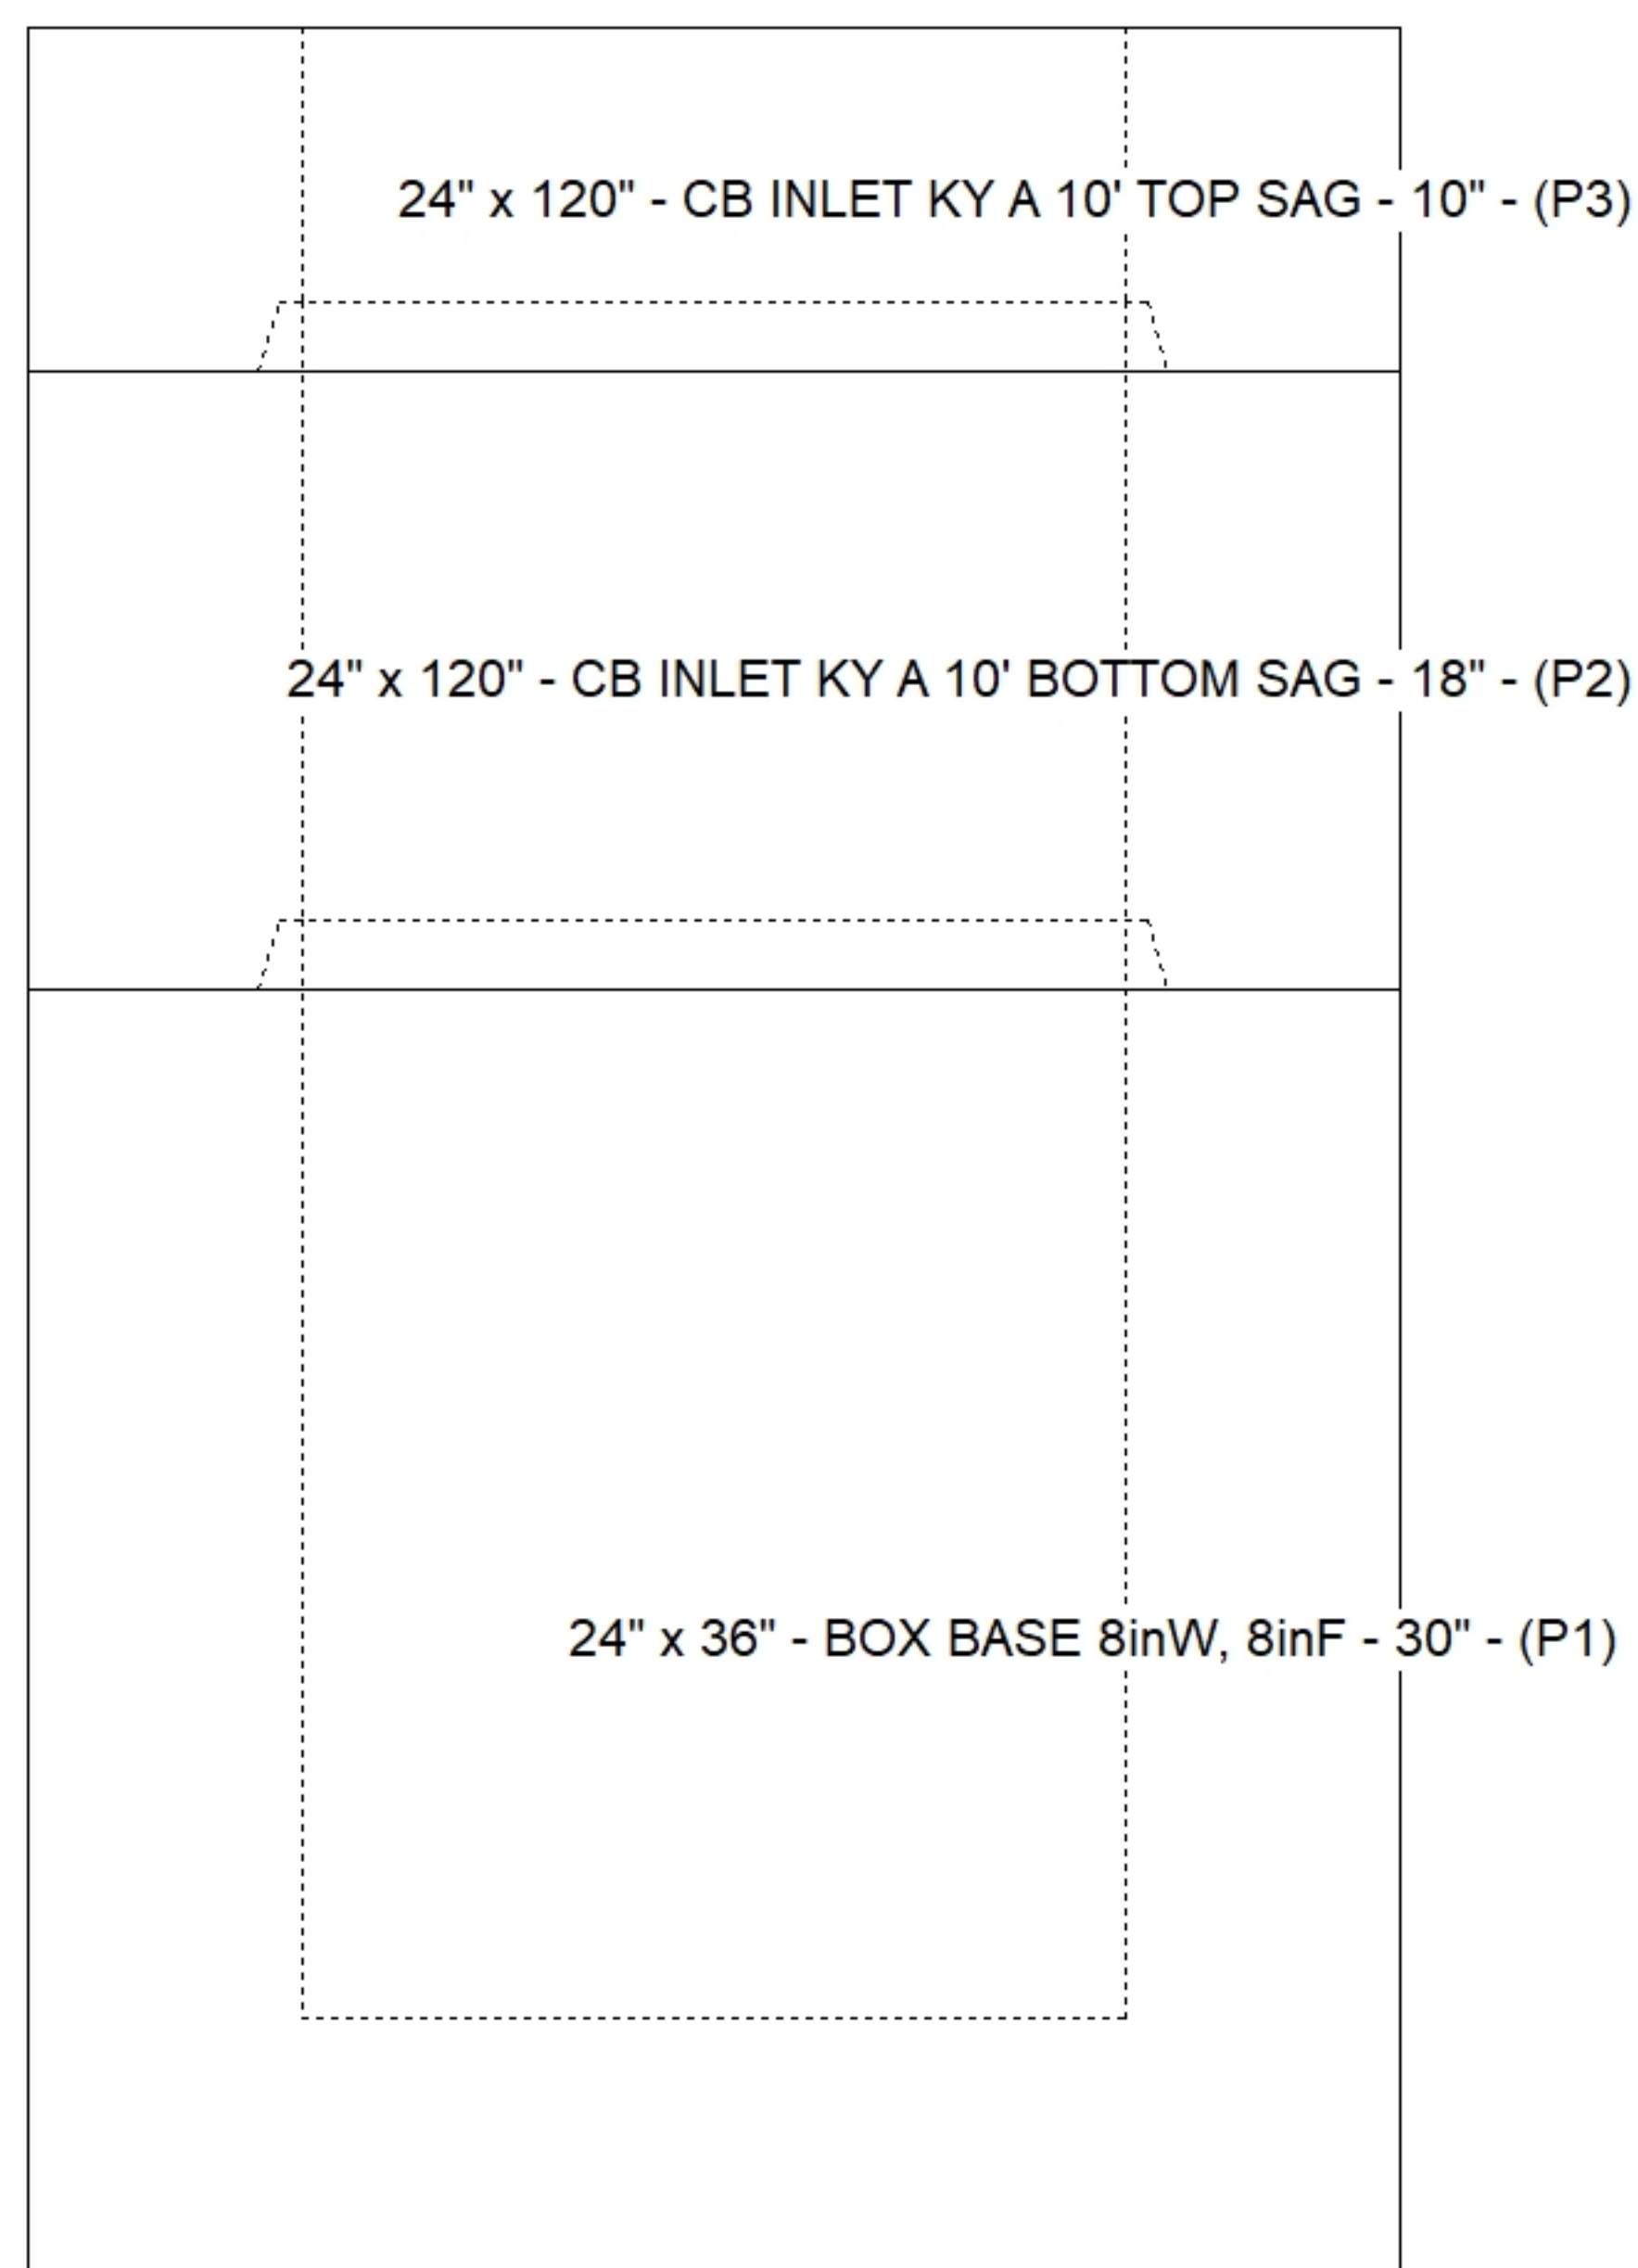

Default - Interior Dimensions

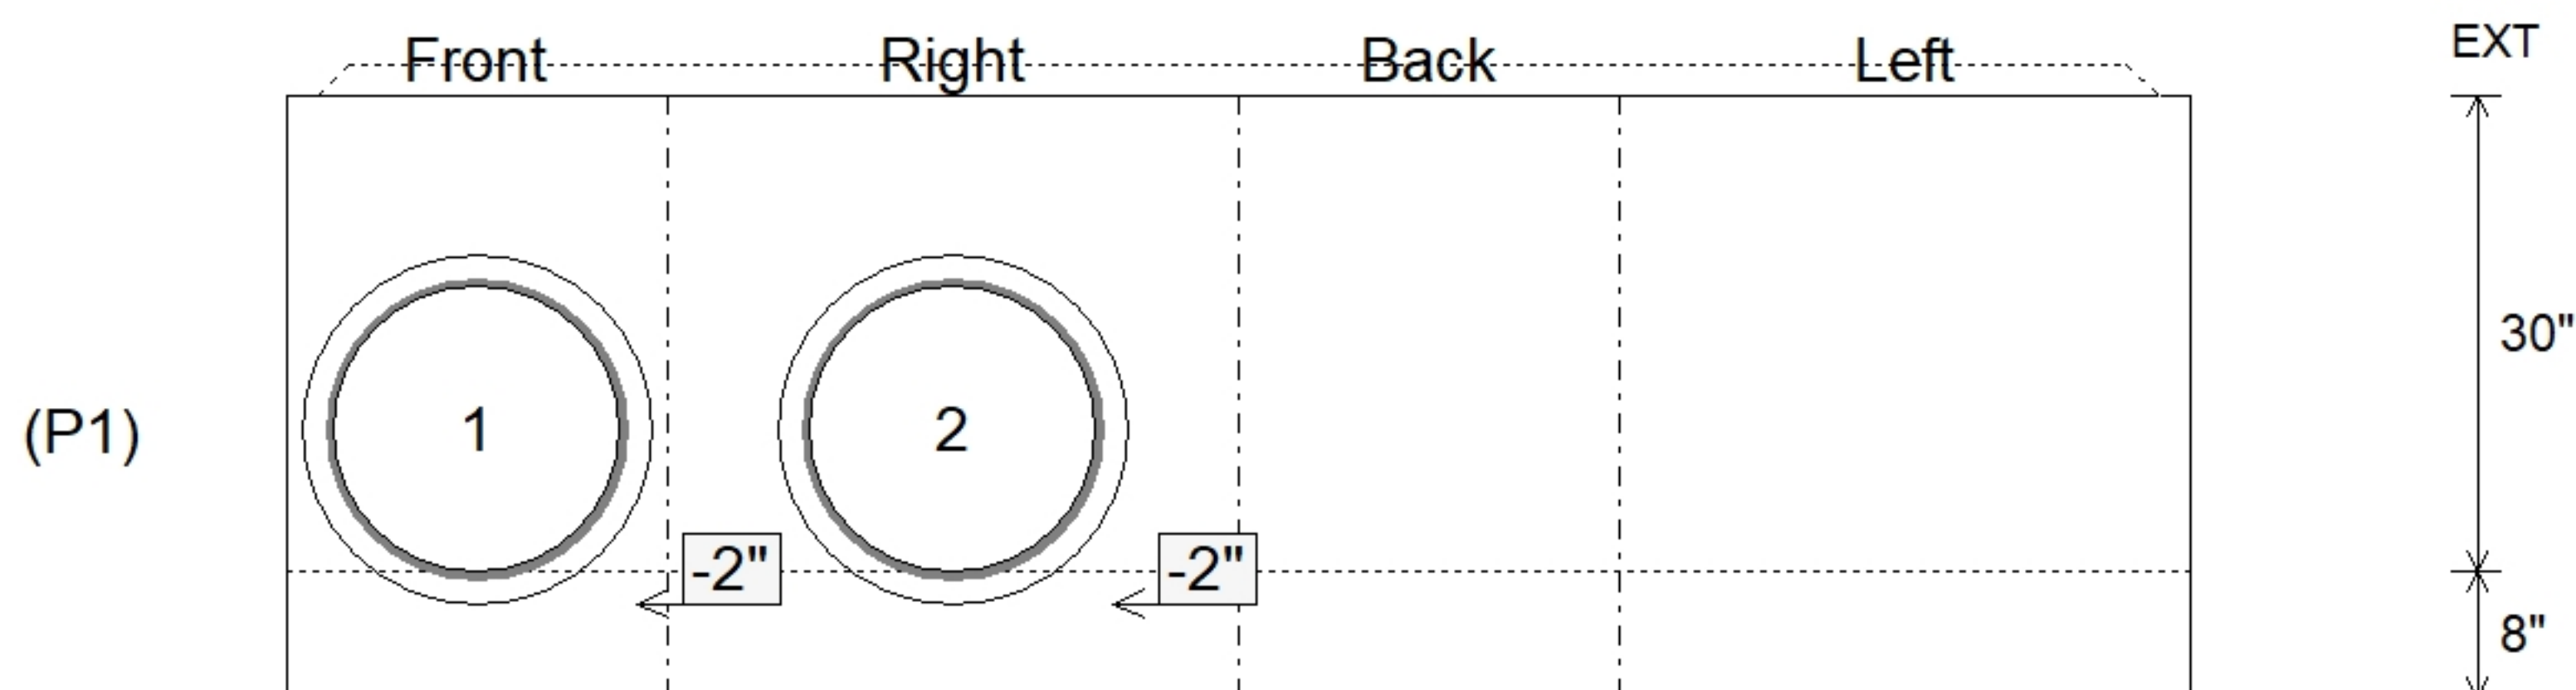

Submittal Drawing
8/18/2026 9:55:13 AM

SUBMITTAL
APPROVED BY:
