

Contractor: Cleary Construction, Inc.

PC: T. Ryan

TECH: J. Coppage

Plant: Beaver Dam, Ky.



Spec: KYTC
Type: CBI TYPE B (10')
Size: 24" x 36"

Rim: 588.68'	Sump: 0"
Invert: 583.4'	Floor (Top): 583.4'
Rim to Invert: 5.28'	Floor Height: 8"


Floor (Bot): 582.733'
Overall Height: 5.667'
Slack: 3.36"

Structure Notes: .
 -KYTC STATE PROJECT 251007
 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
 -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
 -KYTC CERTIFICATIONS REQUIRED.


STRUCTURE SUMMARY:

P4) 8" x 120" - CB INLET KY B 10' TOP - 9"	1660 lb
P3) 24" x 120" - CB INLET KY B 10' BOTTOM LEFT - 17"	2650 lb
P2) 24" x 36" - CB FT REDUCER 24"X24" HOLE - 8"	1010 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26"	3461 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) 24" x 24" - Conseal CS-102 1.00"	0 lb
2) Hole - 22	0 lb


Structure Total:	8781 lb

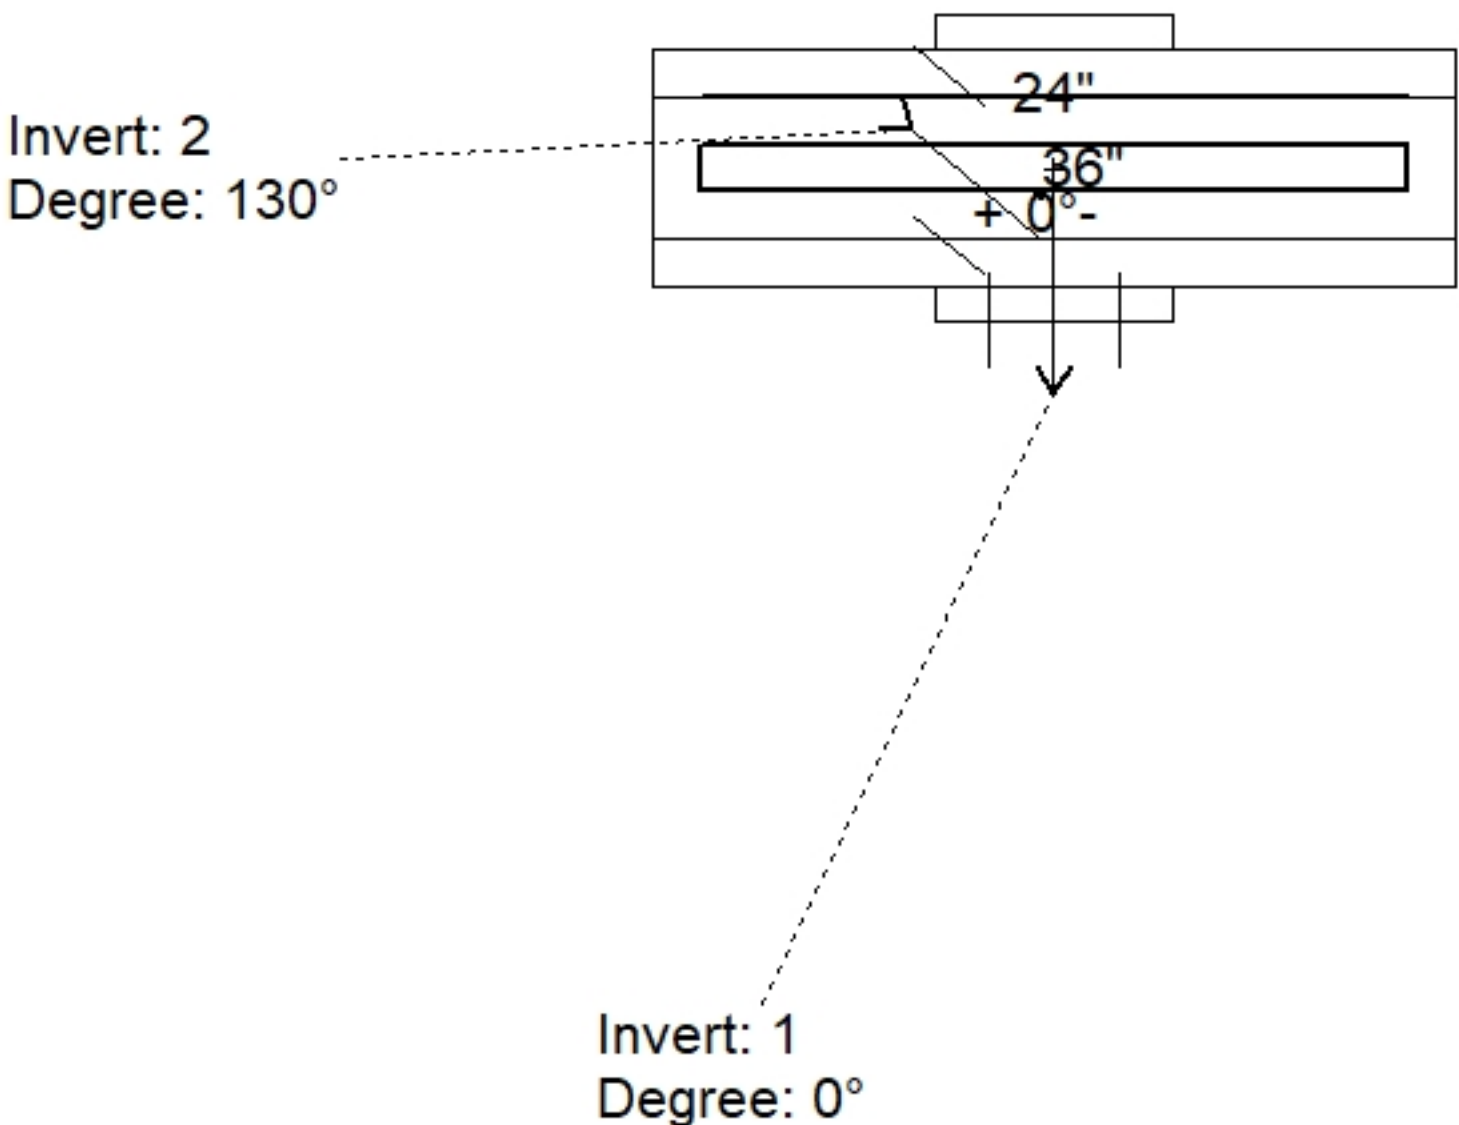

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	588.68'							
Reducer	585.567'							
Invert 1	583.4'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	583.4'	130°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

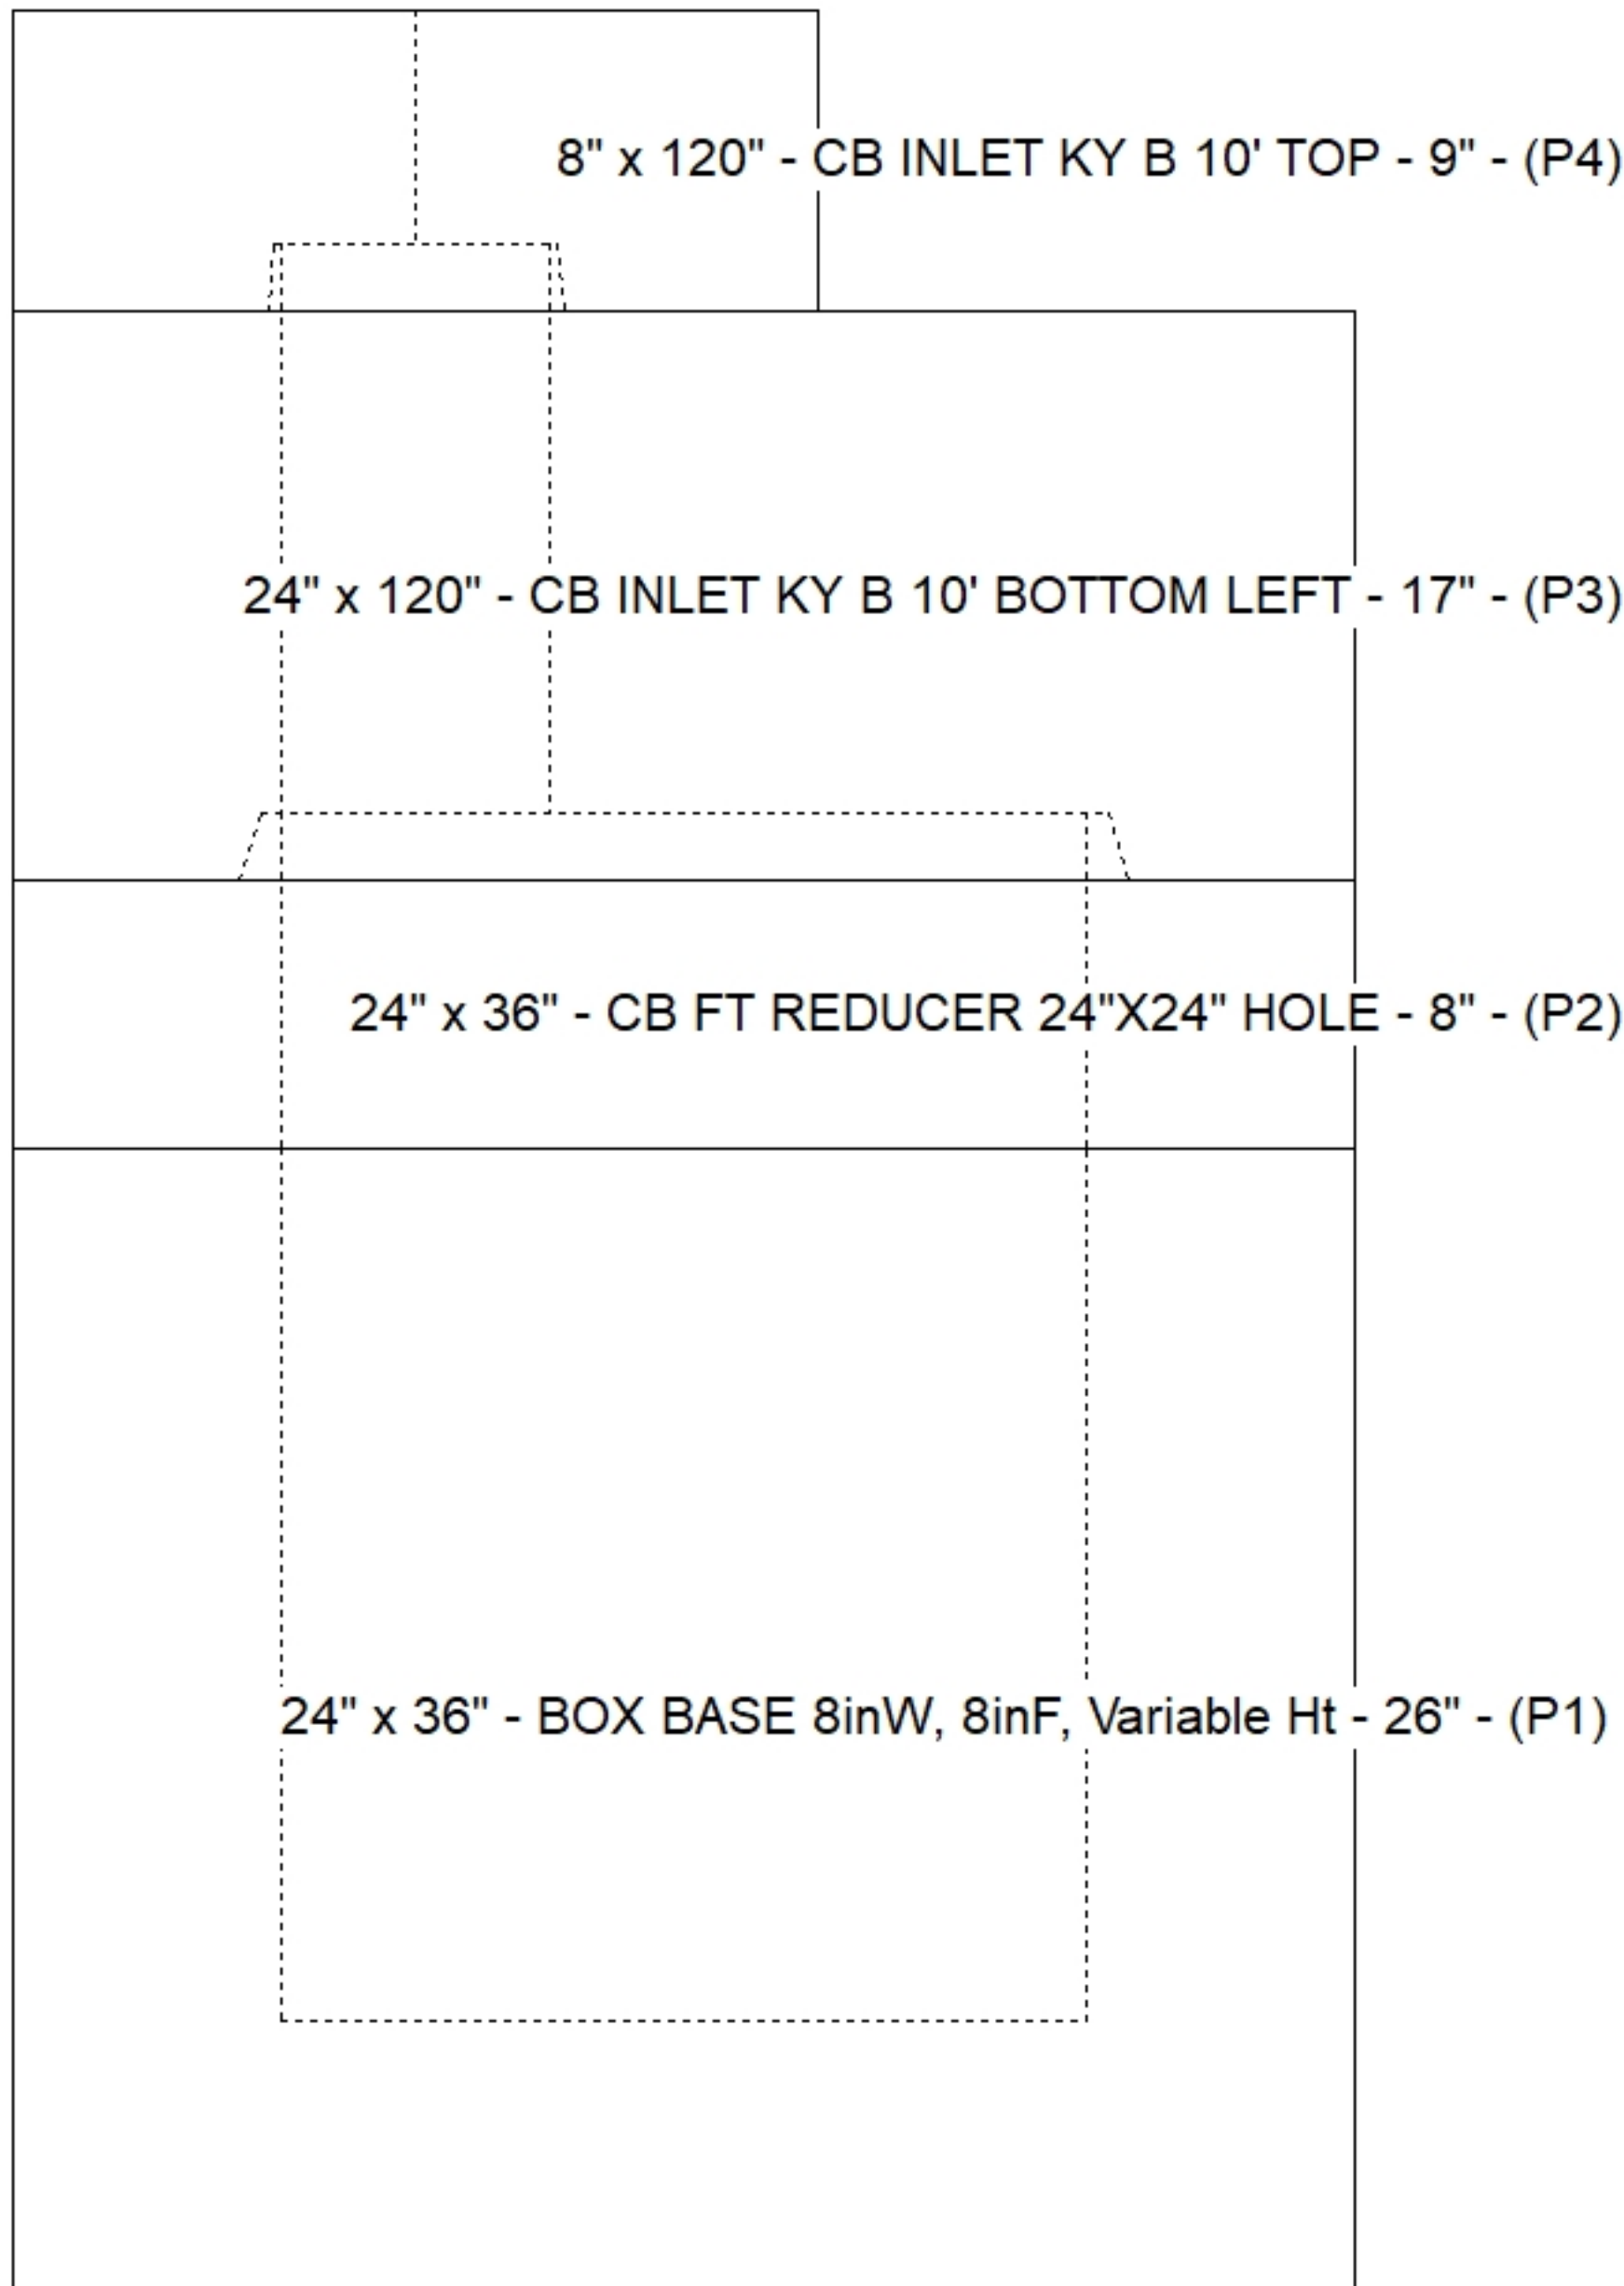

Default - Interior Dimensions

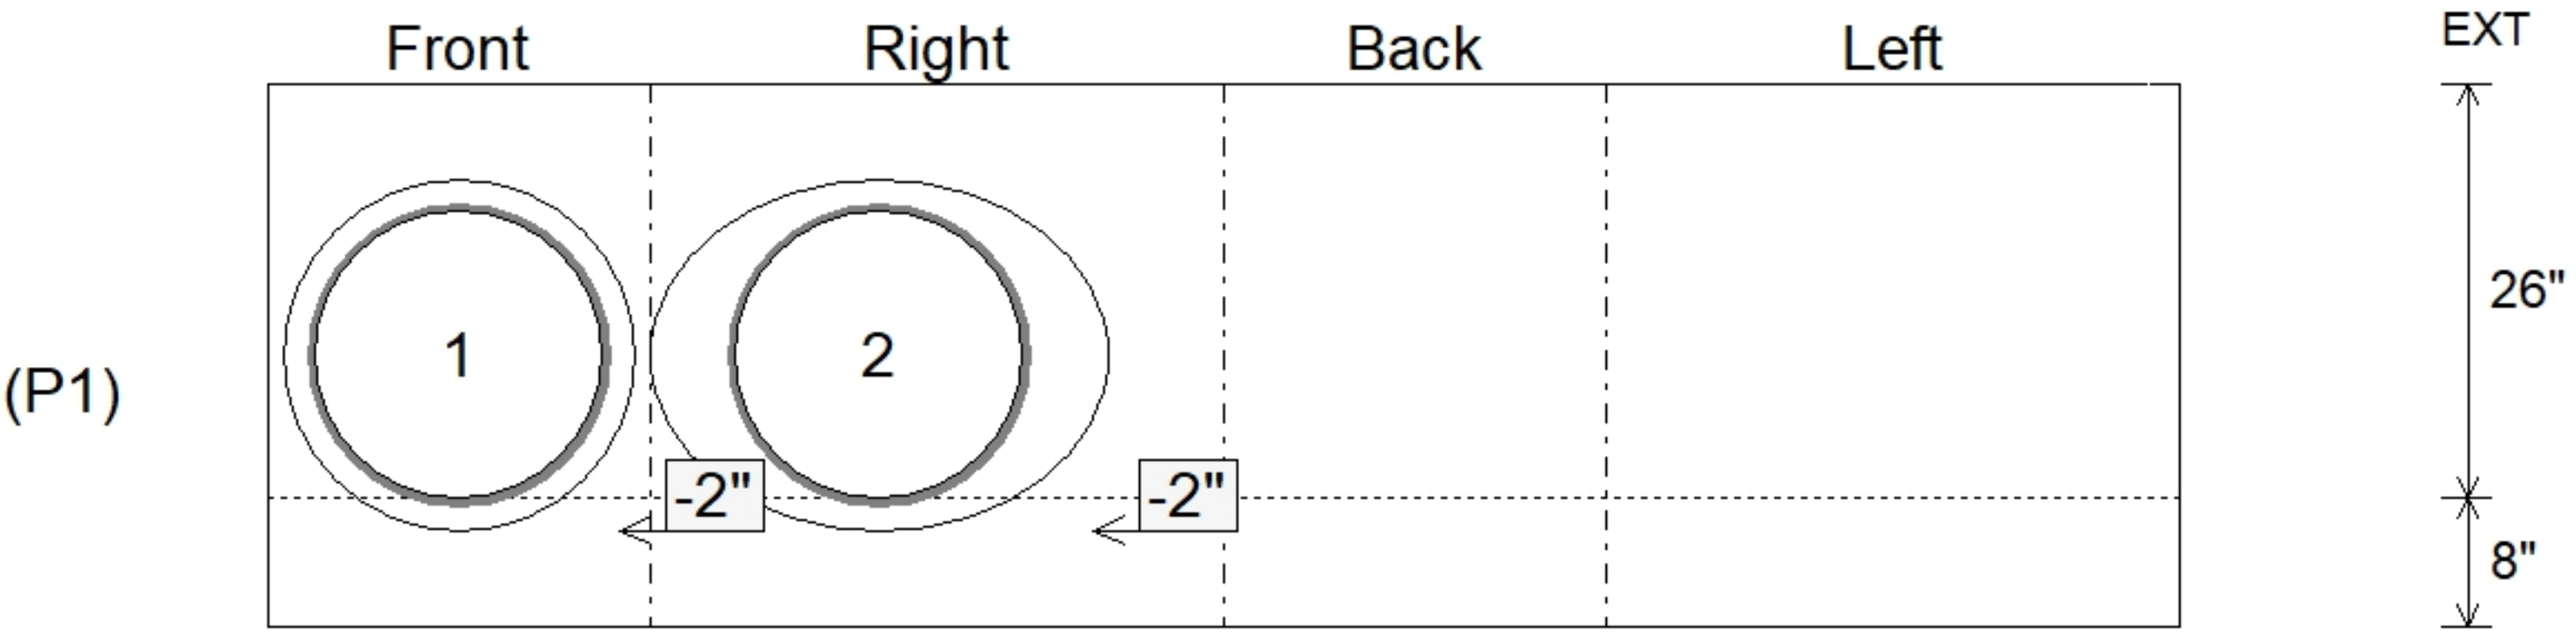

Submittal Drawing
8/18/2026 9:55:25 AM

SUBMITTAL
APPROVED BY:
