

Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.
8/17/2026 10:44:57 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 304+00 LT JB-A INLET 79

P2 BXLD2436FL8-S



BX FLAT LID 8inW SOLID

- P2) 24" x 36" - BX FLAT LID 8inW SOLID - 8"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 27"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 26
1) Hole - 18

1396 lb
3268 lb
0 lb
0 lb
0 lb

Structure Total: 4664 lb

Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

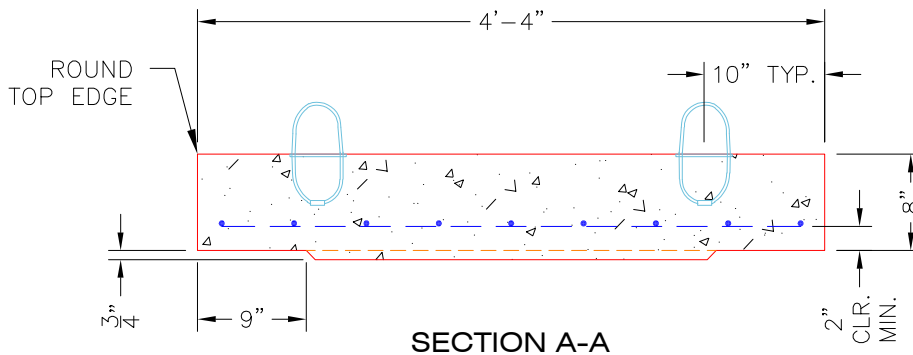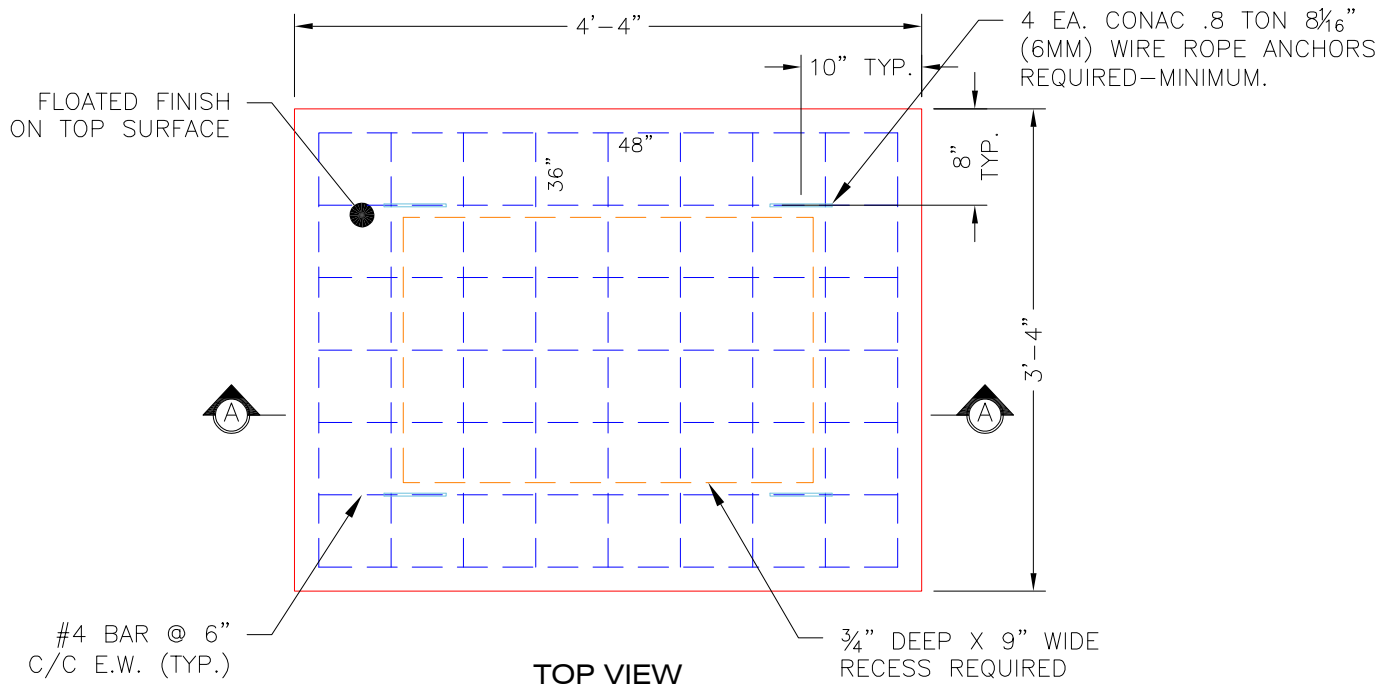

NOTES:
-CONCRETE: 4500 PSI @ 28 DAYS.
-MANUFACTURE TO KYTC SPECIFICATIONS.
-REINFORCING: #4 BAR @ 6" C/C E.W.-GRADE 60.
(BOTTOM LAYER ONLY)
-4 EA. CONAC WIRE LOOP LIFTERS REQUIRED.

#4 BAR CUT LIST
7 EA. @ 48"
9 EA. @ 36"

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1396 lb
Volume (Net): 0.36cu.yd
