

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, Ky.	




Slack: 0.28"

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

P2) 24" x 36" - BX FLAT LID 8inW SOLID - 8"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 27"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 26
1) Hole - 18

1396 lb
3268 lb
0 lb
0 lb
0 lb

Structure Total: 4664 lb

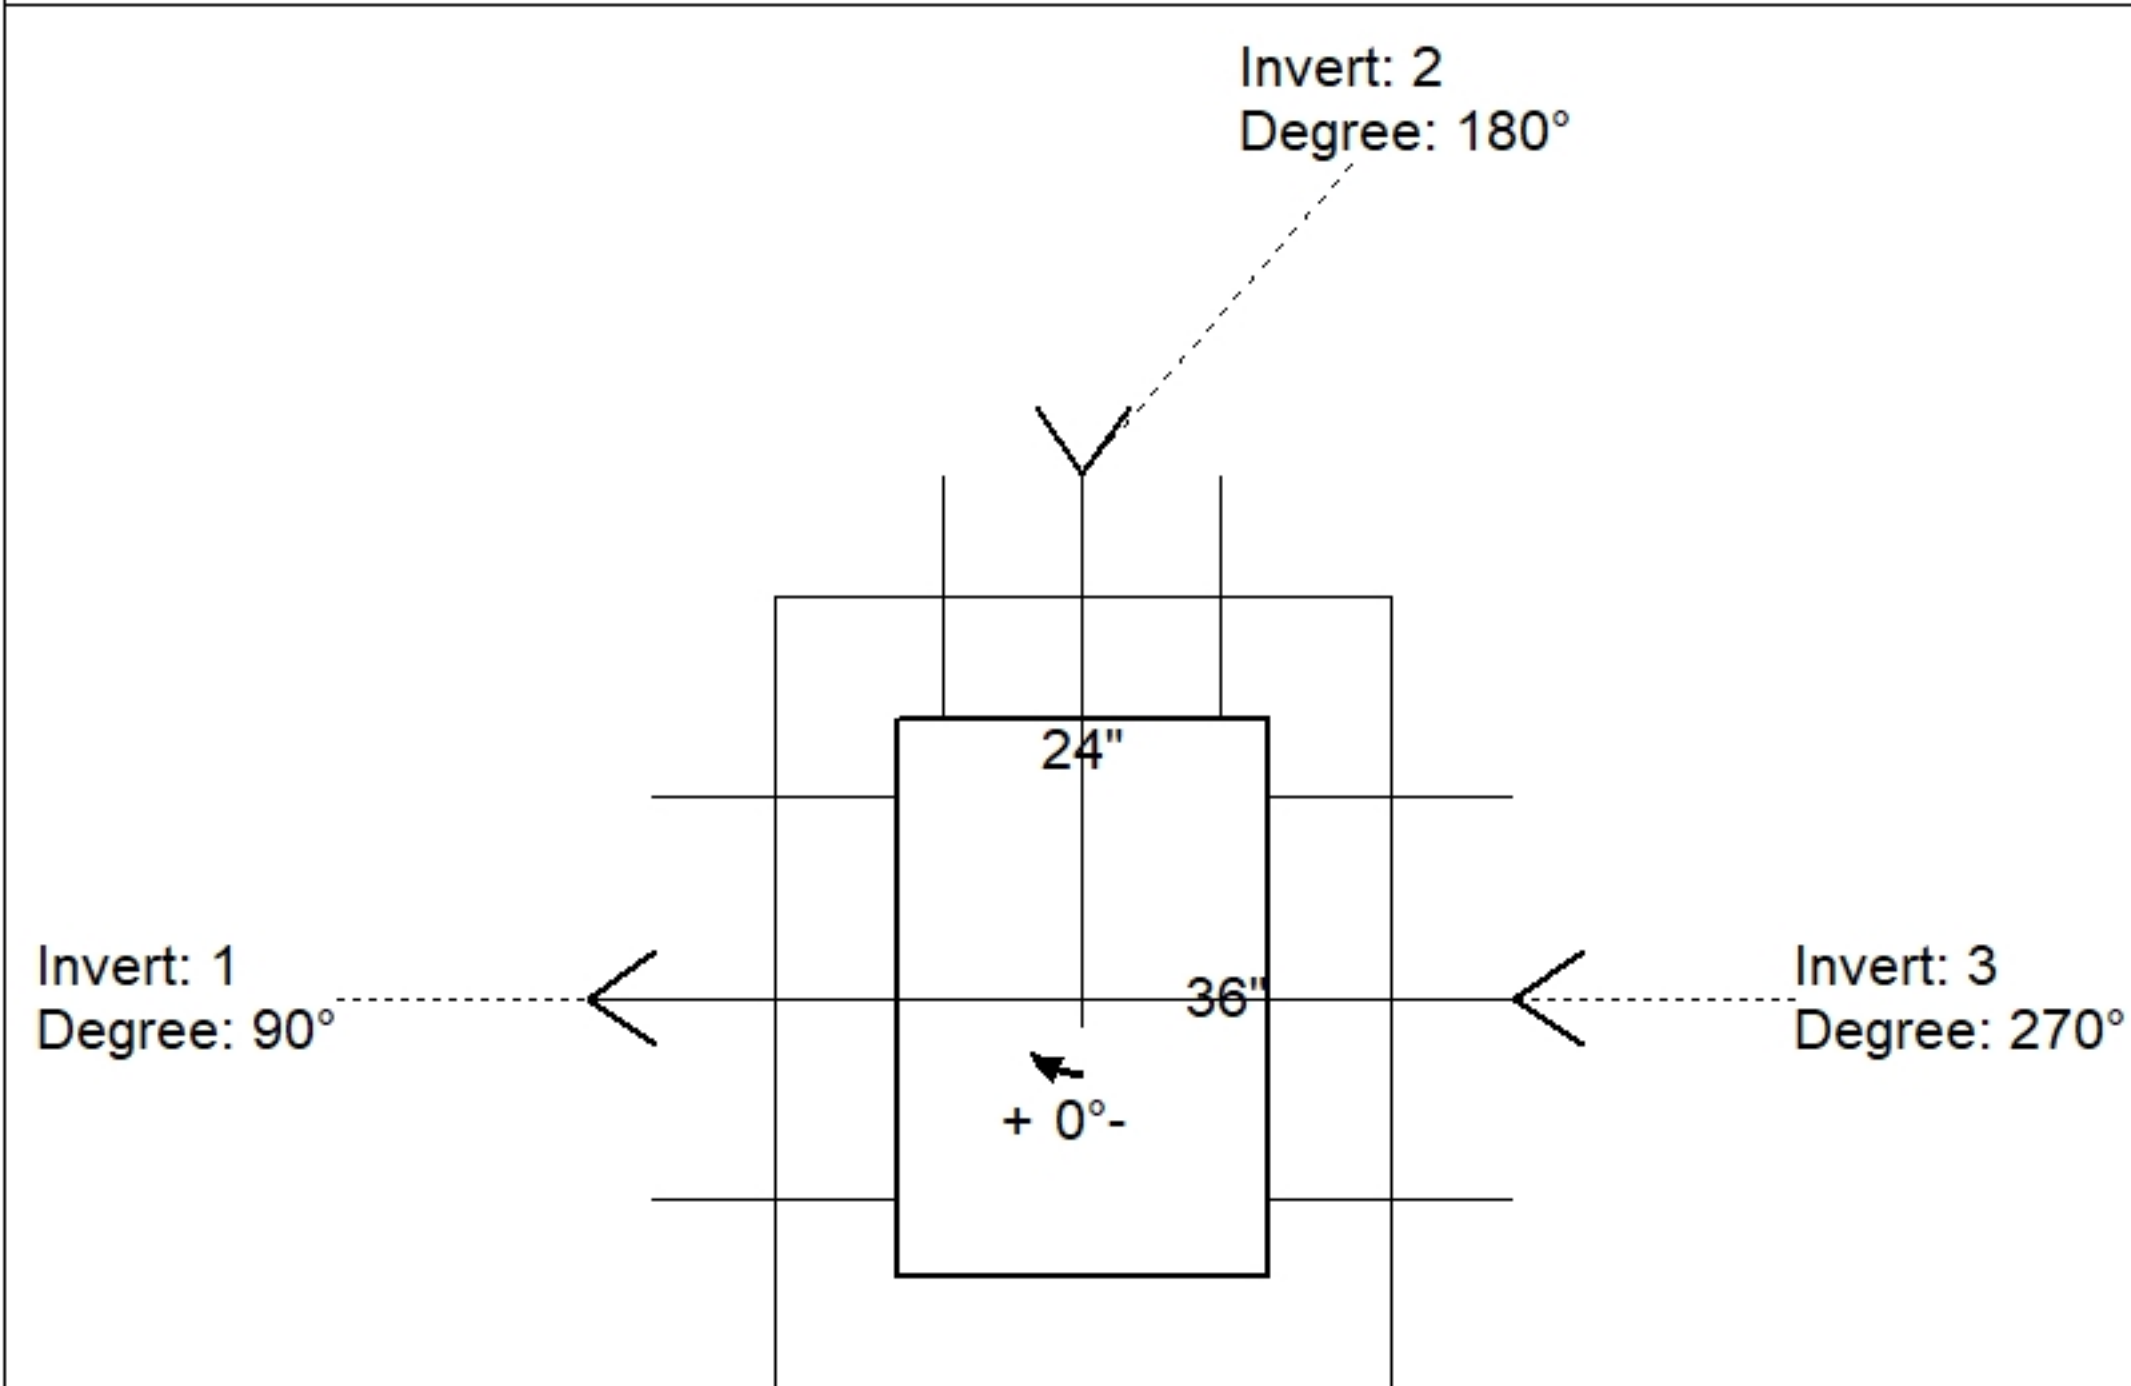


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	588'							
Reducer								
Invert 1	585.06'	90°	18" RCP B WALL	23"	26"	Hole 26	-4"	P1
Invert 2	585.06'	180°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 3	585.06'	270°	18" RCP B WALL	23"	26"	Hole 26	-4"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - BX FLAT LID 8inW SOLID - 8" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 27" - (P1)

Default - Interior Dimensions

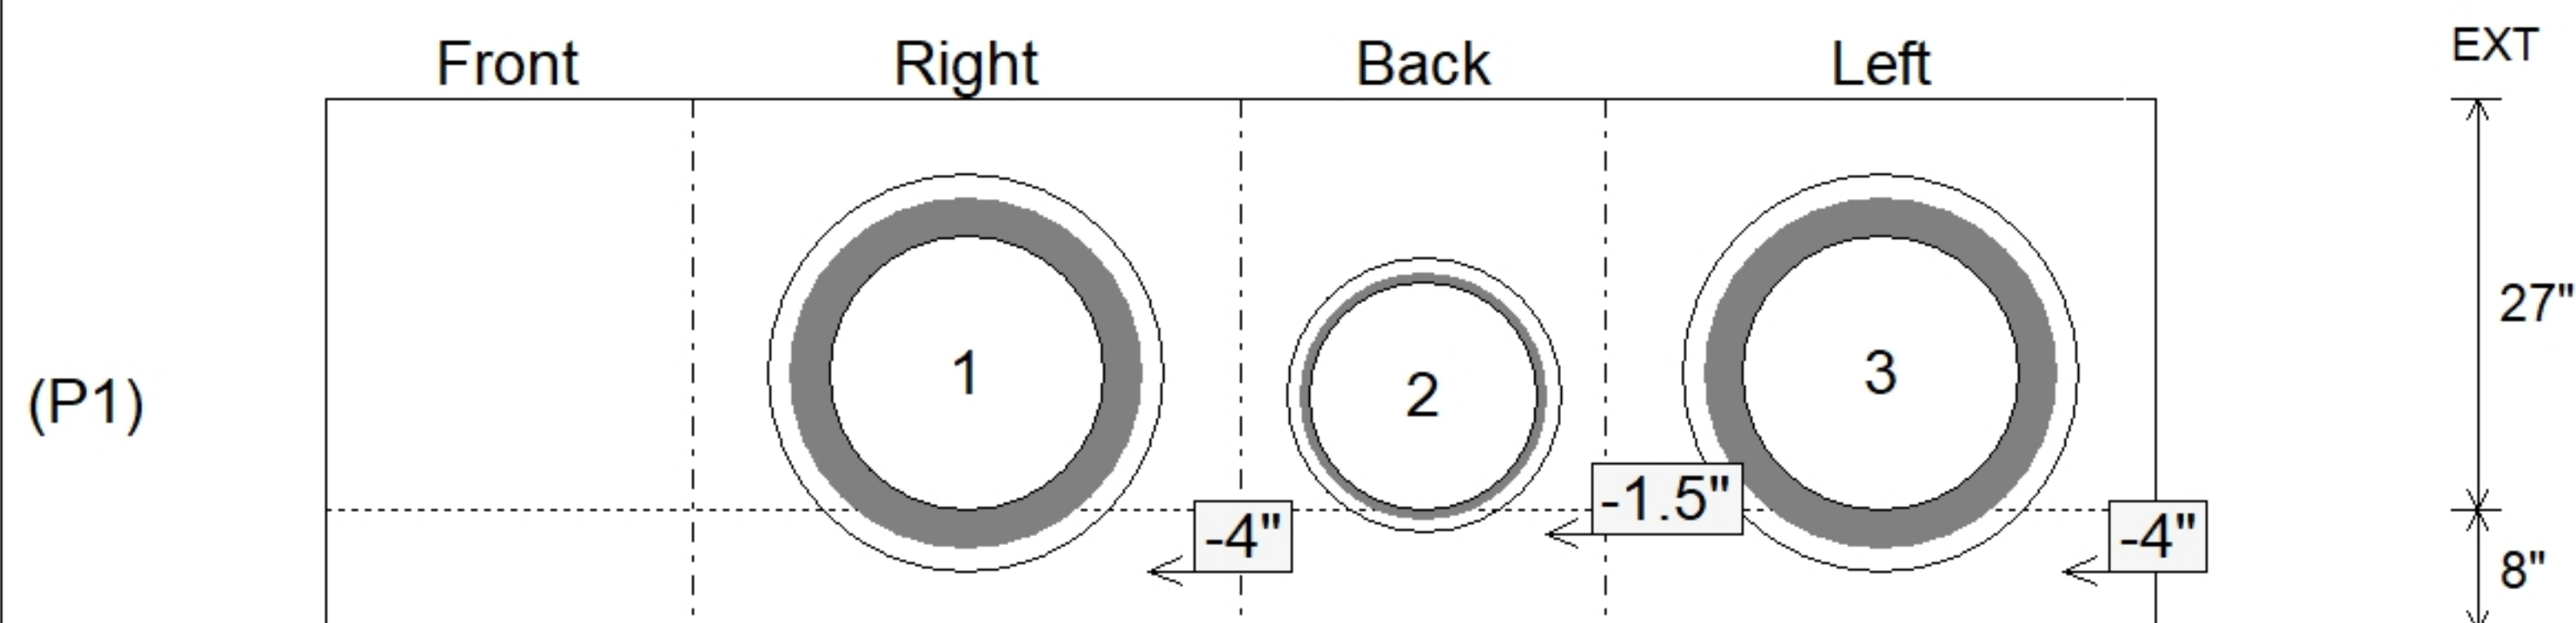

Submittal Drawing
8/18/2026 9:55:24 AM

SUBMITTAL
APPROVED BY:
