


Job Name: 25-1684P16 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.

8/25/2026 10:12:28 AM

Tech: N. Richards

PC: J. Jarvis



Structure ID: 16+47 CBBI-MOD B1

P1 BX4848-08BA48

BOX BASE 8inW, 8inF

P5) 24" x 120" - CASTING (cast in) - 3"
P4) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"
P3) 24" x 36" - BOX RISER 8inW, Variable Ht - 40"
P2) 48" x 48" - CB FT REDUCER 24"X36" HOLE-FT - 8"
P1) 48" x 48" - BOX BASE 8inW, 8inF - 48"
1) 48" x 48" - Conseal CS-102 1.00"
2) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 40

0 lb
4000 lb
4081 lb
2170 lb
8280 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 18531 lb




Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CASTING FRAMES & GRATES BY OTHERS.
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

Rim: 563.57' Rim to Invert: 9.8' Slack: 4.6" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	553.77'	0°	32"	36" CMP	37"	Hole 40	40"	40"	-2"	0"
Invert 2	553.77'	270°	32"	36" CMP	37"	Hole 40	40"	40"	-2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

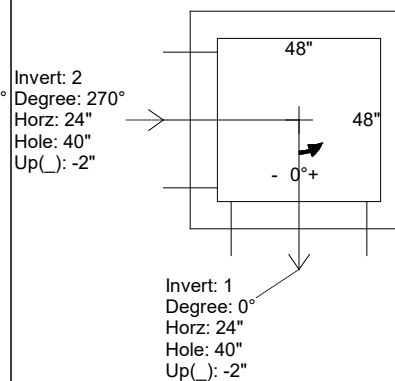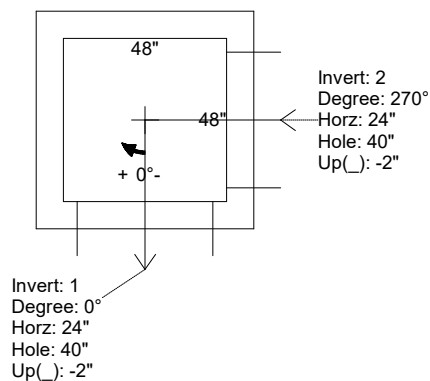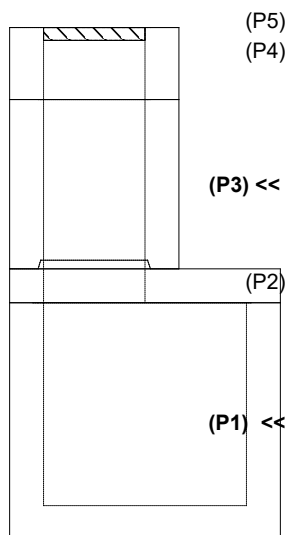

INSIDE WALL DIMENSIONS

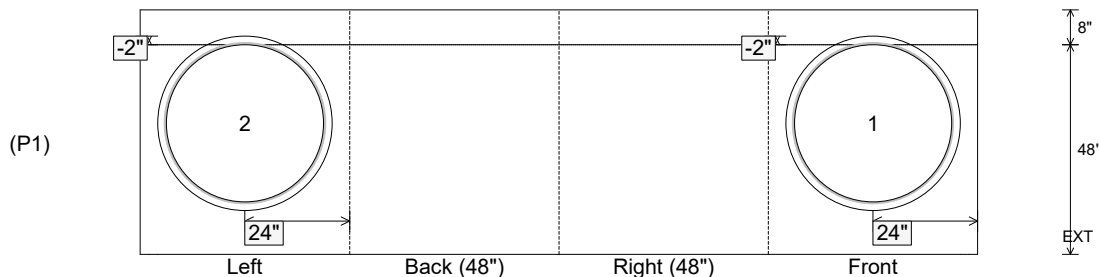

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 48"
Height (Ext): 56"

Weight (Net): 8280 lb
Volume (Net): 2.12cu.yd
