

Job Name: 25-1684P16 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.

8/25/2026 10:12:25 AM

Tech: N. Richards

PC: J. Jarvis



Structure ID: 5132+72 RT CBBI-MOD B1

P1 BX2436-08BA36

BOX BASE 8inW, 8inF

- P3) 24" x 120" - CASTING (cast in) - 3"
P2) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"
P1) 24" x 36" - BOX BASE 8inW, 8inF - 36"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 22"
1) Hole - 18"

Structure Total: 8388 lb

Structure Notes:



- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CASTING FRAMES & GRATES BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

Rim: 560.3' Rim to Invert: 4.75' Slack: 4" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	555.55'	90°	26"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 2	555.55'	180°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 3	555.55'	270°	26"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

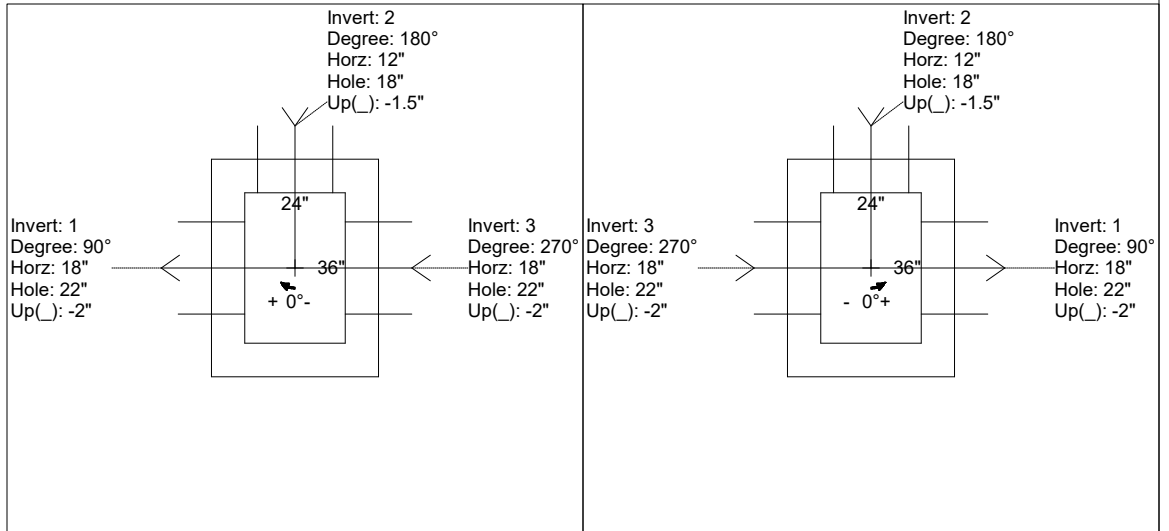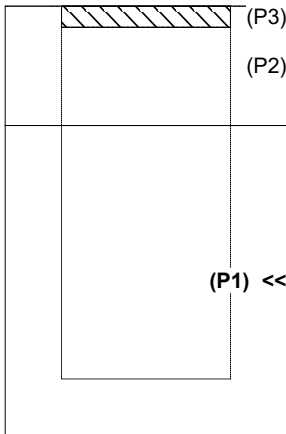

INSIDE WALL DIMENSIONS

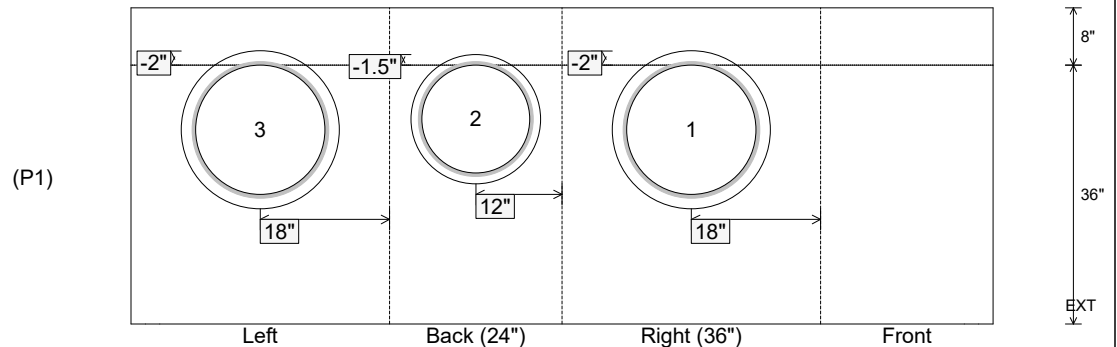

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 36"
Height (Ext): 44"

Weight (Net): 4388 lb
Volume (Net): 1.12cu.yd
