

Contractor: Cleary Construction, Inc.

PC: J. Jarvis

TECH: N. Richards

Plant: Beaver Dam, Ky.




Structure ID: 5132+72 RT CBBI-MOD B1			
Spec: KYTC	Rim: 560.3'	Sump: 0"	Floor (Bot): 554.883'
Type: MBI TYPE 9	Invert: 555.55'	Floor (Top): 555.55'	Overall Height: 5.083'
Size: 24" x 36"	Rim to Invert: 4.75'	Floor Height: 8"	Slack: 4"

Structure Notes:


- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CASTING FRAMES & GRATES BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.

STRUCTURE SUMMARY:	
P3) 24" x 120" - CASTING (cast in) - 3"	0 lb
P2) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"	4000 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF - 36"	4388 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
2) Hole - 22	0 lb
1) Hole - 18	0 lb


Structure Total:	8388 lb

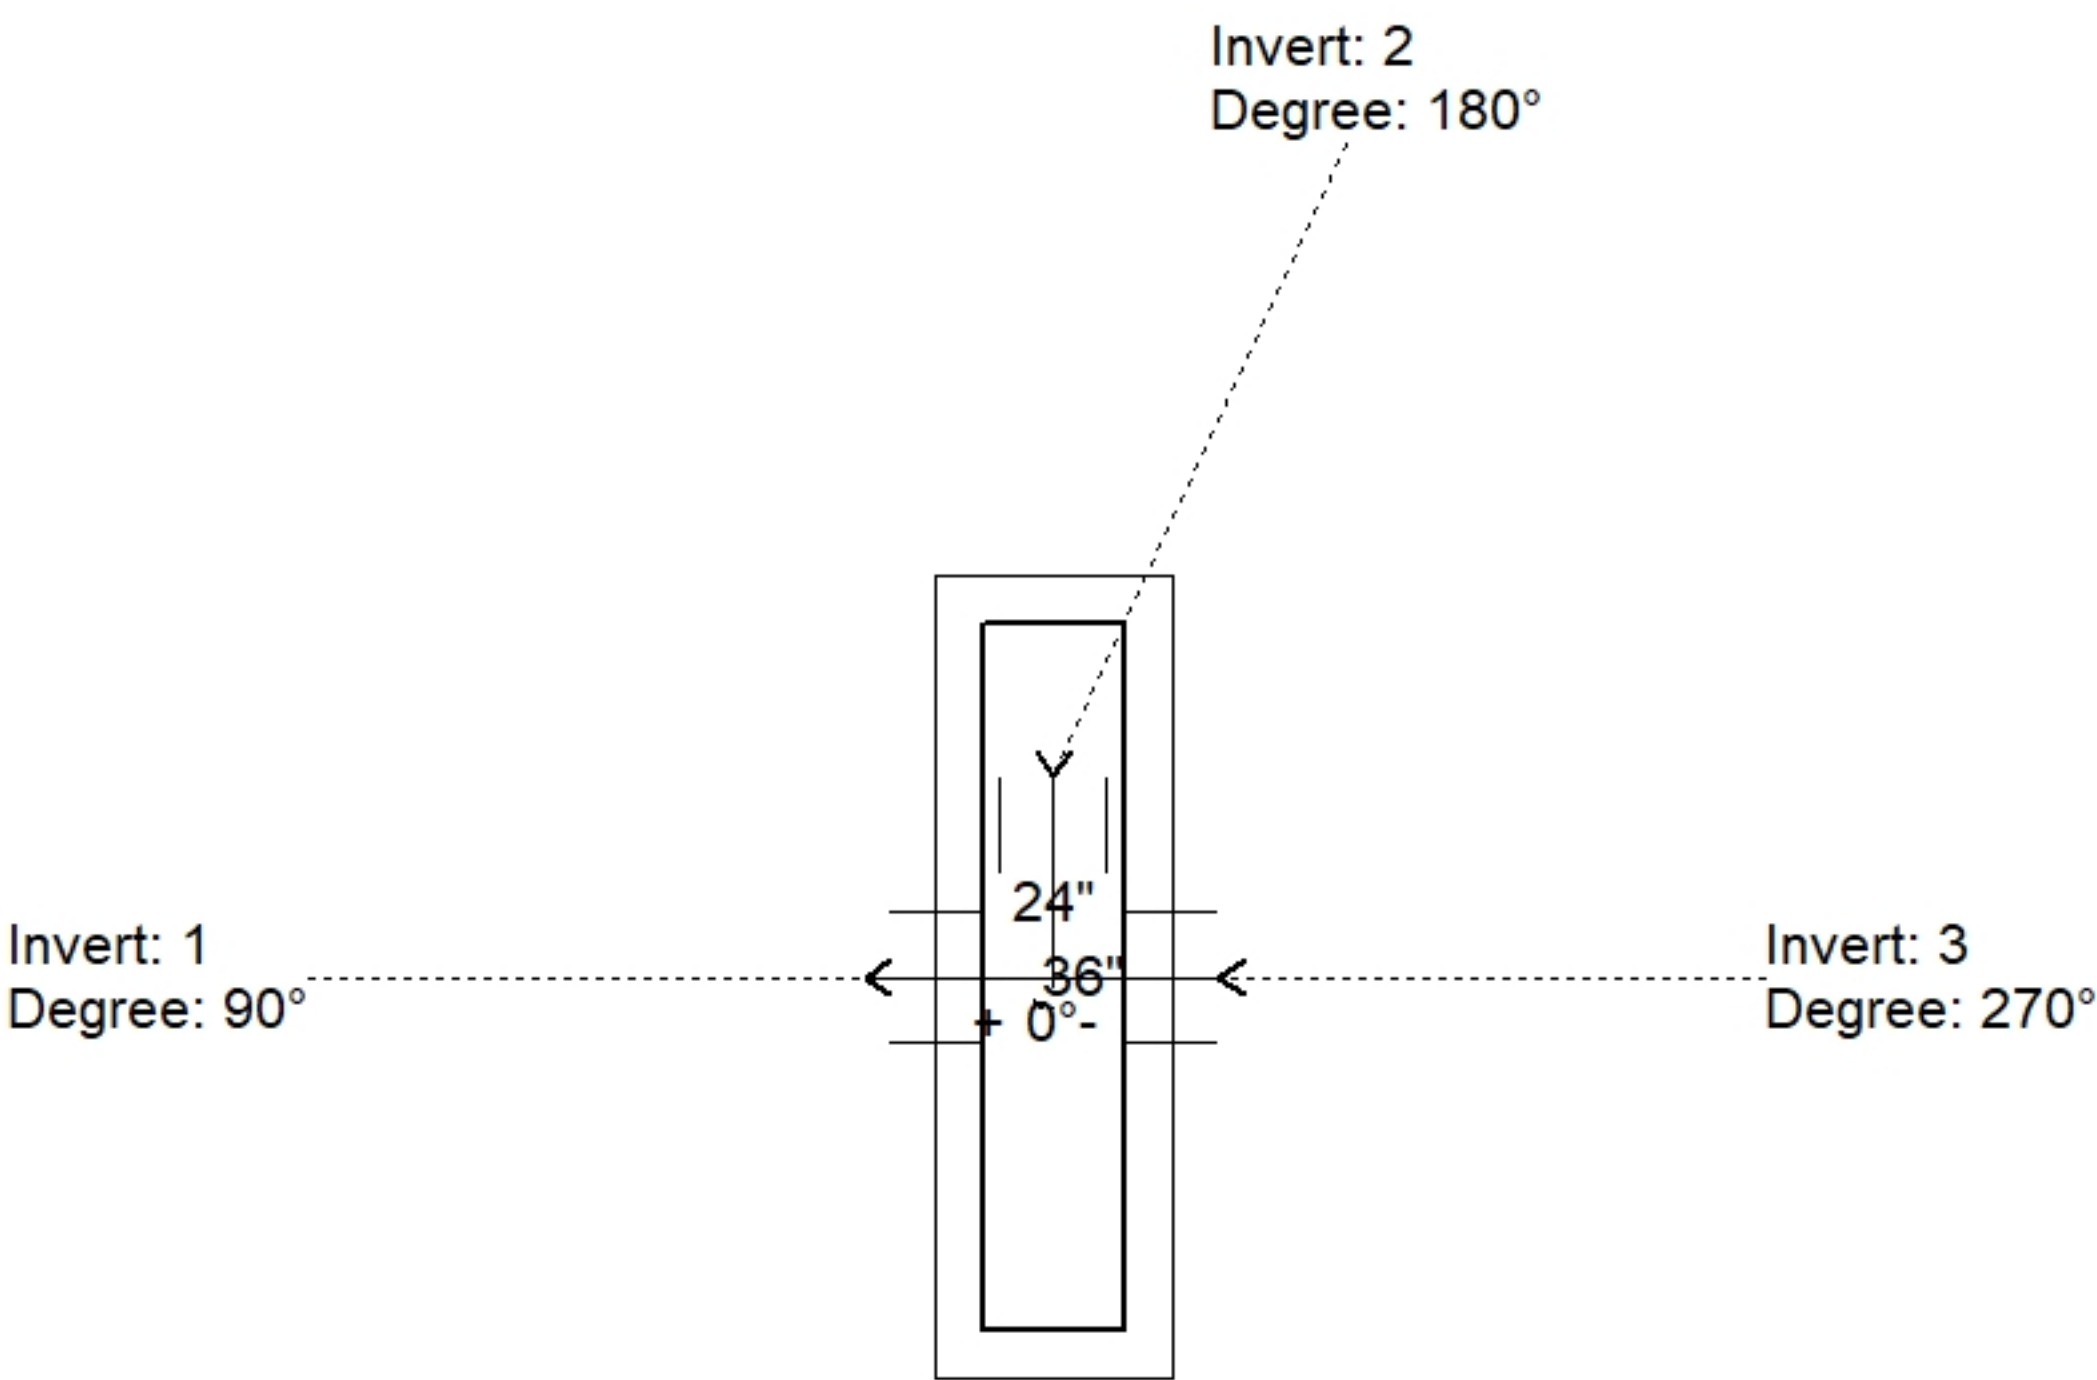

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	560.3'							
Reducer								
Invert 1	555.55'	90°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	555.55'	180°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 3	555.55'	270°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

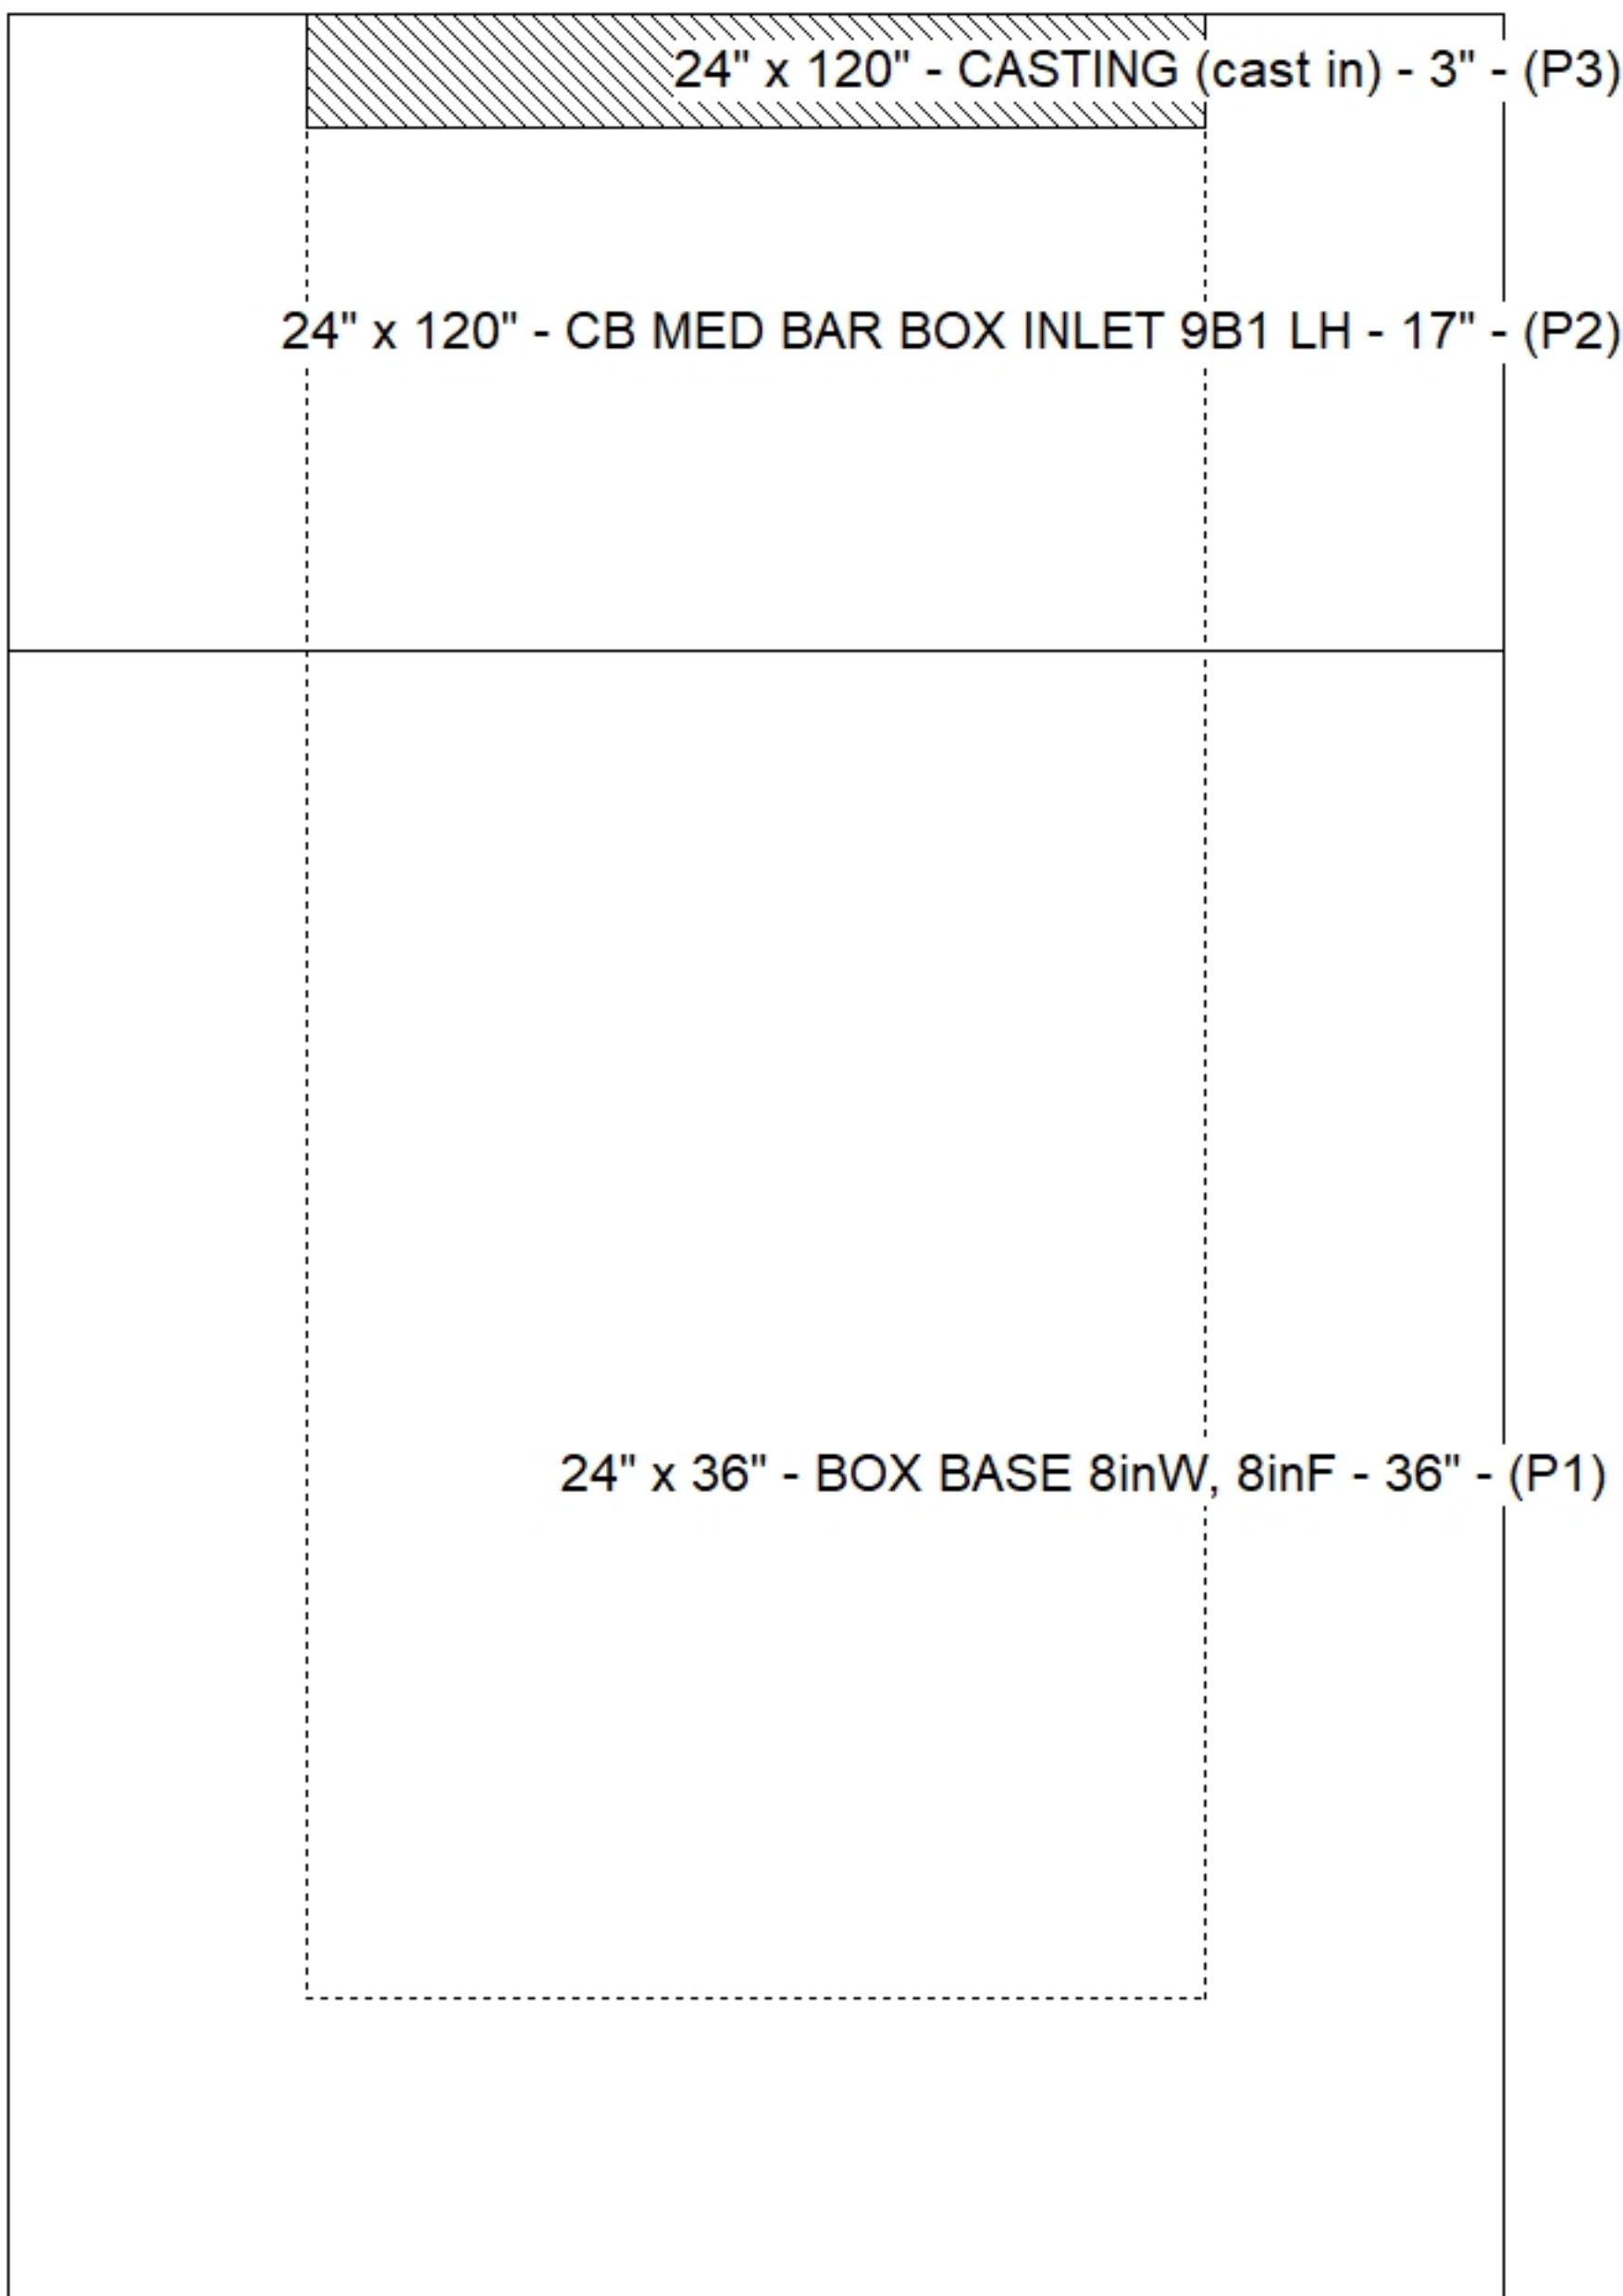

Default - Interior Dimensions

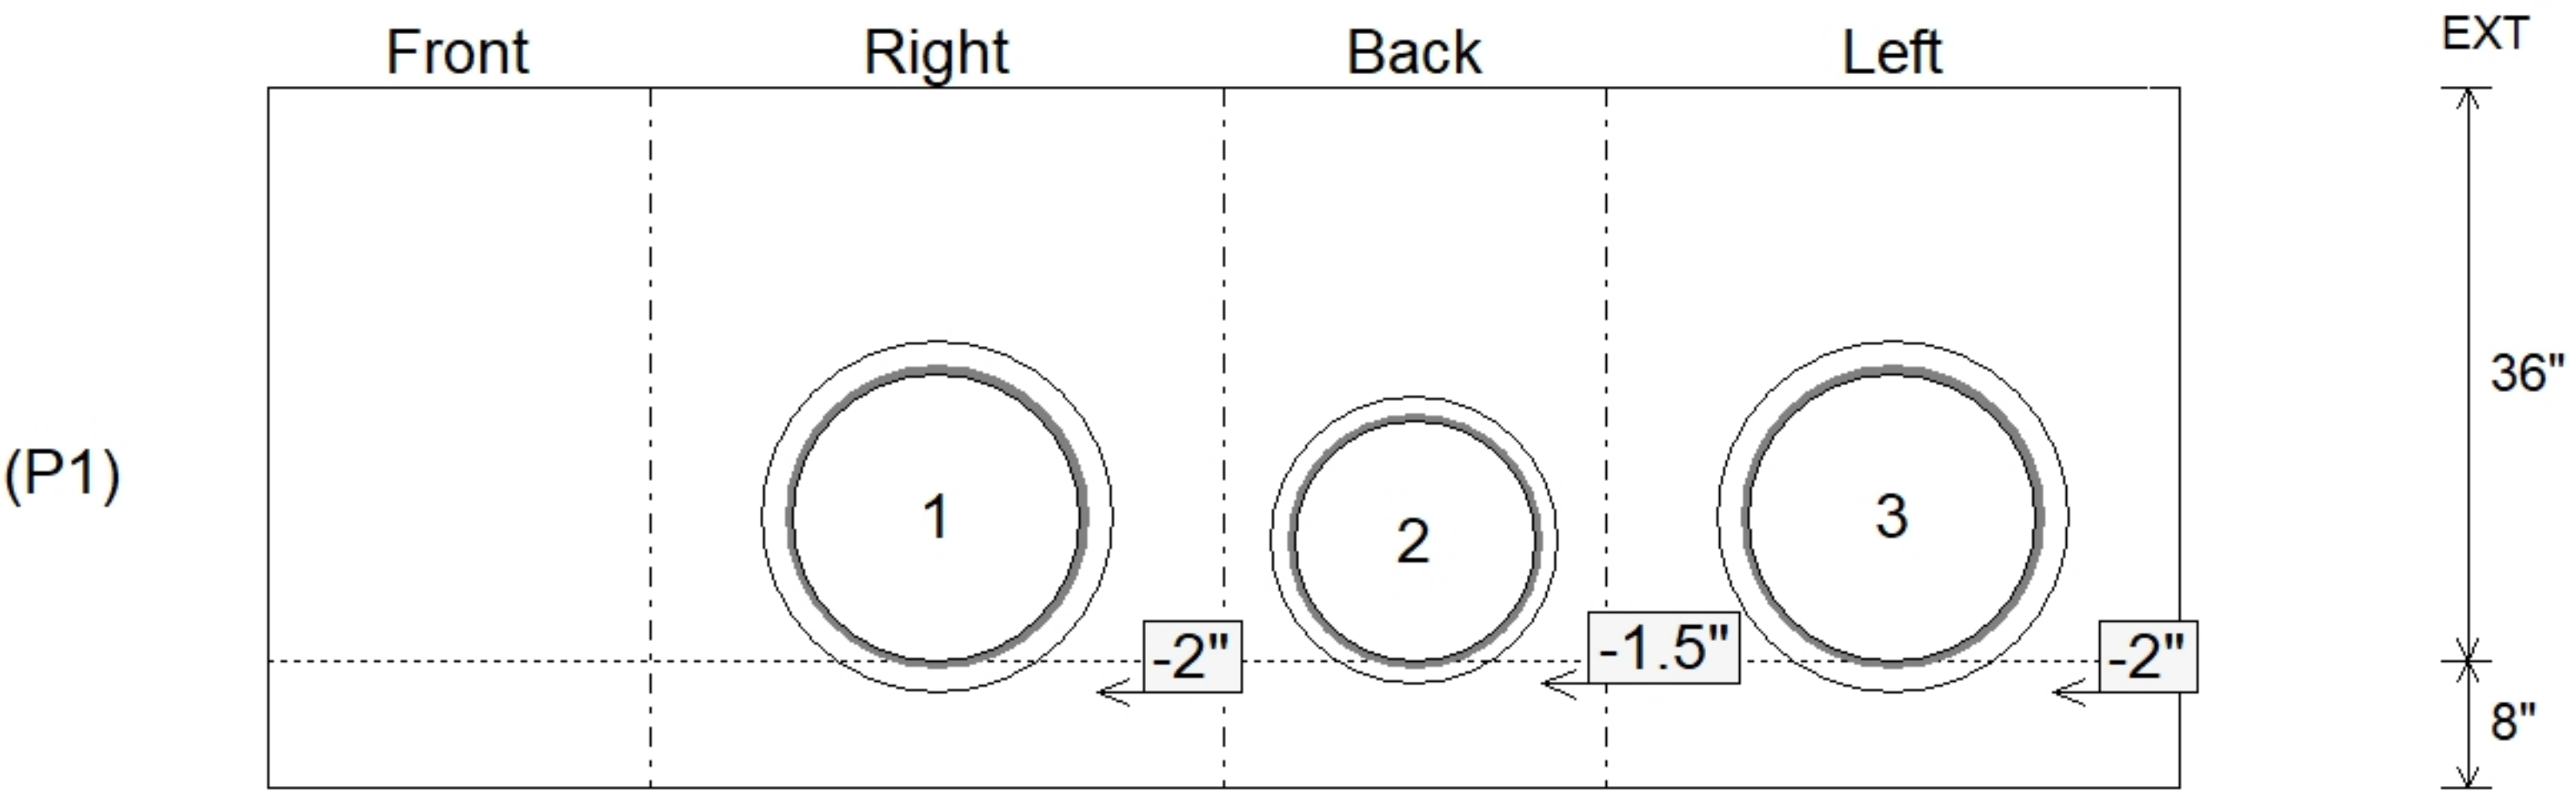

Submittal Drawing
8/26/2026 3:21:50 PM

SUBMITTAL
APPROVED BY:
