

Job Name: 25-1684 KYTC Jefferson Co. Call 200 (251007)  
 Job Location: I-264 Louisville, Ky.  
 Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.  
 7/11/2025 9:25:09 AM

Tech: N. Richards  
 PC: T. Ryan



**Structure ID: 5130+98 RT DBI TYPE 1-NA**

**P1 BX3636-08BAVF**

**BOX BASE 8inW, 8inF, Variable Ht**

- P3) 36" x 36" - P.I.P. - BY OTHERS - 8"
- P2) 36" x 36" - BX3636-08R30 - BOX RISER 8inW - 30"
- P1) 36" x 36" - BX3636-08BAVF - BOX BASE 8inW, 8inF, Variable Ht - 46"
- 2) 36" x 36" - PSCONCS102-1 - SGL 1"x14.5' Butyl - 0"
- 1) Hole - 0"




Structure Notes:  
 -KYTC STATE PROJECT 251007  
 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)  
 -TOP SLAB WITH FRAME & GRATES BY OTHERS (NO APRON).  
 -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).  
 -KYTC CERTIFICATIONS REQUIRED.

Rim: 563.57' Rim to Invert: 7.1' Slack: 1.2" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (↓)	Offset
Invert 1	566.47'	0°	26"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

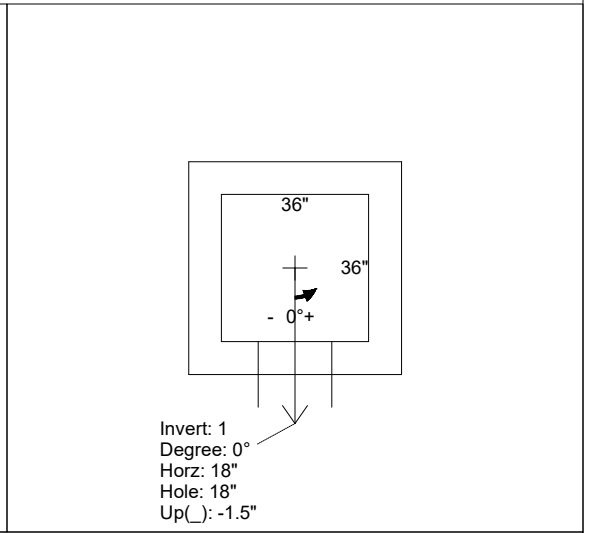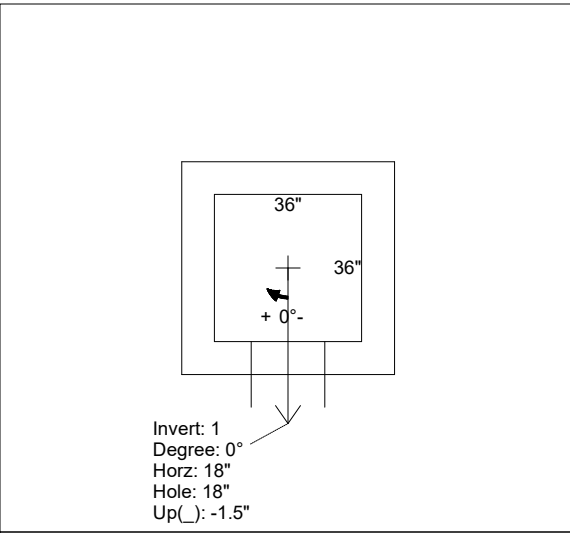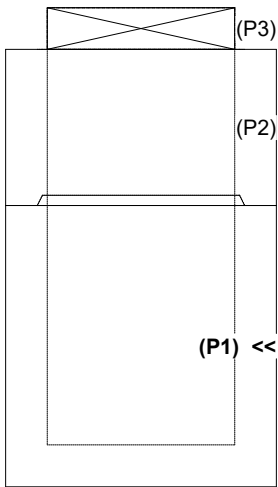

INSIDE WALL DIMENSIONS

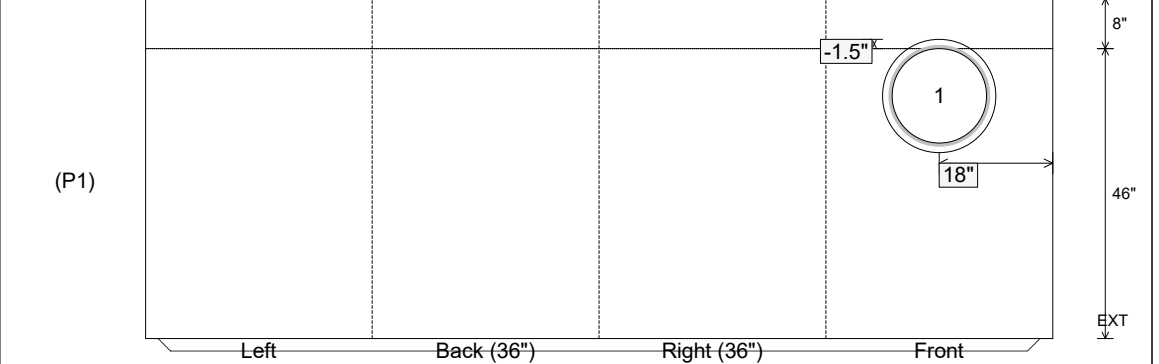

Coating (Int):  
 Coating (Ext):

Seam Up: Tongue  
 Seam Dn: n/a

Wall Thickness: 8"  
 Floor Height: 8"

Height (Int): 46"  
 Height (Ext): 54"

Weight (Net): 7079 lb  
 Volume (Net): 1.81cu.yd
