

Job Name: 25-1684 KYTC Jefferson Co. Call 200 (251007)  
 Job Location: I-264 Louisville, Ky.  
 Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.  
 7/11/2025 10:27:12 AM

Tech: N. Richards  
 PC: T. Ryan



**Structure ID: 5132+72 RT DBI TYPE 1-NA**

**P2 BX3636-08R30**

**BOX RISER 8inW**



- P3) 36" x 36" - P.I.P. - BY OTHERS - 8"
- P2) 36" x 36" - BX3636-08R30 - BOX RISER 8inW - 30"
- P1) 36" x 36" - BX3636-08BAVF - BOX BASE 8inW, 8inF, Variable Ht - 46"
- 2) 36" x 36" - PSCONCS102-1 - SGL 1"x14.5' Butyl - 0"
- 1) Hole - 0"

Structure Notes:  
 -KYTC STATE PROJECT 251007  
 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)  
 -TOP SLAB WITH FRAME & GRATES BY OTHERS (NO APRON).  
 -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).  
 -KYTC CERTIFICATIONS REQUIRED.  
 -#5 BAR EXTENDED OUT OF TOP OF RISER 20" AT 12" C/C.


Rim: 562.8' Rim to Invert: 7' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (L)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

**RIGHT-SIDE UP VIEW (int. dimensions)**

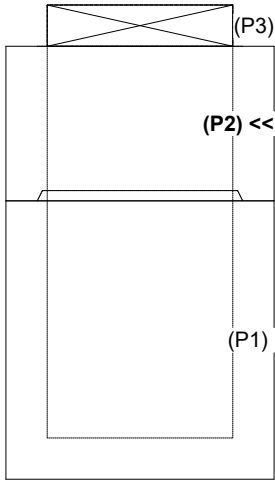

**INSIDE WALL DIMENSIONS**



Coating (Int):  
 Coating (Ext):

Seam Up: Flat  
 Seam Dn: Groove

Wall Thickness: 8"  
 Floor Height: 0"

Height (Int): 30"  
 Height (Ext): 30"

Weight (Net): 3544 lb  
 Volume (Net): 0.9cu.yd
