

Job Name: 25-1684 KYTC Jefferson Co. Call 200 (251007)
 Job Location: I-264 Louisville, Ky.
 Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.
 7/11/2025 10:48:30 AM

Tech: N. Richards
 PC: T. Ryan



Structure ID: 5134+09 RT DBI TYPE 1-NA

P2 BX3636-08R30

BOX RISER 8inW



- P3) 36" x 36" - P.I.P. - BY OTHERS - 8"
- P2) 36" x 36" - BX3636-08R30 - BOX RISER 8inW - 30"
- P1) 36" x 36" - BX3636-08BAVF - BOX BASE 8inW, 8inF, Variable Ht - 46"
- 2) 36" x 36" - PSCONCS102-1 - SGL 1"x14.5' Butyl - 0"
- 1) Hole - 0"

Structure Notes:
 -KYTC STATE PROJECT 251007
 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
 -TOP SLAB WITH FRAME & GRATES BY OTHERS (NO APRON).
 -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
 -KYTC CERTIFICATIONS REQUIRED.
 -#5 BAR EXTENDED OUT OF TOP OF RISER 20" AT 12" C/C.


Rim: 562.1' Rim to Invert: 7.1' Slack: 1.2" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (L)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

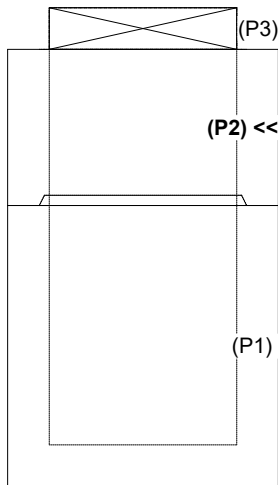

INSIDE WALL DIMENSIONS



Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: Groove

Wall Thickness: 8"
 Floor Height: 0"

Height (Int): 30"
 Height (Ext): 30"

Weight (Net): 3544 lb
 Volume (Net): 0.9cu.yd
