

**Job Name: 25-1684P2 KYTC Jefferson Co. Call 200 (251007)**  
**Job Location: I-264 Louisville, Ky.**  
**Contractor: Cleary Construction, Inc.**

PC: J. Jarvis  
 TECH: N. Richards  
 Plant: Beaver Dam, Ky.



Structure ID: 5136+37 RT DBI TYPE 1-NA


Spec: KYTC Rim: 560.97' Sump: 0" Floor (Bot): 553.203'  
 Type: DBI TYPE 1 Invert: 553.87' Floor (Top): 553.87' Overall Height: 7.667'  
 Size: 36" x 36" Rim to Invert: 7.1' Floor Height: 8" Slack: 1.2"

**Structure Notes:**


- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- TOP SLAB WITH FRAME & GRATES BY OTHERS (NO APRON).
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.
- #5 BAR EXTENDED OUT OF TOP OF RISER 20" AT 12" C/C.

**STRUCTURE SUMMARY:**


P3) 36" x 36" - P.I.P. - BY OTHERS - 8"	0 lb
P2) 36" x 36" - BOX RISER 8inW - 30"	3544 lb
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 46"	7079 lb
1) 36" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 18	0 lb
<b>Structure Total:</b>	<b>10624 lb</b>

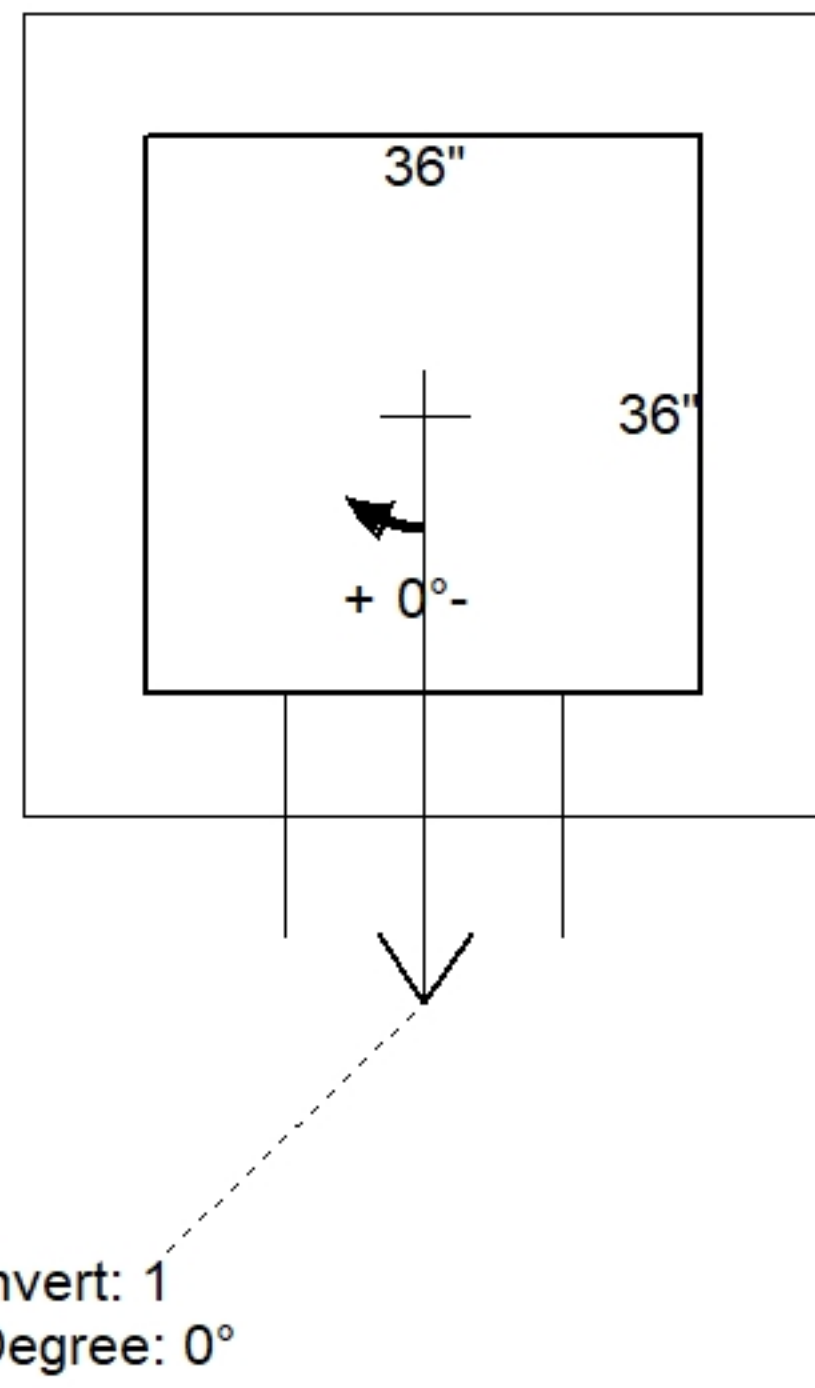

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (L)	Ref
Rim	560.97'							
Reducer								
Invert 1	553.87'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

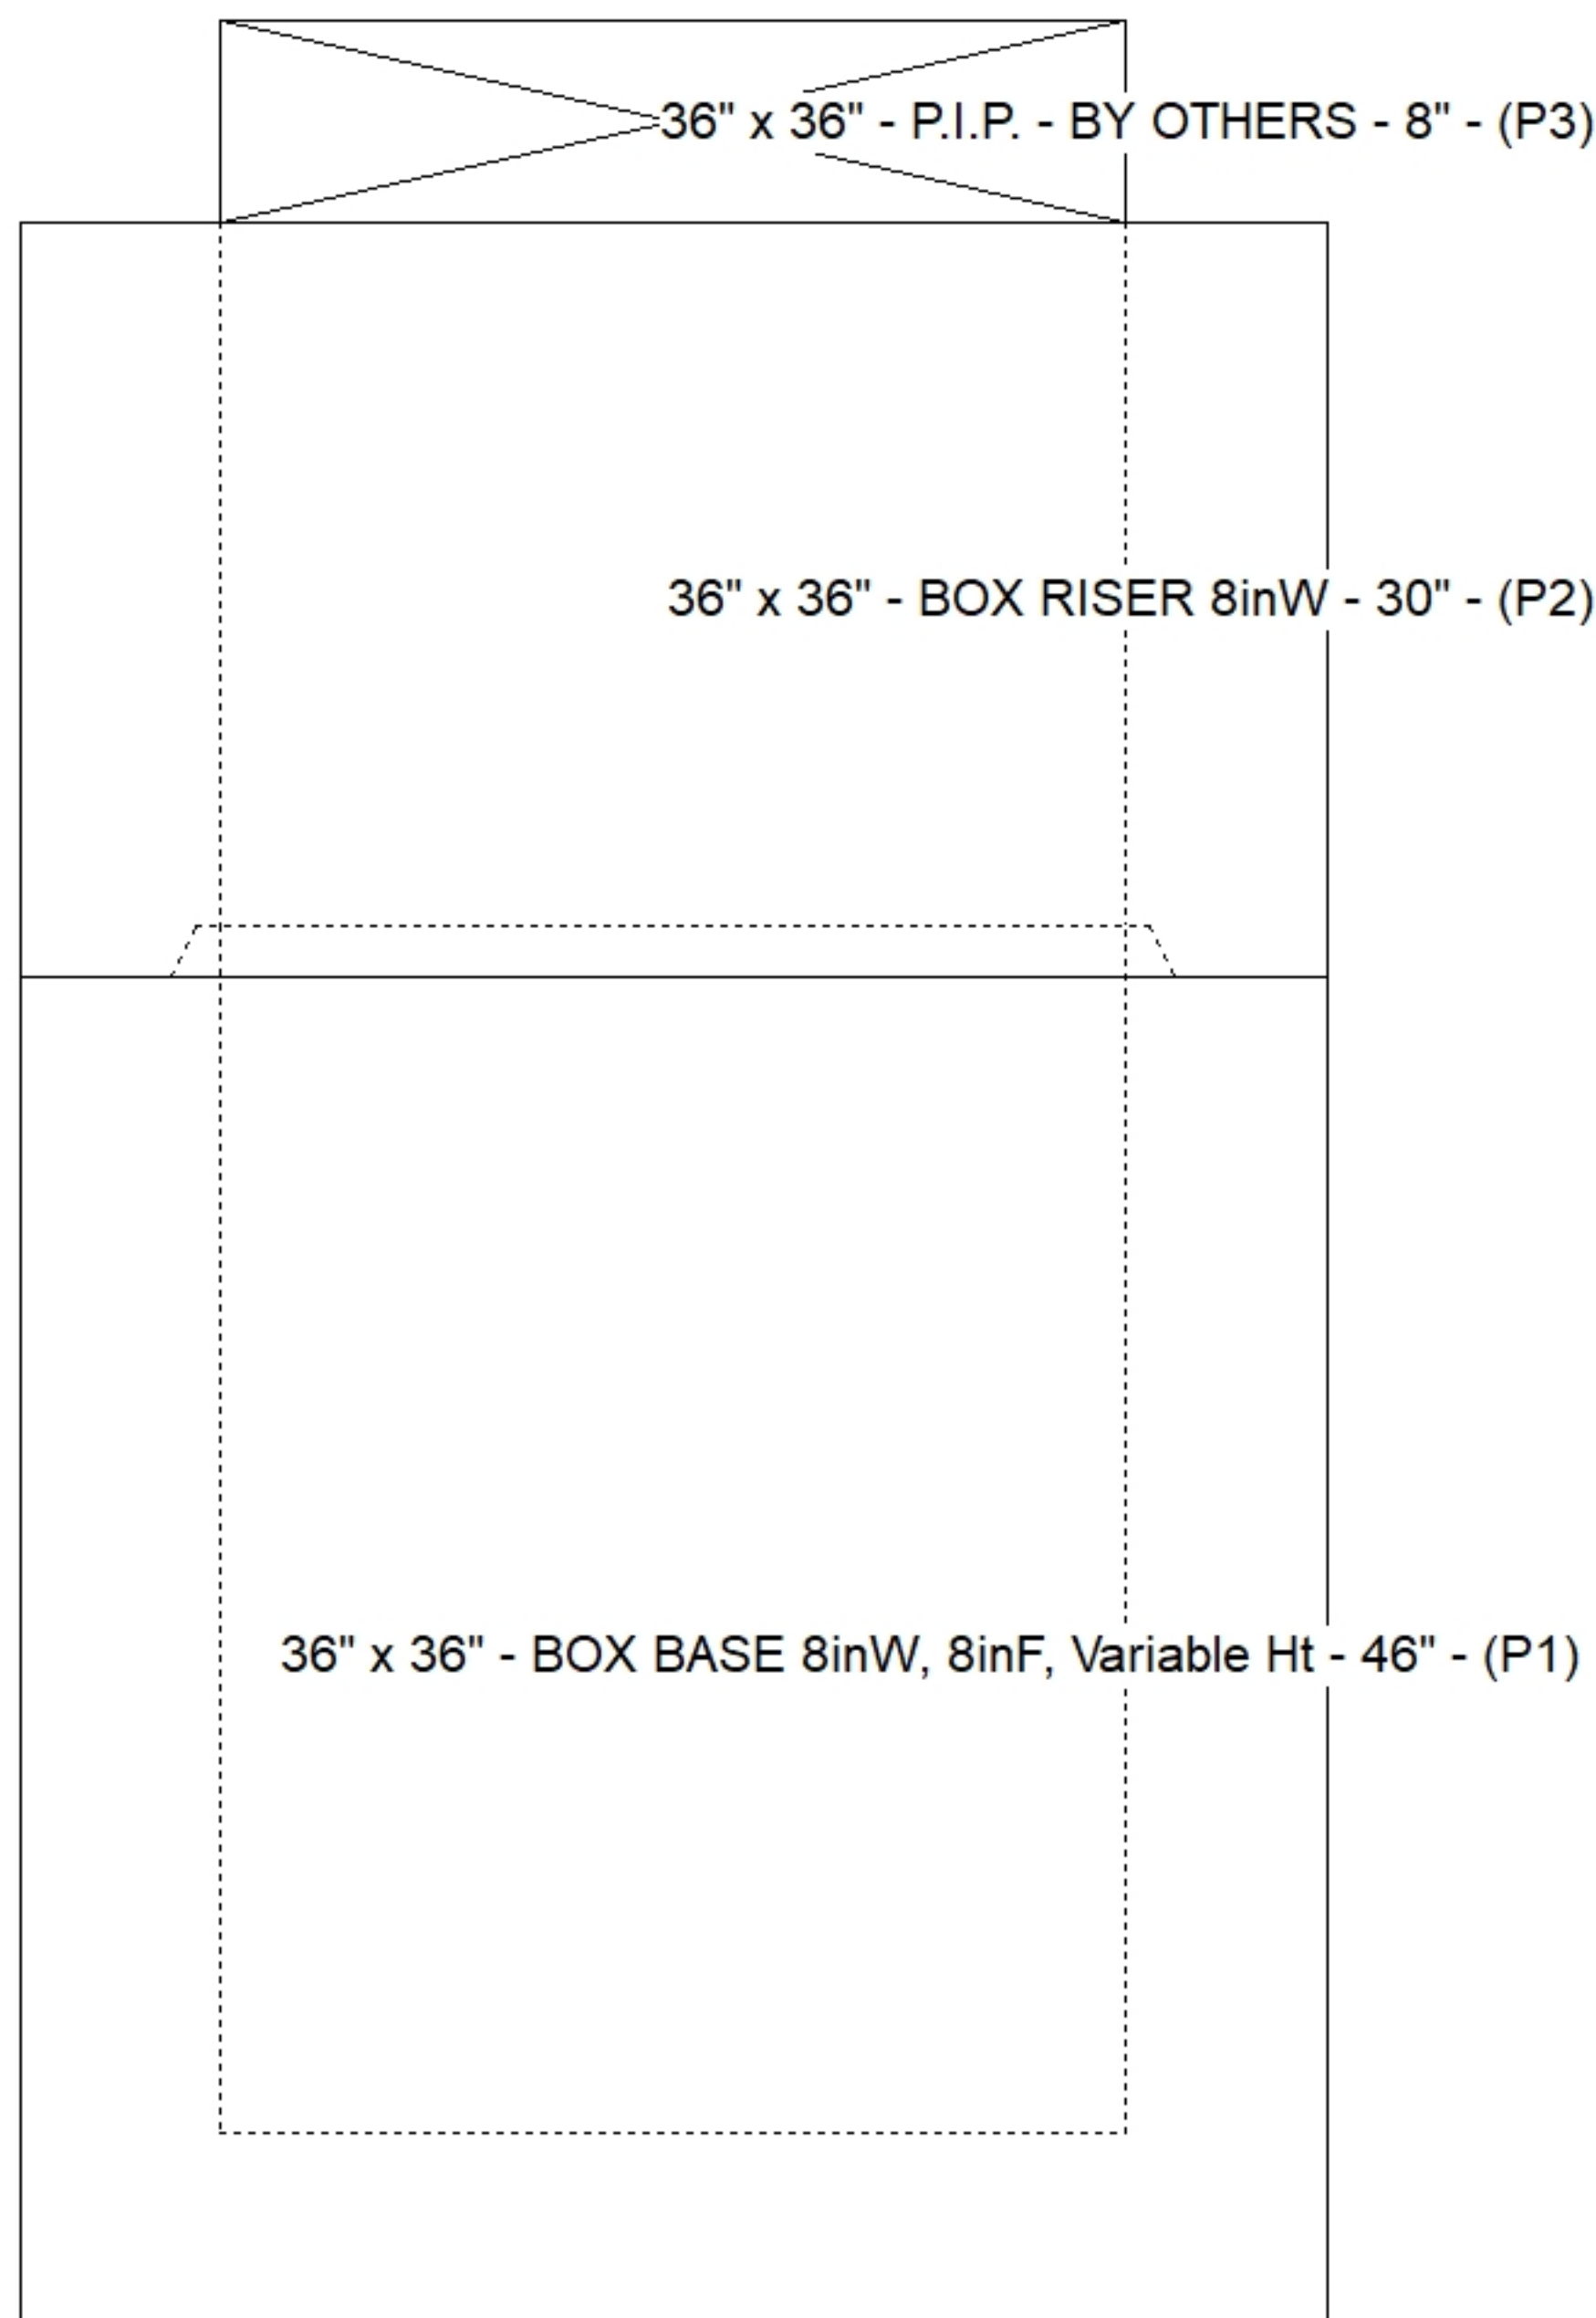

**Default - Interior Dimensions**

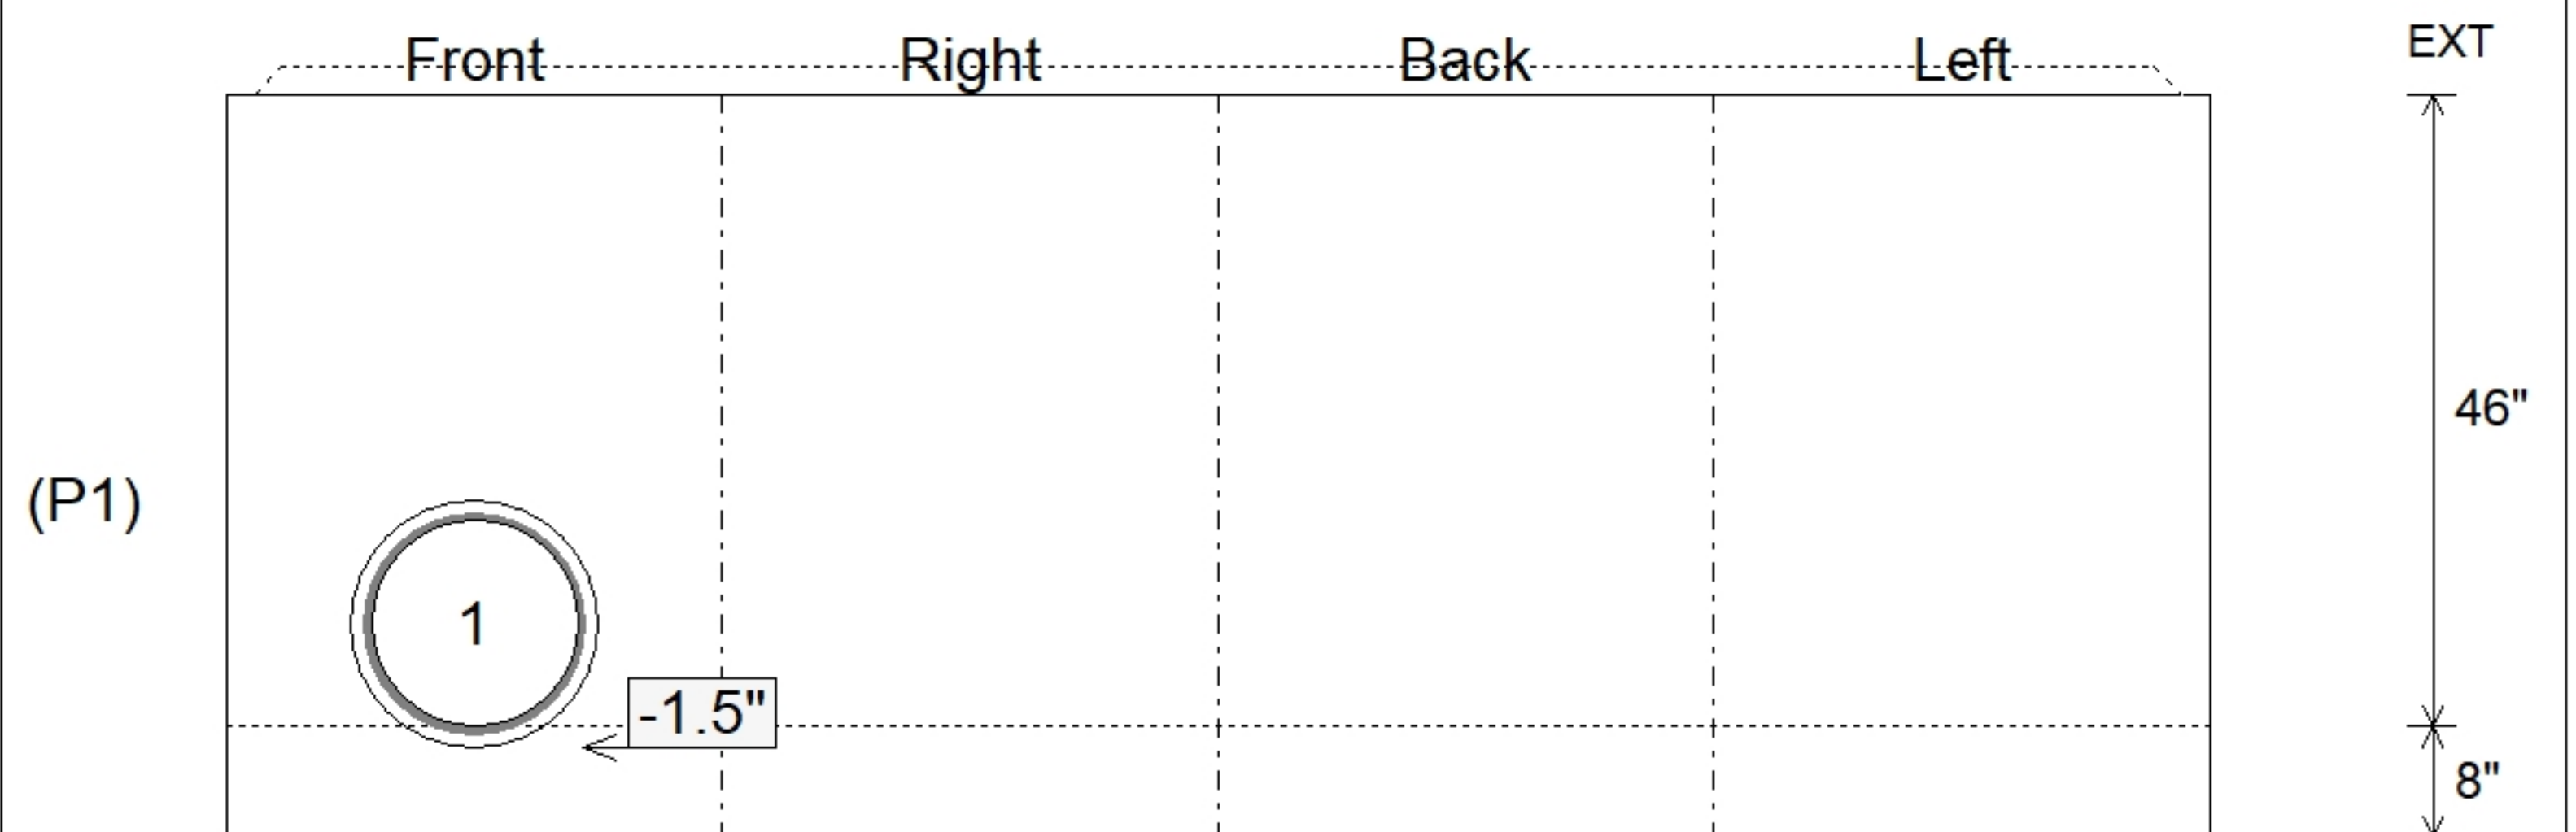

Submittal Drawing  
 12/17/2025 9:35:08 AM

SUBMITTAL  
 APPROVED BY:
