

Job Name: 25-1684P2 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

PC: J. Jarvis
 TECH: N. Richards
 Plant: Beaver Dam, Ky.



Structure ID: 5141+50 RT CBBI-MOD B1

Spec: KYTC Rim: 556.26' Sump: 0" Floor (Bot): 545.593'
 Type: MBI TYPE 9 Invert: 546.26' Floor (Top): 546.26' Overall Height: 10.333'
 Size: 24" x 36" Rim to Invert: 10' Floor Height: 8" Slack: 4"

Structure Notes:

- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CASTING FRAMES & GRATES BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
- KYTC CERTIFICATIONS REQUIRED.


STRUCTURE SUMMARY:

P4) 24" x 120" - CASTING (cast in) - 3"	0 lb
P3) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"	4000 lb
P2) 24" x 36" - BOX RISER 8inW, Variable Ht - 39"	3979 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF - 60"	7277 lb
2) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 18	0 lb
Structure Total:	15256 lb


Invert: 1
 Degree: 135°



Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (L)	Ref
Rim	556.26'							
Reducer								
Invert 1	546.26'	135°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

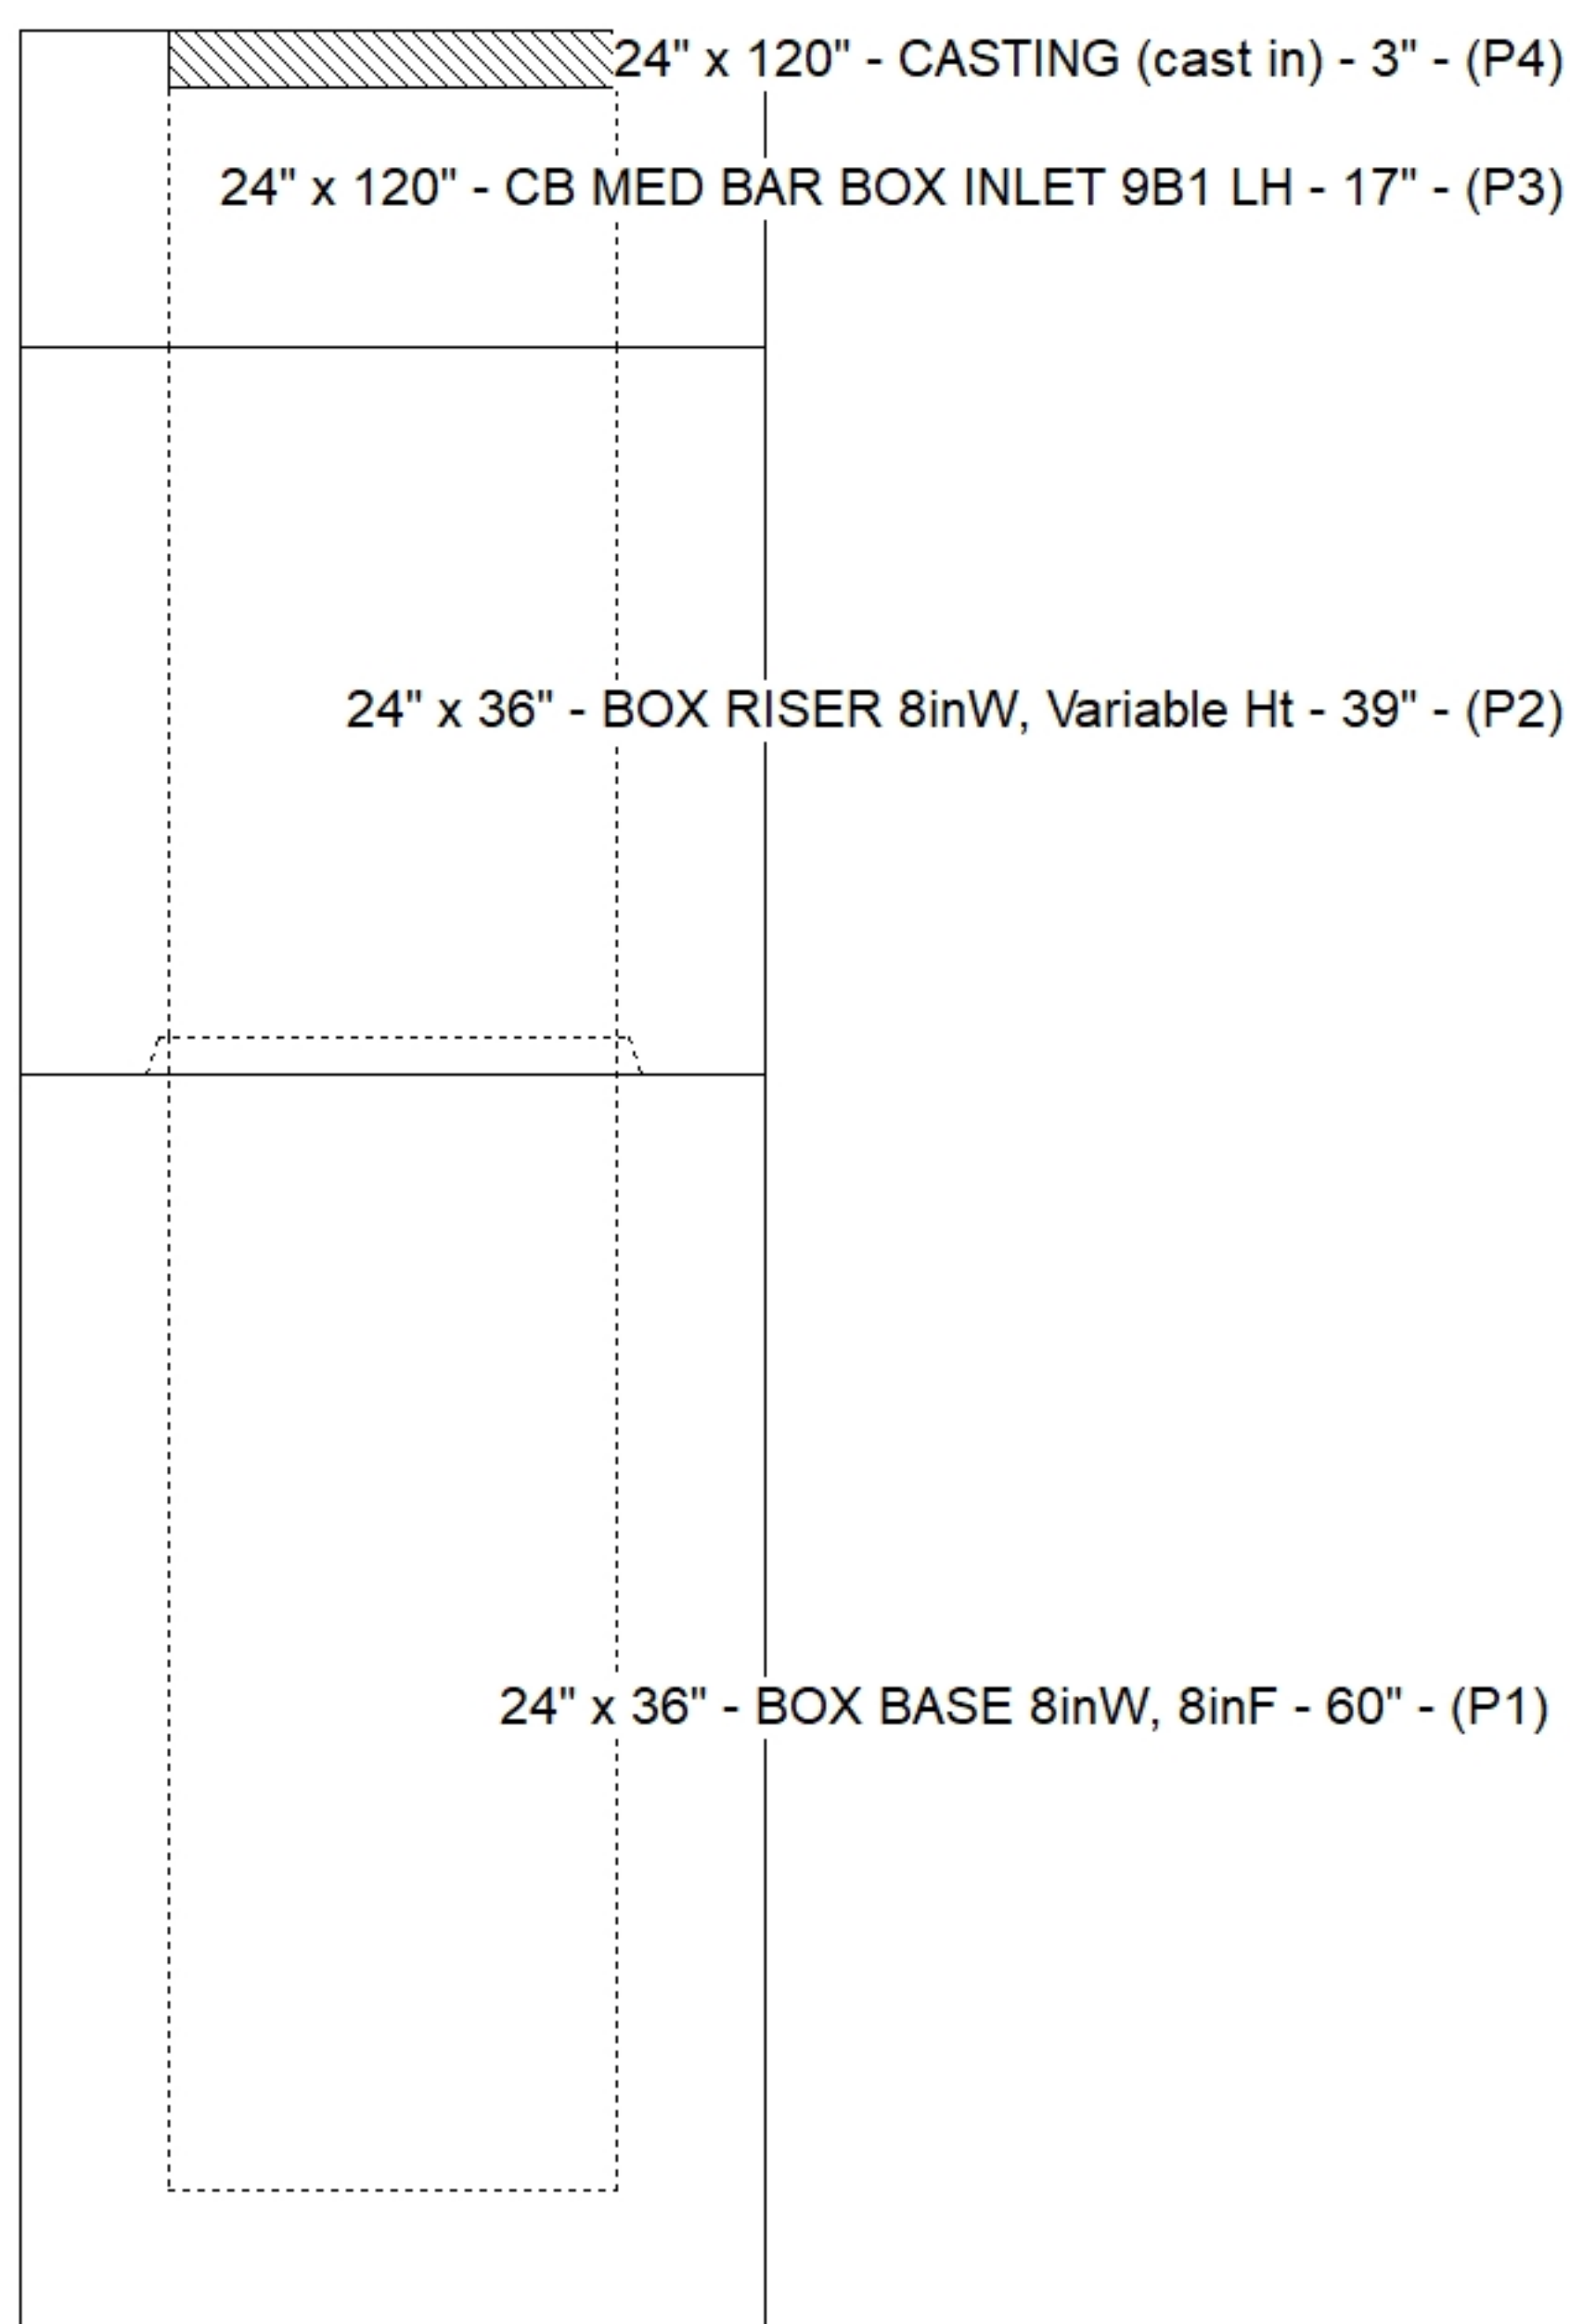

Default - Interior Dimensions

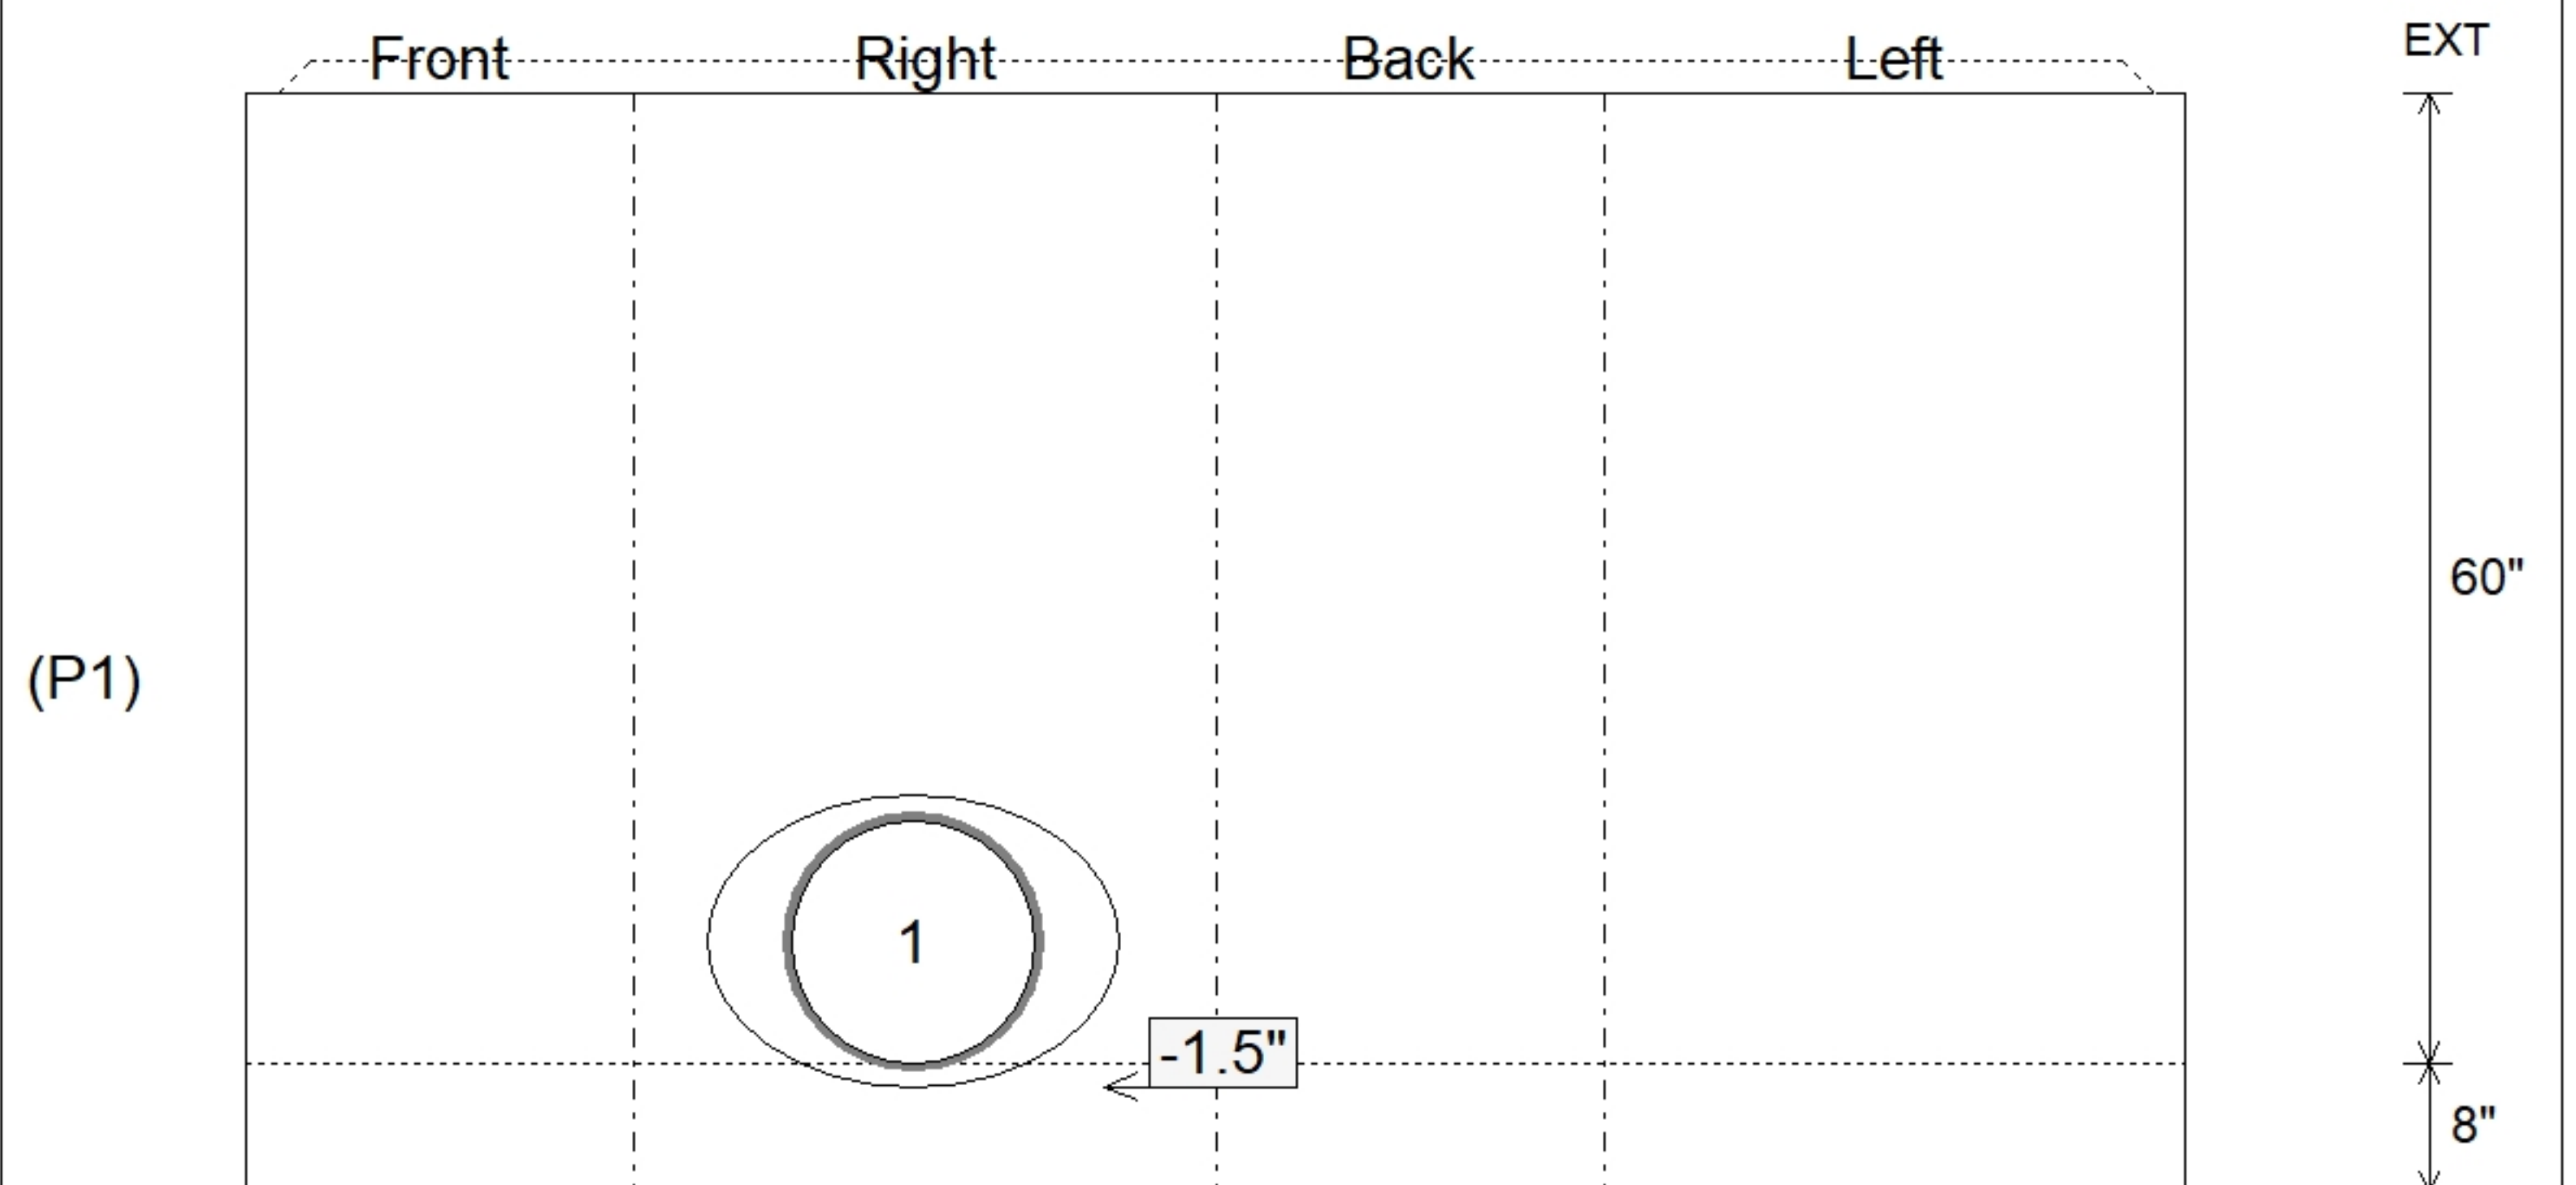

Submittal Drawing
 12/17/2025 9:35:06 AM

SUBMITTAL
 APPROVED BY:
