

**Job Name: 25-1684P2 KYTC Jefferson Co. Call 200 (251007)**  
**Job Location: I-264 Louisville, Ky.**  
**Contractor: Cleary Construction, Inc.**

PC: J. Jarvis  
 TECH: N. Richards  
 Plant: Beaver Dam, Ky.




Structure ID: 5143+04 RT CBBI-MOD B1  
 Spec: KYTC Rim: 555.06' Sump: 0" Floor (Bot): 550.493'  
 Type: MBI TYPE 9 Invert: 551.16' Floor (Top): 551.16' Overall Height: 4.25'  
 Size: 24" x 36" Rim to Invert: 3.9' Floor Height: 8" Slack: 3.8"


**Structure Notes:**  
 -KYTC STATE PROJECT 251007  
 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)  
 -CASTING FRAMES & GRATES BY OTHERS.  
 -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).  
 -KYTC CERTIFICATIONS REQUIRED.

**STRUCTURE SUMMARY:**


P3) 24" x 120" - CASTING (cast in) - 3"	0 lb
P2) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"	4000 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26"	3878 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 18	0 lb
<b>Structure Total:</b>	<b>7878 lb</b>

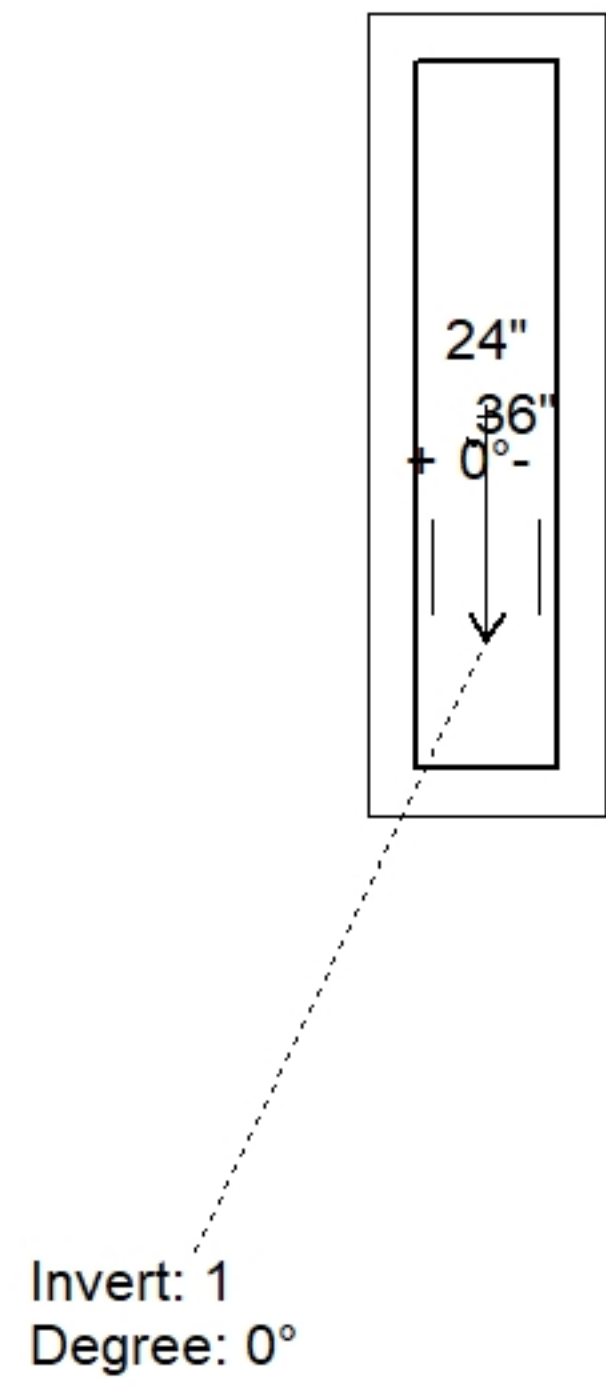

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (L)	Ref
Rim	555.06'							
Reducer								
Invert 1	551.16'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

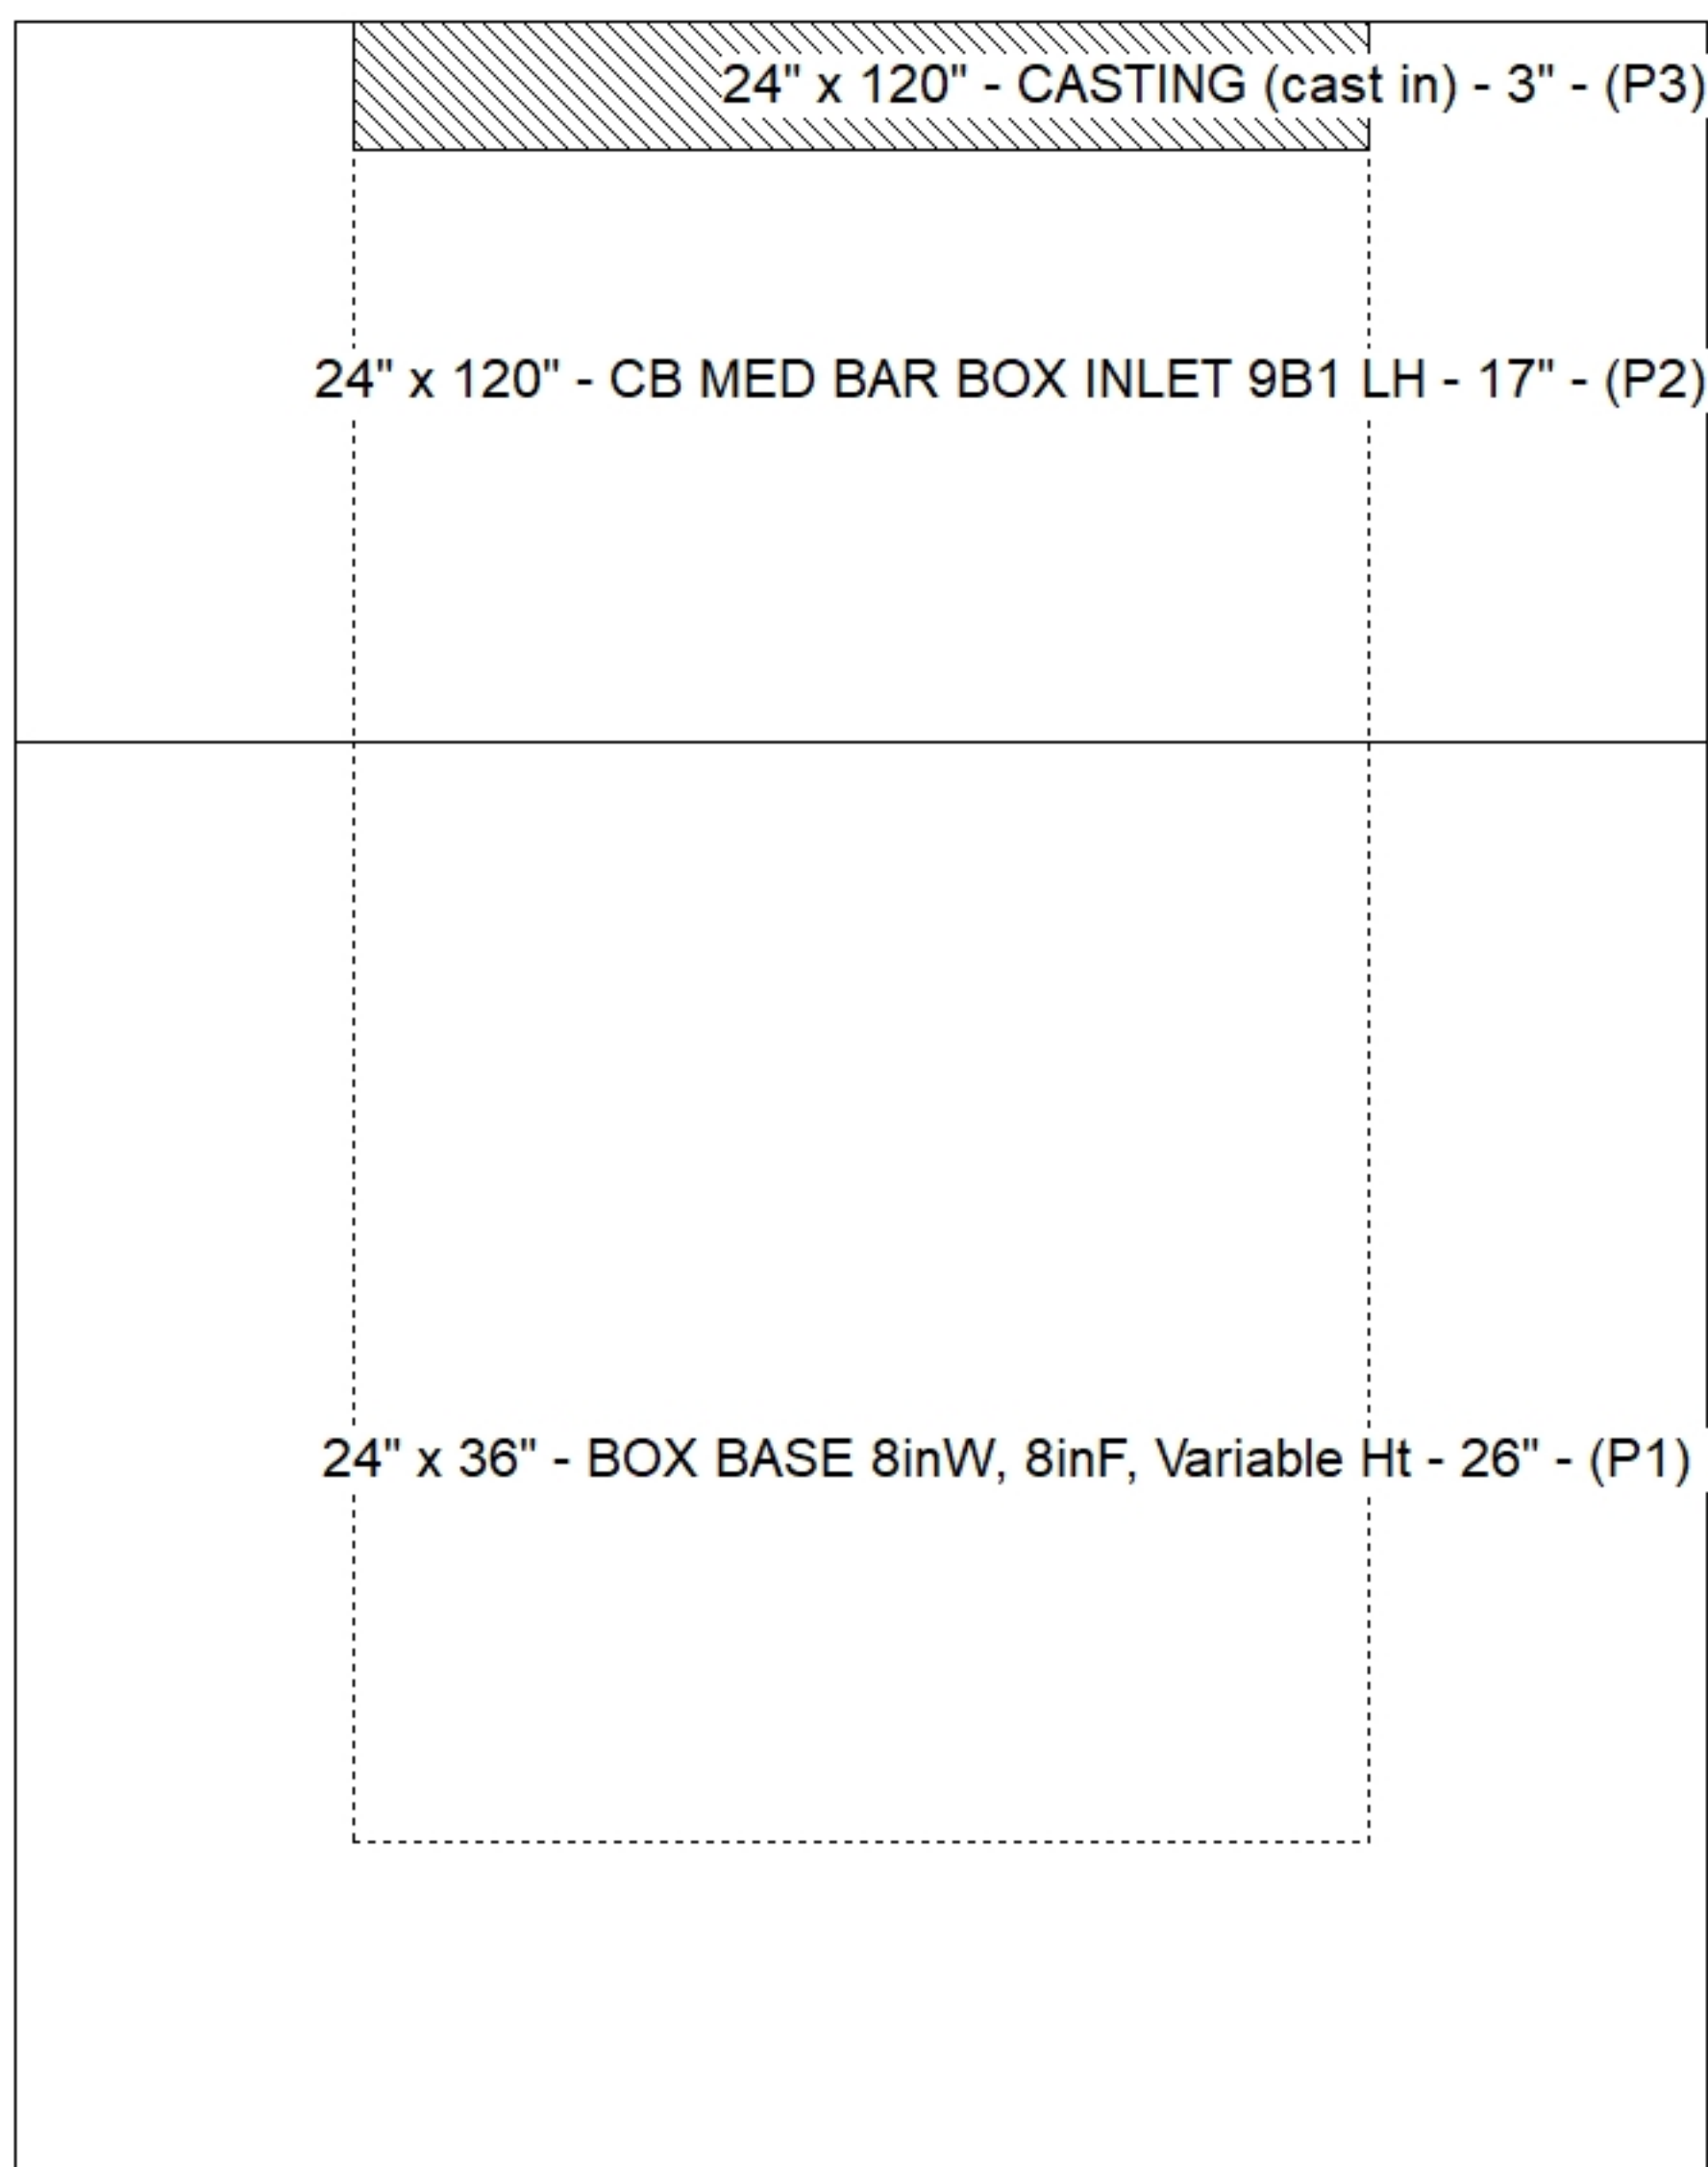

**Default - Interior Dimensions**

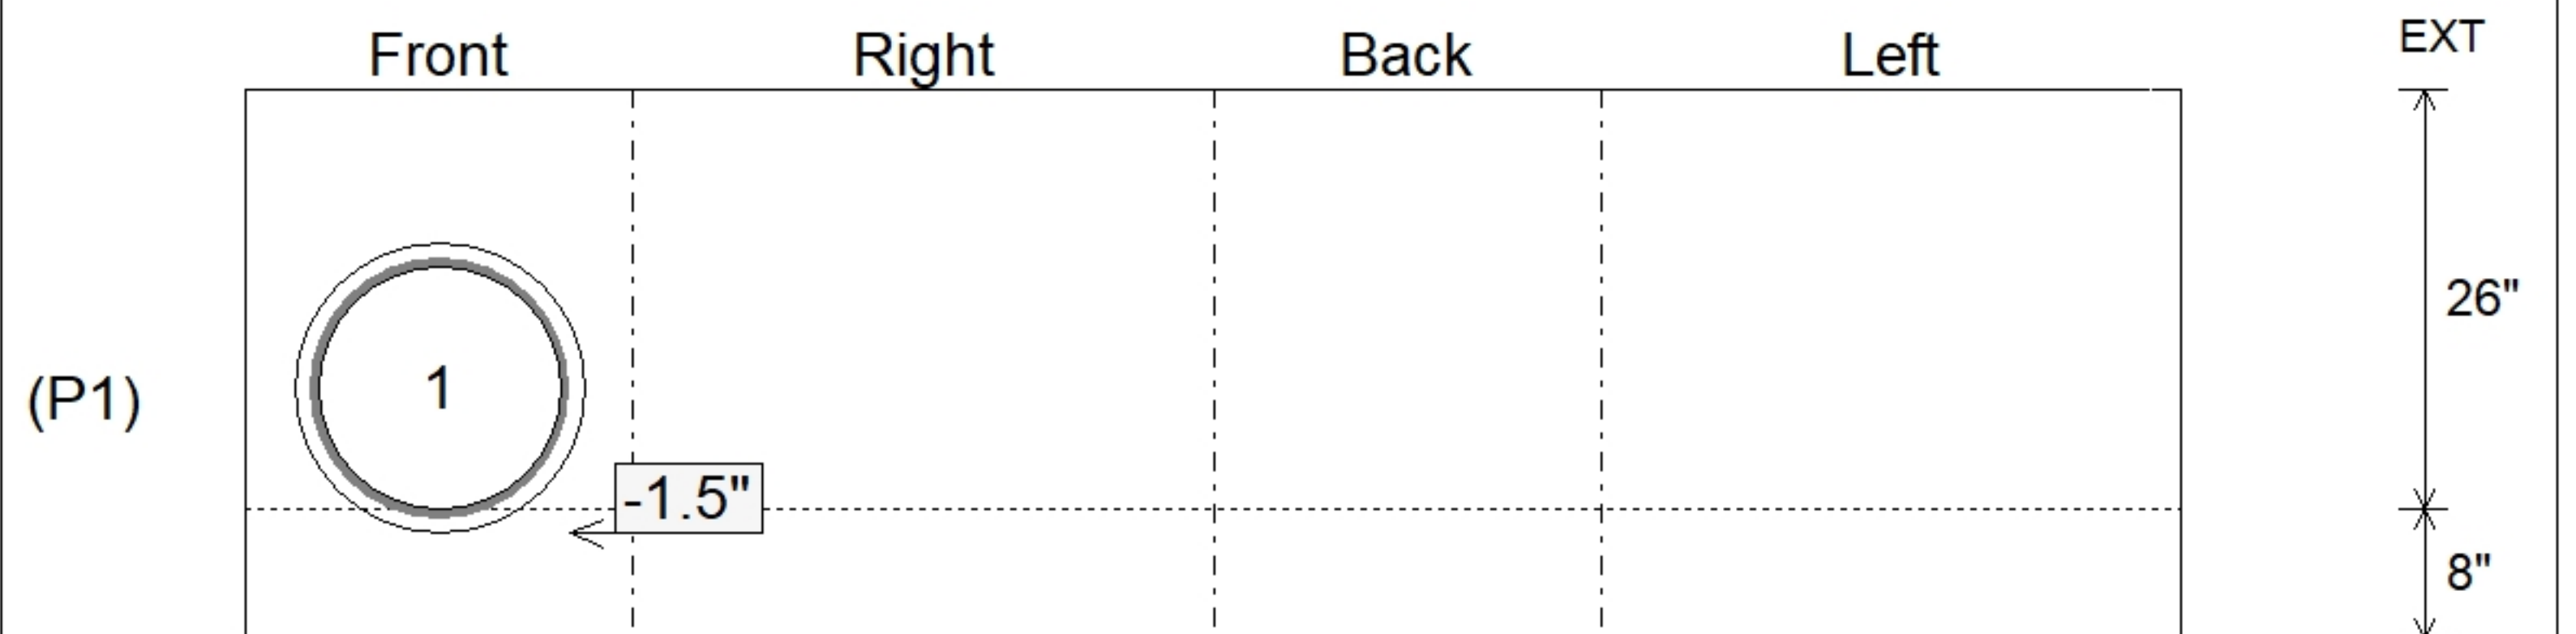

Submittal Drawing  
 12/17/2025 9:35:06 AM

SUBMITTAL  
 APPROVED BY:
