

Job Name: 25-1684P4 KYTC Jefferson Co. Call 200 (251007)
 Job Location: I-264 Louisville, Ky.
 Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.
 1/22/2026 6:51:25 AM

Tech: J. Horsley
 PC: J. Jarvis



Structure ID: JB 04 - JB-A

P1 BX3660-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

- P2) 36" x 60" - BX FLAT LID 8inW SOLID F/F - 8"
- P1) 36" x 60" - BOX BASE 8inW, 8inF, Variable Ht F/n - 56"
- 1) 36" x 60" - Conseal CS-102 1.00"
- 2) Hole - 52

2653 lb
 8222 lb
 0 lb
 0 lb

 Structure Total: 10875 lb

Structure Notes:

- ** KYTC STATE PROJECT **
- 1. PER KYTC JUNCTION BOX /ASTM C913 SPEC'S.
- 2. CONCRETE = 4,000 PSI AT 28 DAYS.
- 3. SOLID TOP SLAB - NO CASTING.

REINFORCING PER ASTM A615 (GRADE 60).



- TOP SLAB (As. 62) #5 BARS AT 6" C.C.E.W.
- WALLS (As. 31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As. 31) #5 BARS AT 12" C.C.E.W.

Rim: 5.35' Rim to Invert: 5.35' Slack: 0.2" Sump: 0" Step Position:

| Position | Elev | Angle | Ext. (cw) | Pipe | Pipe OD | Connector | Hole | Horz Size | Up () | Offset |
|----------|------|-------|-----------|---------|---------|-----------|------|-----------|--------|--------|
| Invert 1 | 0' | 90° | 38" | 48" CMP | 49" | Hole 52 | 52" | 52" | -2" | 0" |
| Invert 2 | 0' | 270° | 38" | 48" CMP | 49" | Hole 52 | 52" | 52" | -2" | 0" |
| Invert 3 | | | | | | | | | | |
| Invert 4 | | | | | | | | | | |
| Invert 5 | | | | | | | | | | |
| Invert 6 | | | | | | | | | | |
| Invert 7 | | | | | | | | | | |
| Invert 8 | | | | | | | | | | |

RIGHT-SIDE UP VIEW (int. dimensions)


UPSIDE-DOWN VIEW (int. dimensions)

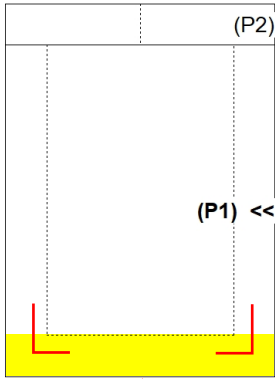

1ST POUR (FLOOR) = 2,654 LBS
 2ND POUR (WALLS) = 5,568 LBS
 4 EA. CONAC 5CA14 LIFTERS
 IN FLOOR

1ST POUR (FLOOR)
 STUB #5 L BARS YOUR TOP
 OF FLOOR AT 12" C/C FOR
 CONNECTING WALLS

INSIDE WALL DIMENSIONS

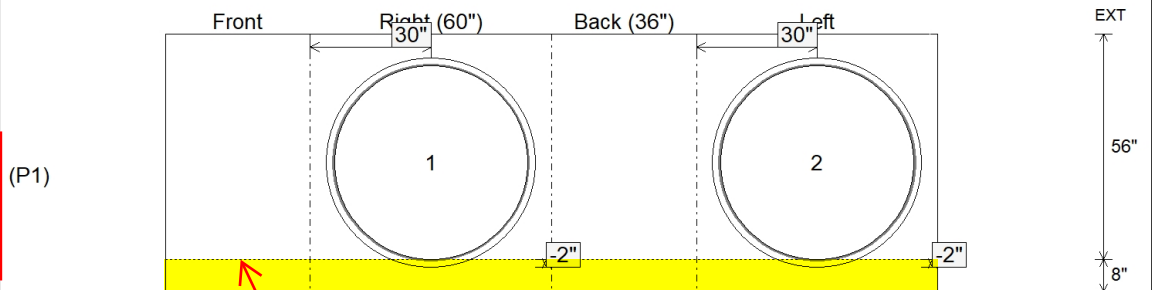

CONSEAL CS-231
 BETWEEN FLOOR & WALLS

| | | | | |
|----------------------------------|-------------------------------|--|--|---|
| Coating (Int): Coating (Ext): | Seam Up: Flat Seam Dn: n/a | Wall Thickness: 8" Floor Height: 8" | Height (Int): 56" Height (Ext): 64" | Weight (Net): 8222 lb Volume (Net): 2.1cu.yd |
|----------------------------------|-------------------------------|--|--|---|

Job Name: 25-1684P4 KYTC Jefferson Co. Call 200 (251007)
 Job Location: I-264 Louisville, Ky.
 Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.
 1/22/2026 6:51:25 AM

Tech: J. Horsley
 PC: J. Jarvis



Structure ID: JB 04 - JB-A

P1A BX3660-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

P2) 36" x 60" - BX FLAT LID 8inW SOLID F/F - 8"
 P1) 36" x 60" - BOX BASE 8inW, 8inF, Variable Ht F/n - 56"
 1) 36" x 60" - Conseal CS-102 1.00"
 2) Hole - 52

2653 lb
 8222 lb
 0 lb
 0 lb

 Structure Total: 10875 lb

Structure Notes:

- ** KYTC STATE PROJECT ****
1. PER KYTC JUNCTION BOX /ASTM C913 SPEC'S.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. SOLID TOP SLAB - NO CASTING.

REINFORCING PER ASTM A615 (GRADE 60).


- TOP SLAB (As. 62) #5 BARS AT 6" C.C.E.W.
- WALLS (As. 31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As. 31) #5 BARS AT 12" C.C.E.W.

Rim: 5.35' Rim to Invert: 5.35' Slack: 0.2" Sump: 0" Step Position:


| Position | Elev | Angle | Ext. (cw) | Pipe | Pipe OD | Connector | Hole | Horz Size | Up () | Offset |
|----------|------|-------|-----------|---------|---------|-----------|------|-----------|--------|--------|
| Invert 1 | 0' | 90° | 38" | 48" CMP | 49" | Hole 52 | 52" | 52" | -2" | 0" |
| Invert 2 | 0' | 270° | 38" | 48" CMP | 49" | Hole 52 | 52" | 52" | -2" | 0" |
| Invert 3 | | | | | | | | | | |
| Invert 4 | | | | | | | | | | |
| Invert 5 | | | | | | | | | | |
| Invert 6 | | | | | | | | | | |
| Invert 7 | | | | | | | | | | |
| Invert 8 | | | | | | | | | | |

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

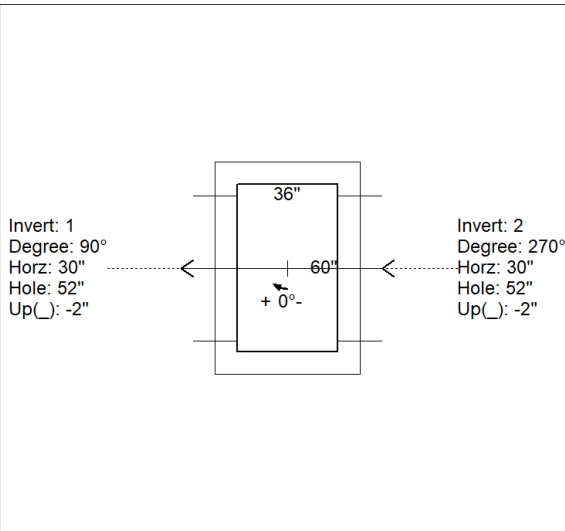


1ST POUR (FLOOR) = 2,654 LBS
2ND POUR (WALLS) = 5,568 LBS
4 EA. CONAC 5CA14 LIFTERS
IN FLOOR

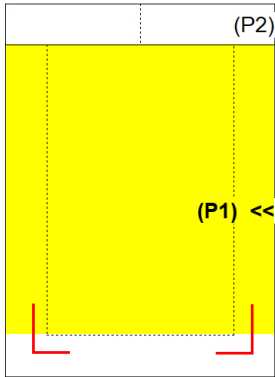

2ND POUR (WALLS)

INSIDE WALL DIMENSIONS

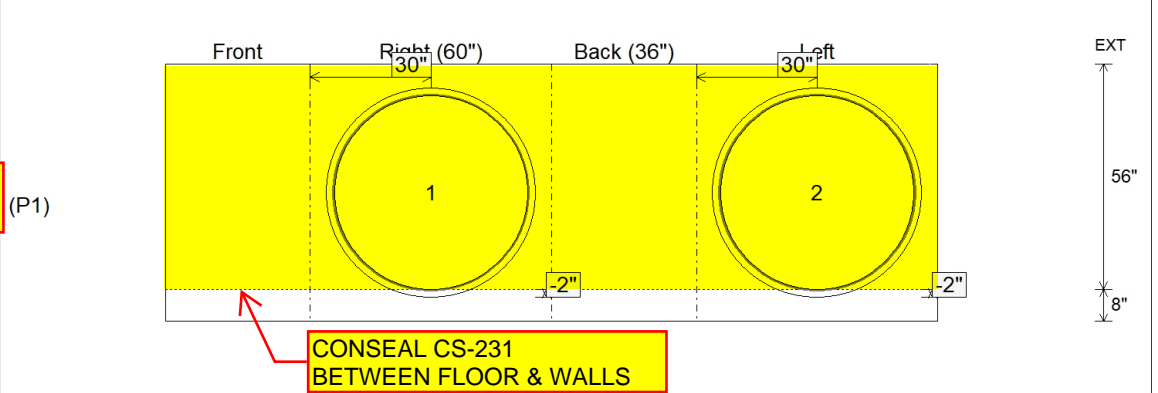

| | | | | |
|----------------------------------|-------------------------------|--|--|---|
| Coating (Int): Coating (Ext): | Seam Up: Flat Seam Dn: n/a | Wall Thickness: 8" Floor Height: 8" | Height (Int): 56" Height (Ext): 64" | Weight (Net): 8222 lb Volume (Net): 2.1cu.yd |
|----------------------------------|-------------------------------|--|--|---|
