

Job Name: 25-1684P7 KYTC Jefferson Co. Call 200 (251007)  
 Job Location: I-264 Louisville, Ky.  
 Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.  
 3/19/2026 1:03:54 PM

Tech: J. Coppage  
 PC: J. Jarvis



**Structure ID: 125+87 LT CBIA INLET 31**

**P1 BX2436-08BA48**

**BOX BASE 8inW, 8inF**

- P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT - 10"
- P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT - 18"
- P1) 24" x 36" - BOX BASE 8inW, 8inF - 48"
- 1) 24" x 36" - Conseal CS-102 1.00"
- 1) Hole - 22
- 2) Hole - 18

**Structure Notes:**  
 -KYTC STATE PROJECT 251007  
 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)  
 -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).  
 -KYTC CERTIFICATIONS REQUIRED.


Structure Total: 14294 lb

Rim: 591.85' Rim to Invert: 6.74' Slack: 4.88" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ( )	Offset
Invert 1	585.11'	0°	20"	18" CMP	19"	Hole 22	22"	22"	-2"	0"
Invert 2	585.11'	135°	34.686"	15" CMP	16"	Hole 18	18"	25.456"	-1.5"	-8"
Invert 3	585.11'	180°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

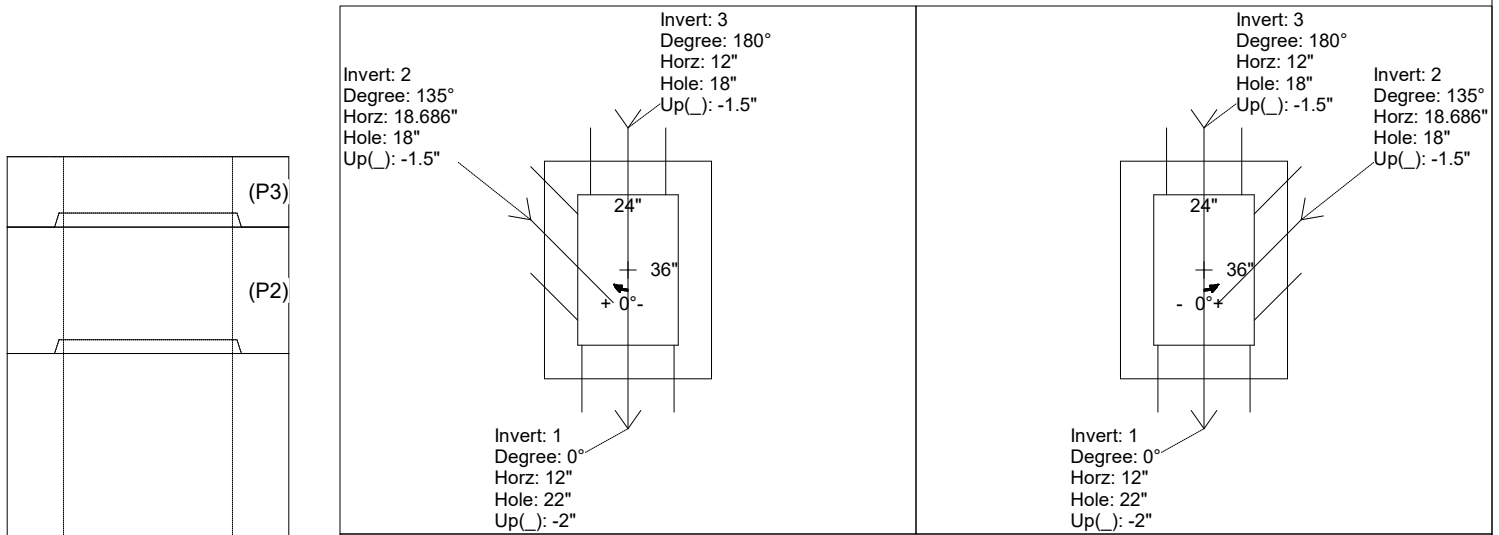

INSIDE WALL DIMENSIONS

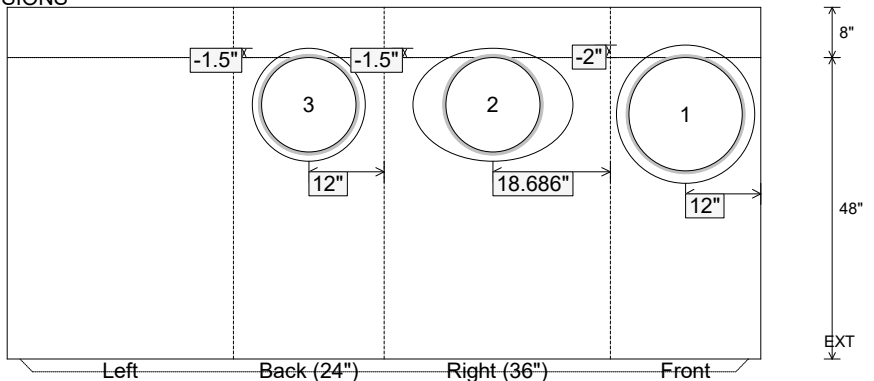

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 48" Height (Ext): 56"	Weight (Net): 5626 lb Volume (Net): 1.44cu.yd
----------------------------------	---------------------------------	--	--	--
