

Job Name: 25-2023 - Guthrie KY. Convenience Store Job Location: Guthrie, KY Contractor: Core & Main LP					Plant: 100		Tech: Jared - F			
					5/5/2026 1:11:16 PM		PC: T. Lewis			
Structure ID: MH 2										
P1 MH048BAEVFCDARED					MH BASE w/FLANGE (08F/08EF) w/ConBlock-CDA Red					
P3) 24" - CASTING HEIGHT - 7.50" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 36" P1) 48" - MH BASE w/FLANGE (08F/08EF) w/ConBlock-CDA Red T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE CONBLOCK CDA RED 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) CASTING - JBS 1123 WT F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) PSX - 8QRS-S NYLO 6) MH Step ML-10-TDS-NCR - 10"					0 lb 2251 lb 5333 lb 0 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 8 lb 6 lb 0 lb ----- Structure Total: 9289 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING BY ICAST (JBS 1123 WT F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 554.1' Rim to Invert: 6.5' Slack: 0.5" Sump: 2" Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	547.6'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	547.8'	90°	45.553"	4" PVC SDR35	4.25"	PSX 8QRS-S NYLO	8"	8.038"	2.4"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)


UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS


Coating (Int):	Seam Up: Tongue	Wall Thickness: 5"	Height (Int): 36"	Weight (Net): 5333 lb
Coating (Ext):	Seam Dn: n/a	Floor Height: 8"	Height (Ext): 44"	Volume (Net): 1.36cu.yd

Job Name: 25-2023 - Guthrie KY. Convenience Store Job Location: Guthrie, KY Contractor: Core & Main LP				Plant: 100 5/5/2026 1:11:16 PM		Tech: Jared - F PC: T. Lewis				
Structure ID: MH 2										
P1 MH048BAEVFCDARED				MH BASE w/FLANGE (08F/08EF) w/ConBlock-CDA Red						
P3) 24" - CASTING HEIGHT - 7.50" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 36" P1) 48" - MH BASE w/FLANGE (08F/08EF) w/ConBlock-CDA Red T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE CONBLOCK CDA RED 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) CASTING - JBS 1123 WT F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) PSX - 8QRS-S NYLO 6) MH Step ML-10-TDS-NCR - 10"				0 lb 2251 lb 5333 lb 0 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 8 lb 6 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING BY ICAST (JBS 1123 WT F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 554.1' Rim to Invert: 6.5' Slack: 0.5' Sump: 2' Step Position: 0°				Structure Total: 9289 lb		Invert channel drawing Full height invert				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	547.6'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	547.8'	90°	45.553"	4" PVC SDR35	4.25"	PSX 8QRS-S NYLO	8"	8.038"	2.4"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

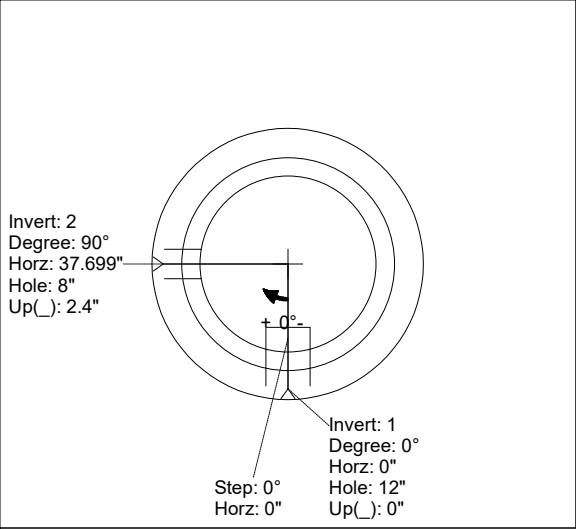

UPSIDE-DOWN VIEW (int. dimensions)

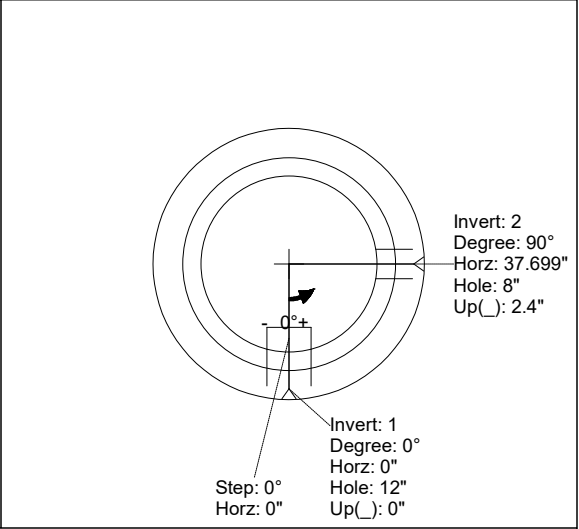

INSIDE WALL DIMENSIONS

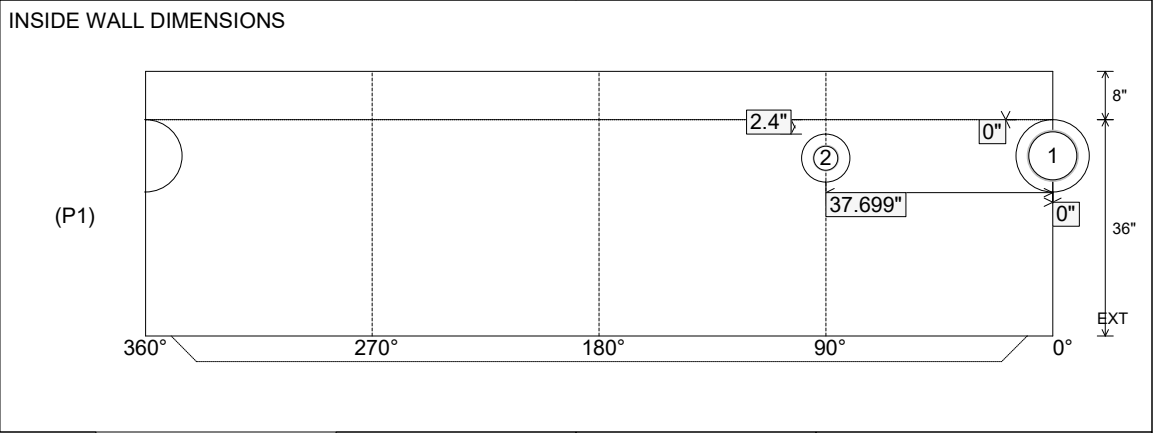

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 8"	Height (Int): 36" Height (Ext): 44"	Weight (Net): 5333 lb Volume (Net): 1.36cu.yd
----------------------------------	---------------------------------	--	--	--
