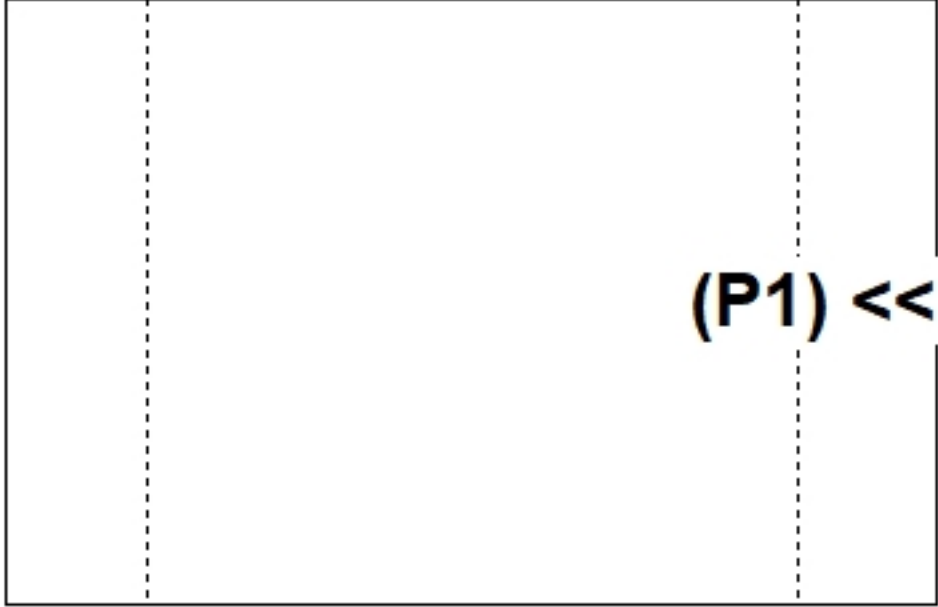
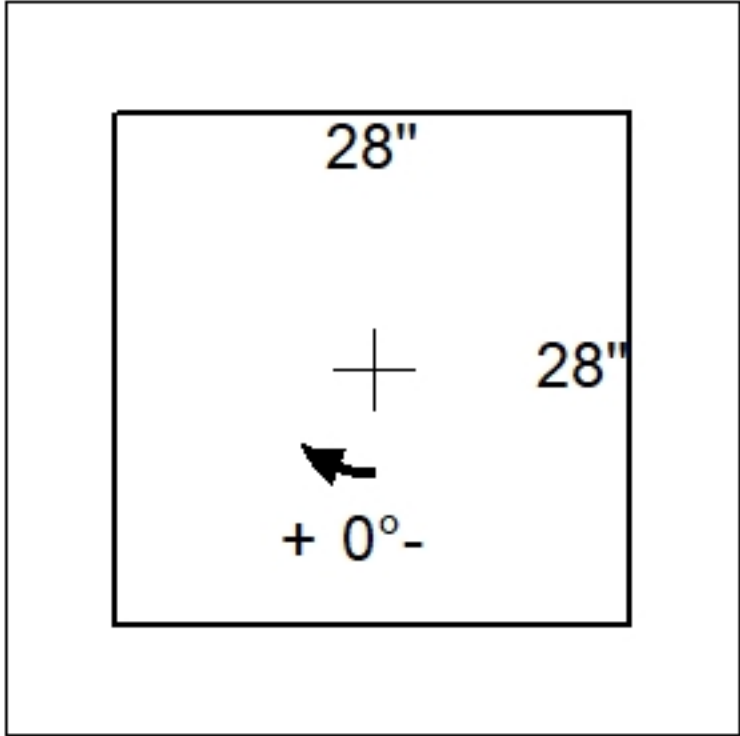



Job Name: 25-2284C Parks at Cane Ridge Ph.2B Job Location: Antioch, TN Contractor: Josh King Excavating					Plant: Beaver Dam 6/22/2026 8:23:29 AM		Tech: S. Felletter PC: A. Chambers				
Structure ID: D4.3											
P1		BX2828-06R-VH		BOX RISER 6inW, Variable Ht F/F							
P1) 28" x 28" - BOX RISER 6inW, Variable Ht F/F - 26"							1780 lb Structure Total: 1780 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. . REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.		
Rim: 2.167' Rim to Invert: 0' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
		INSIDE WALL DIMENSIONS									
(P1)										EXT 26"	
		Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: Flat		Wall Thickness: 6" Floor Height: 0"		Height (Int): 26" Height (Ext): 26"		Weight (Net): 1780 lb Volume (Net): 0.46cu.yd	
