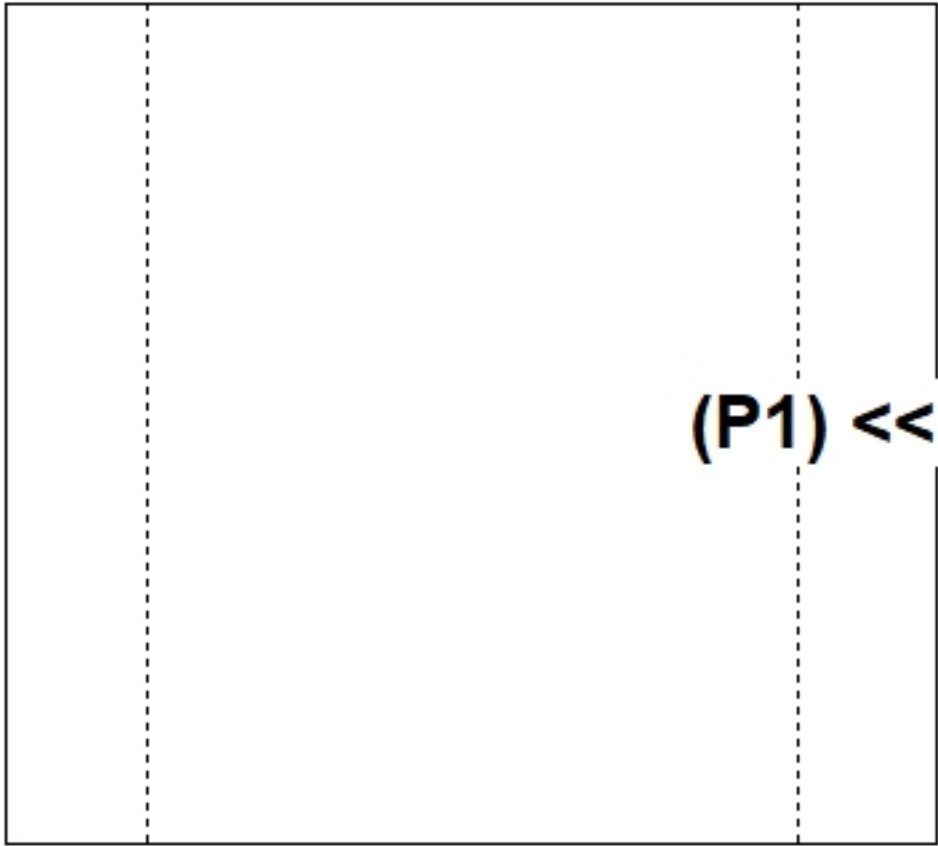
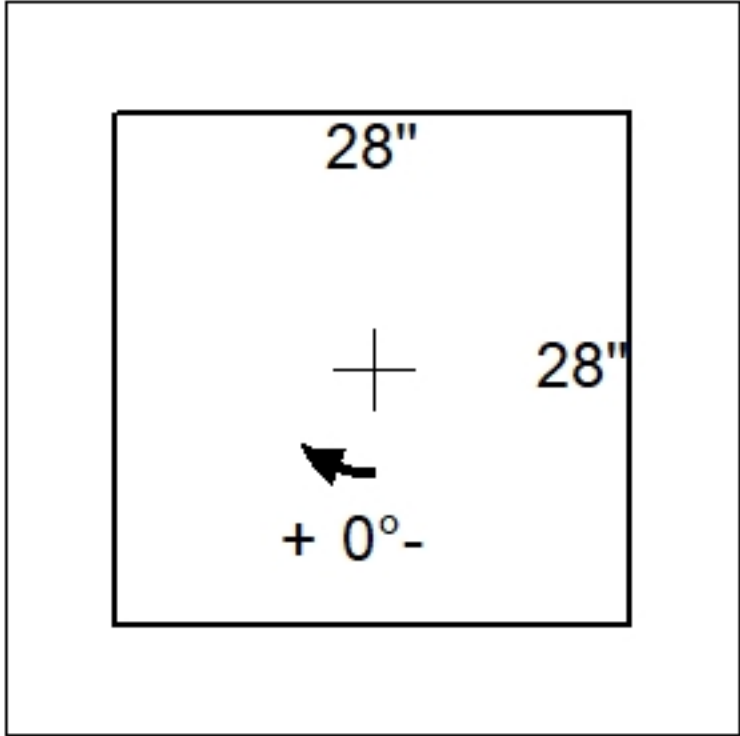


Job Name: 25-2284C Parks at Cane Ridge Ph.2B Job Location: Antioch, TN Contractor: Josh King Excavating					Plant: Beaver Dam 7/21/2026 8:41:50 AM		Tech: S. Felletter PC: A. Chambers					
Structure ID: E4.11												
P1		BX2828-06R-VH			BOX RISER 6inW, Variable Ht F/F							
P1) 28" x 28" - BOX RISER 6inW, Variable Ht F/F - 36"							2465 lb Structure Total: 2465 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. . REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 3'		Rim to Invert: 0'		Slack: 0"		Sump: 0"		Step Position:				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1												
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions)												
												
		INSIDE WALL DIMENSIONS										
(P1)		Front				Right (28")		Back (28")		Left		EXT 36"
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: Flat		Wall Thickness: 6" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 2465 lb Volume (Net): 0.63cu.yd		
