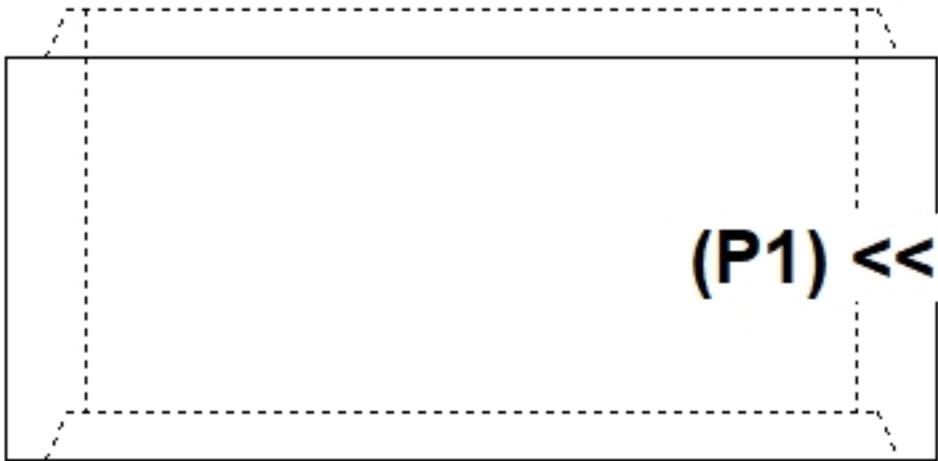
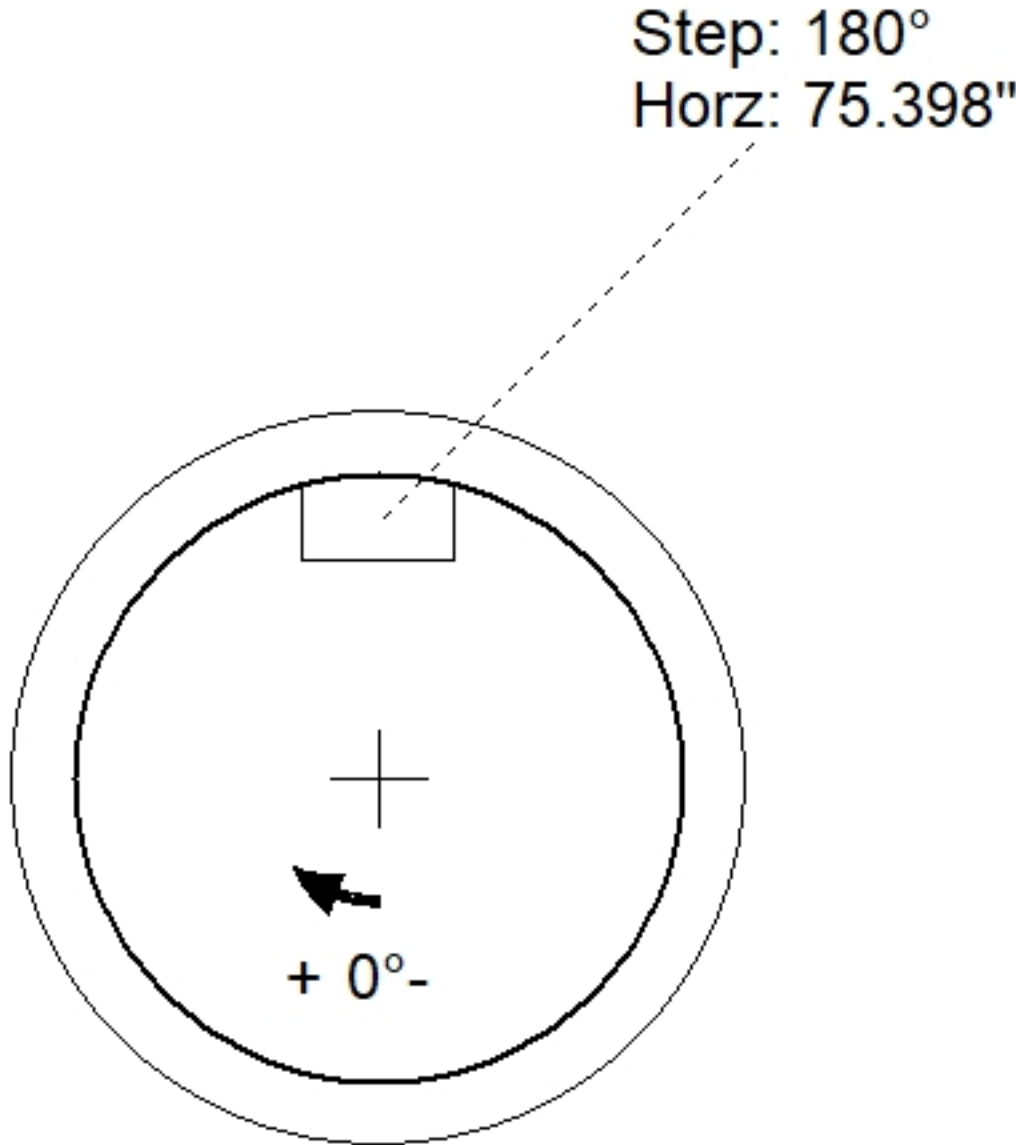
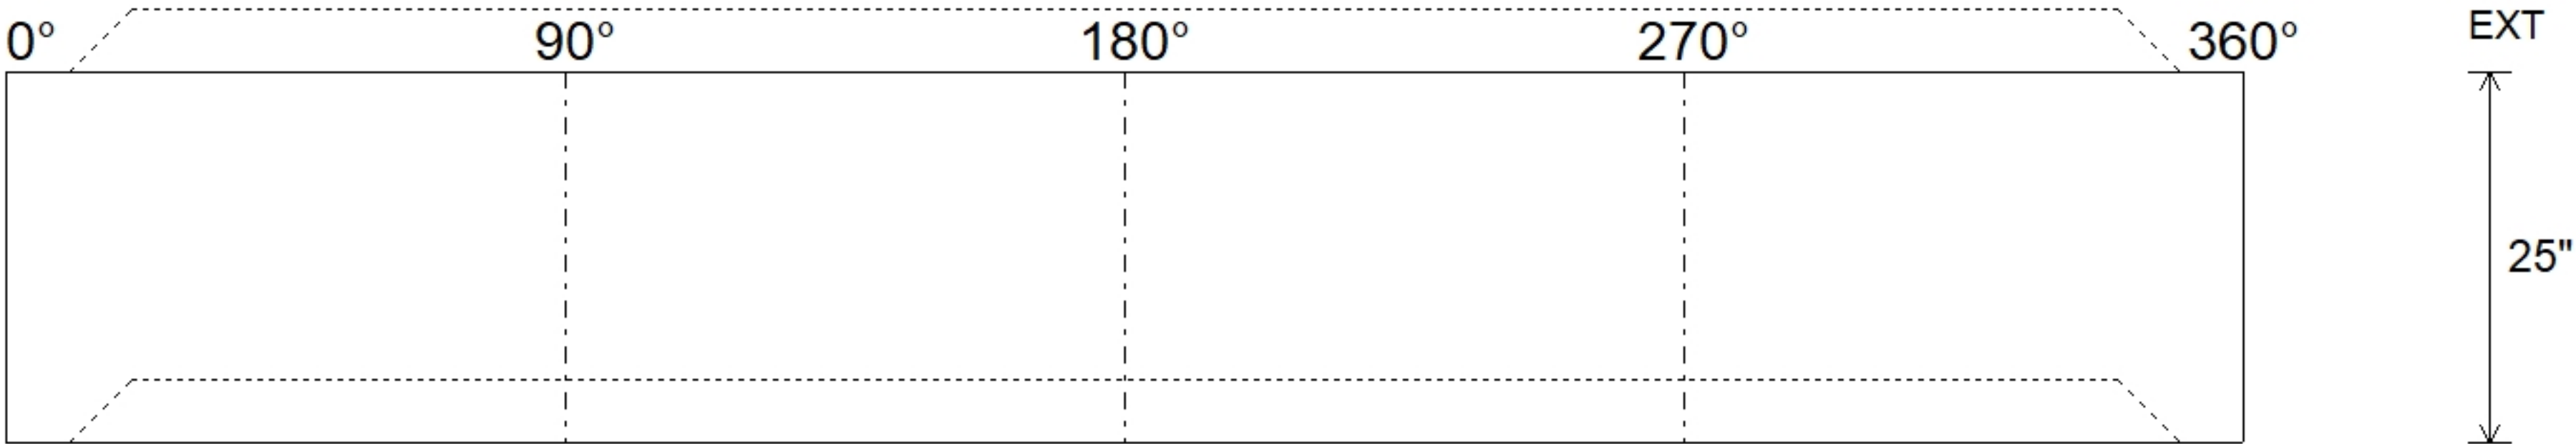


Job Name: 25-2284C Parks at Cane Ridge Ph.2B Job Location: Antioch, TN Contractor: Josh King Excavating					Plant: Beaver Dam 7/21/2026 8:41:53 AM		Tech: S. Felletter PC: A. Chambers				
Structure ID: E7.0											
P1		MH048RSVF		MH RISER Custom Ht T/G							
P1) 48" - MH RISER Custom Ht T/G - 25" 2) MH Step ML-10-TDS-NCR - 10"						1746 lb 0 lb ----- Structure Total: 1746 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. . REINFORCING PER ASTM A615 (GRADE 60). - RISER/WALLS (As .12)			
Rim: 2.083'		Rim to Invert: 0'		Slack: 0"		Sump: 0"		Step Position: 180			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
		INSIDE WALL DIMENSIONS									
(P1)											
		Coating (Int): Coating (Ext):		Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 25" Height (Ext): 25"		Weight (Net): 1746 lb Volume (Net): 0.45cu.yd	
