

Contractor: Josh King Excavating

Plant: Beaver Dam



Size: 28" x 96"

Rim: 0.667'
Invert: 0.667'
Rim to Invert: 0'

Sump: 0"
Floor (Top): 0'
Floor Height: 0"

Floor (Bot): 0'
Overall Height: 0.667'
Slack: 0"


Structure Notes: 1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:

P1) 28" x 96" - CB FLAT TOP 6"W w/CASTING CAST IN F/F - 8"
1) CASTING - JBS 1072 F/C STORM
1) 24" - Conseal CS-102 1.00"

2596 lb
250 lb
0 lb

Structure Total: 2846 lb

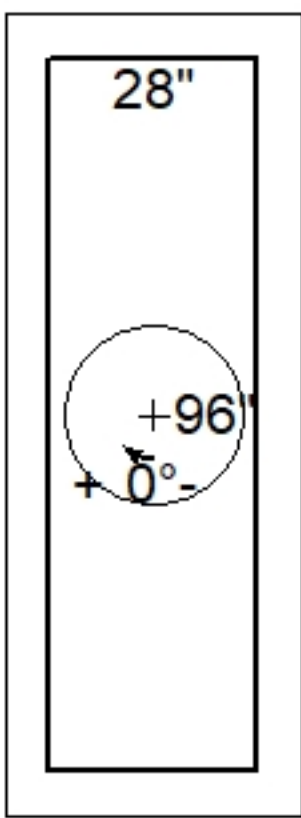

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	0.667'							
Reducer								
Invert 1								
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions



Diagram showing a rectangular object with dimensions and labels:

- Length: 12" (labeled above the rectangle)
- Width: 8" (labeled to the right of the rectangle)
- Labels above the rectangle: Front, Right, Back, Left
- Label to the left of the rectangle: (P1)
- Label to the right of the rectangle: EXT

Submittal Drawing
8/5/2026 8:19:36 AM

SUBMITTAL
APPROVED BY:
