

Job Name: 25-2397 Sandy Springs Sec. 2
Job Location: Elizabethtown, KY 42701
Contractor: Dirt Works Unlimited, LLC.

Plant: 100

7/9/2026 2:51:26 PM

Tech: Jared - A

PC: Thomas Ryan



Structure ID: B

P1 MH048BAVF

MH BASE Custom Ht

- P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x36" Hole - 7"
P1) 48" - MH BASE Custom Ht - 38"
1) CASTING - HOE 525 SET (F/G/H)
1) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 30
1) Hole - 18
3) MH Step ML-10-TDS-NCR - 10"

- 0 lb
1044 lb
3244 lb
442 lb
0 lb
0 lb
0 lb
0 lb
0 lb



Structure Total: 4730 lb
- Structure Notes:**
PLAN LABEL: B
1. HOE 525 SET (F/G/H) PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 693.25' Rim to Invert: 4.1' Slack: 0.2" Sump: 2" Step Position: 186°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	689.15'	0°	0"	24" HDPE	27.8"	Hole 30	30"	32.406"	0.1"	0"
Invert 2	689.15'	97°	49.096"	12" RCP B WALL	16"	Hole 18	18"	18.451"	0"	0"
Invert 3	689.15'	275°	139.19"	24" HDPE	27.8"	Hole 30	30"	32.406"	0.1"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

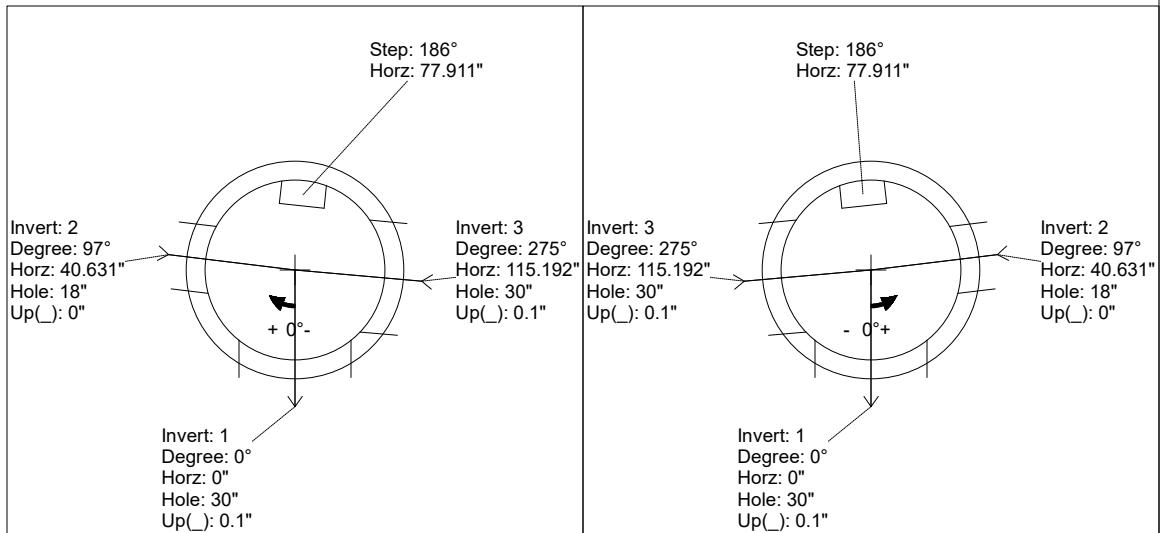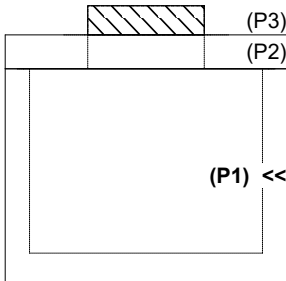

INSIDE WALL DIMENSIONS

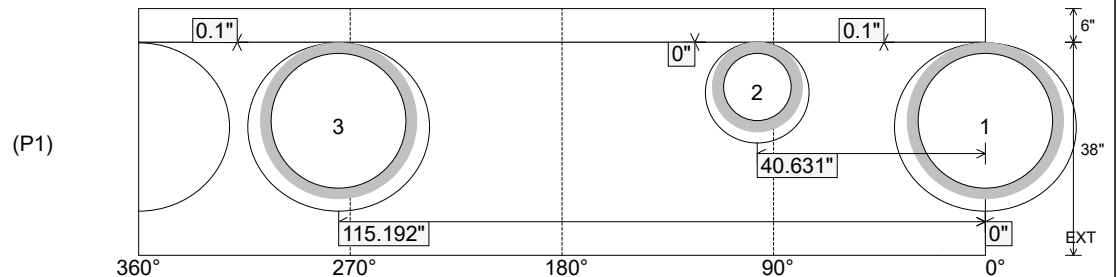

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 38"
Height (Ext): 44"

Weight (Net): 3244 lb
Volume (Net): 0.83cu.yd
