




Structure ID: C			
Spec: Storm	Rim: 693.25'	Sump: 0"	Floor (Bot): 689.323'
Type: BX 8inW, 8inF	Invert: 689.99'	Floor (Top): 689.99'	Overall Height: 3.917'
Size: 24" x 36"	Rim to Invert: 3.26'	Floor Height: 8"	Slack: 0.12"

Structure Notes: PLAN LABEL: C


1. HOE 525 SET (F/G/H) PROVIDED BY ICAST.
2. PER ASTM C913 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .12) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:	
P2) 24" x 36" - CASTING HEIGHT - 6"	0 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 33"	4593 lb
1) CASTING - HOE 525 SET (F/G/H)	442 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 18	0 lb


Structure Total:	5035 lb

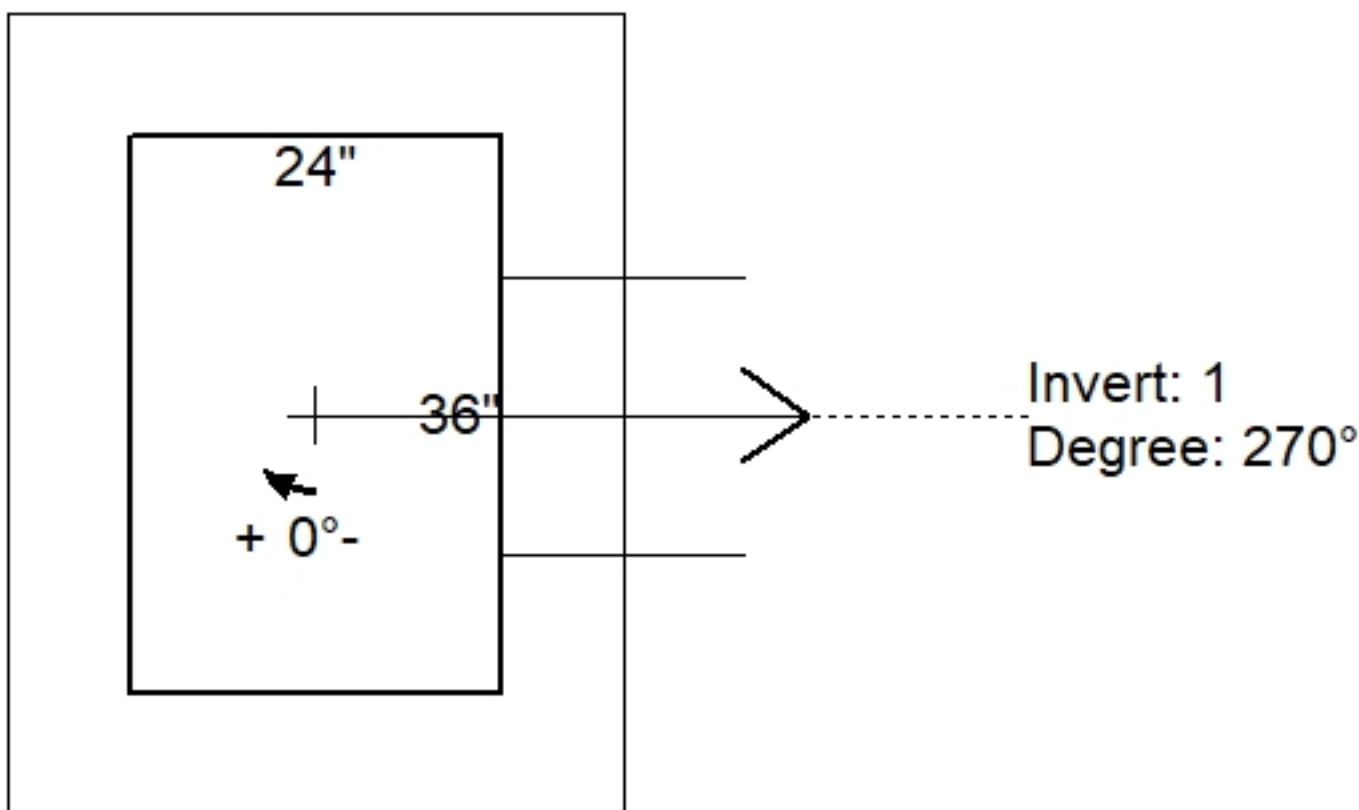

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	693.25'							
Reducer								
Invert 1	689.99'	270°	12" RCP B WALL	16"	18"	Hole 18	-2"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

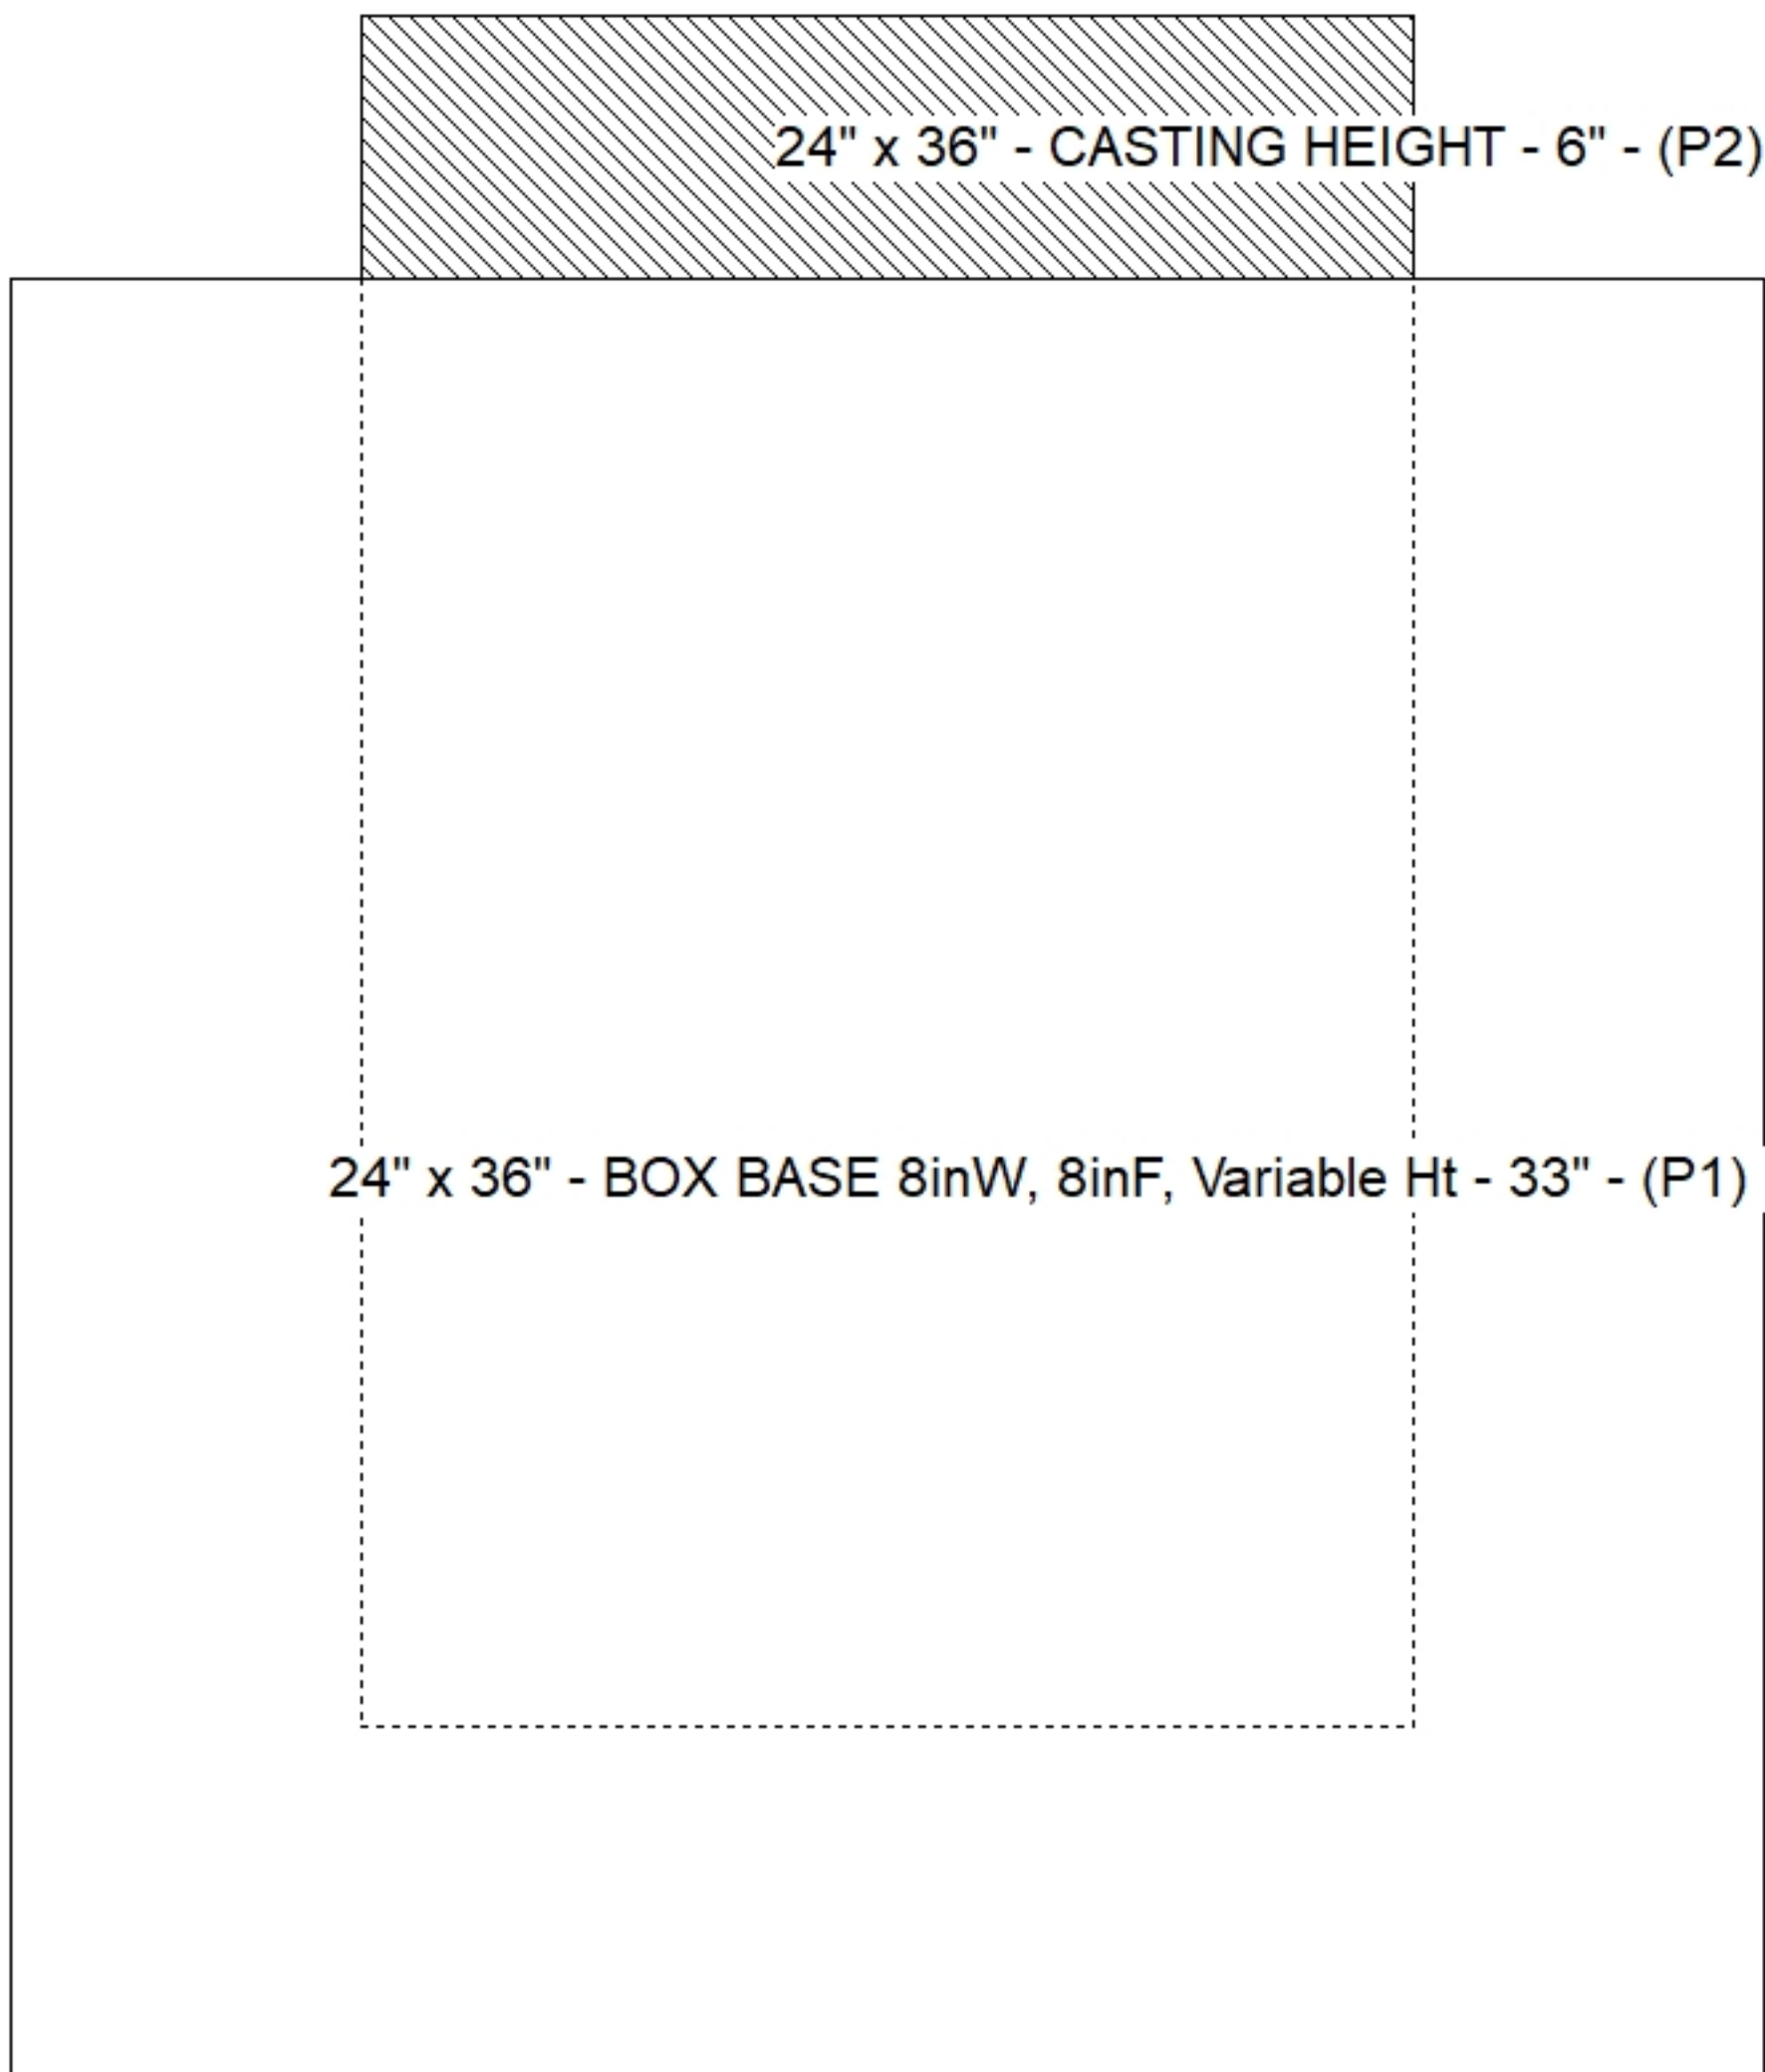

Default - Interior Dimensions

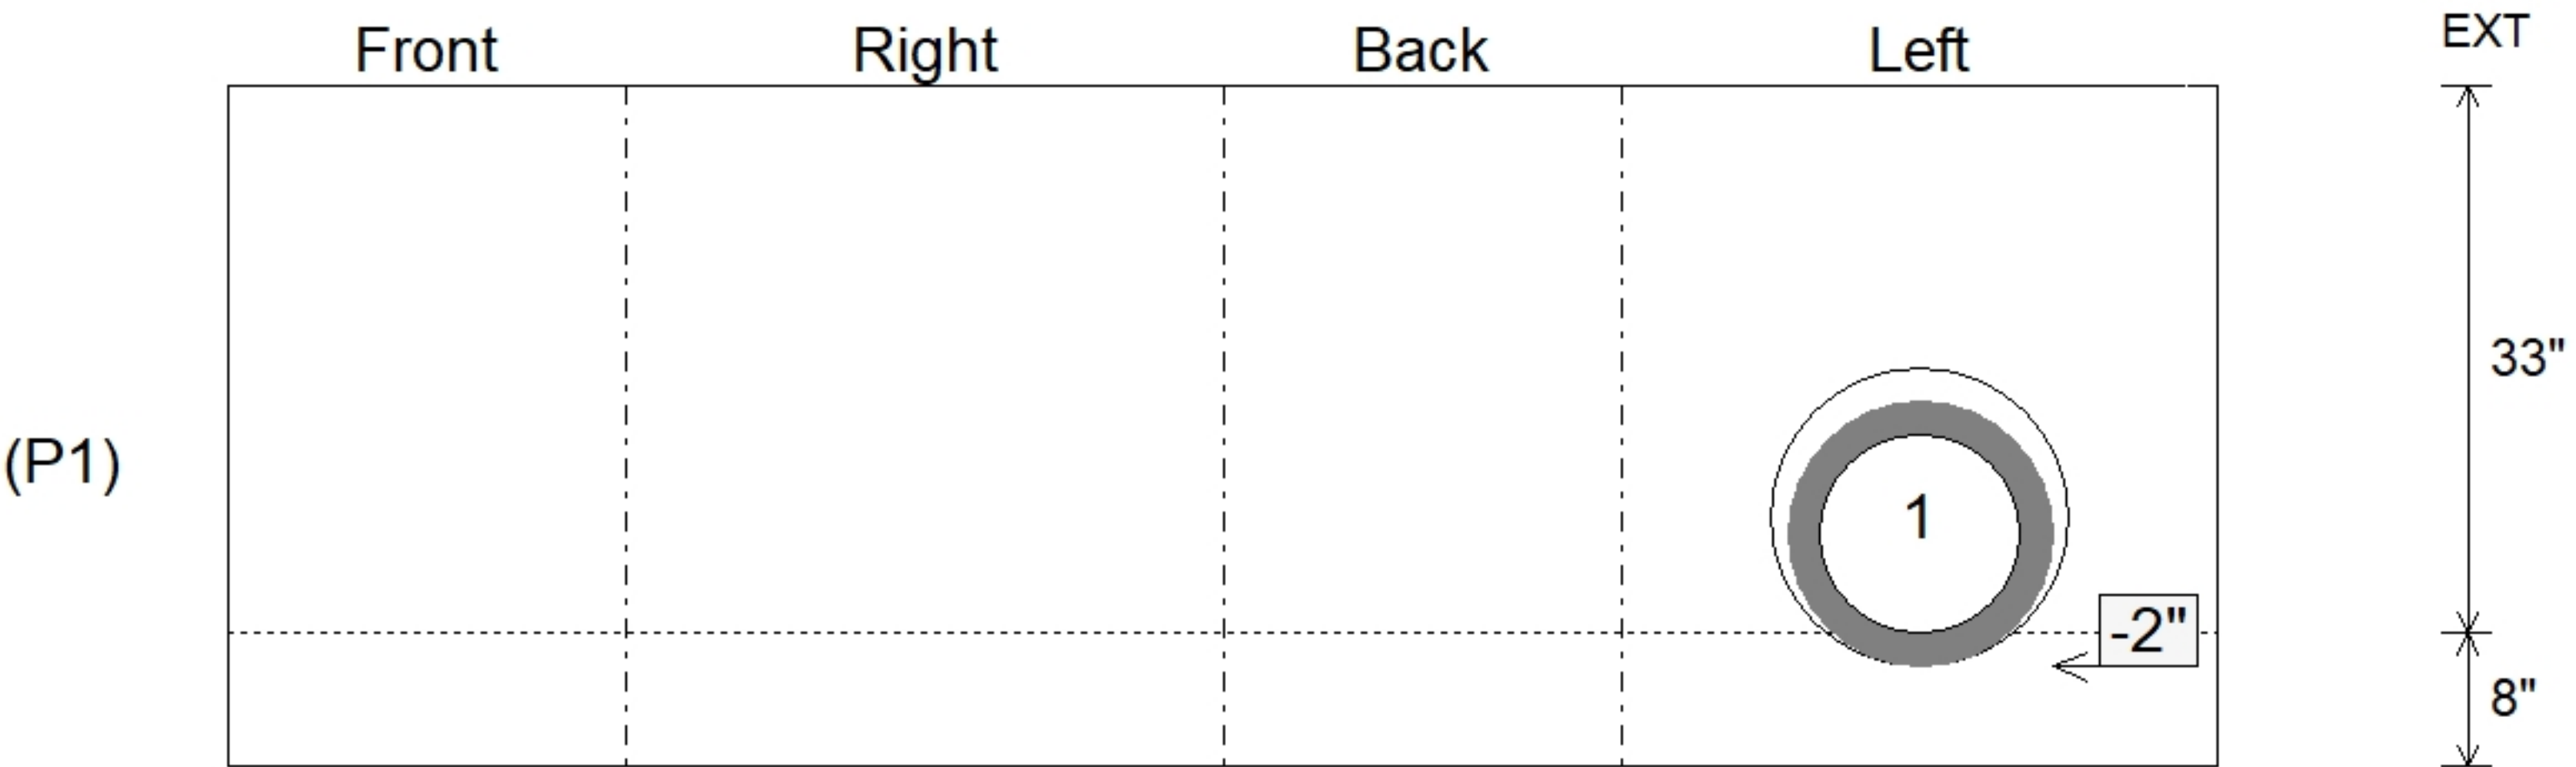

Submittal Drawing 7/14/2026 12:21:17 PM	SUBMITTAL APPROVED BY:
--	---------------------------
