

Job Name: 25-2397 Sandy Springs Sec. 2  
Job Location: Elizabethtown, KY 42701  
Contractor: Dirt Works Unlimited, LLC.

Plant: 100

7/9/2026 2:52:12 PM

Tech: Jared - A

PC: Thomas Ryan



## Structure ID: E



### P2 MH048LD07-24X36RECT

### MH FLAT TOP w/24"x36" Hole

- P3) 24" x 36" - CASTING HEIGHT - 6"  
P2) 48" - MH FLAT TOP w/24"x36" Hole - 7"  
P1) 48" - MH BASE Custom Ht - 39"  
1) CASTING - HOE 525 SET (F/G/H)  
1) 48" - Conseal CS-102 1.00"  
1) 24" x 36" - Conseal CS-102 1.00"  
1) Hole - 32  
1) Hole - 30  
1) Hole - 20  
3) MH Step ML-10-TDS-NCR - 10"

- 0 lb  
1044 lb  
3240 lb  
442 lb  
0 lb  
0 lb  
0 lb  
0 lb  
0 lb  
0 lb  
0 lb
- Structure Notes:**  
**PLAN LABEL: E**  
1. HOE 525 SET (F/G/H) PROVIDED BY ICAST.  
2. PER ASTM C478 SPECIFICATIONS.  
3. CONCRETE = 4,000 PSI AT 28 DAYS.  
4. REINFORCING PER ASTM A615 (GRADE 60).  
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..  
- RISER/WALLS (As .12)  
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 4726 lb

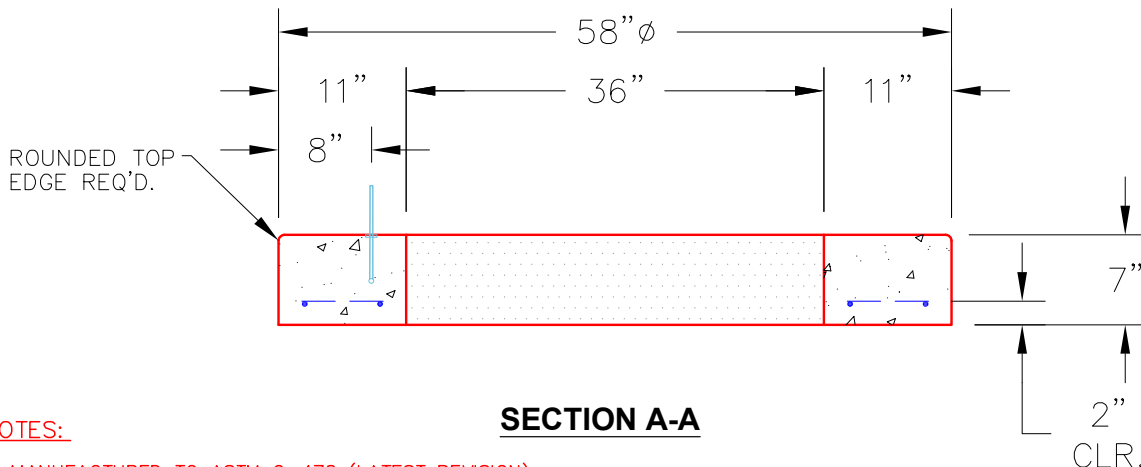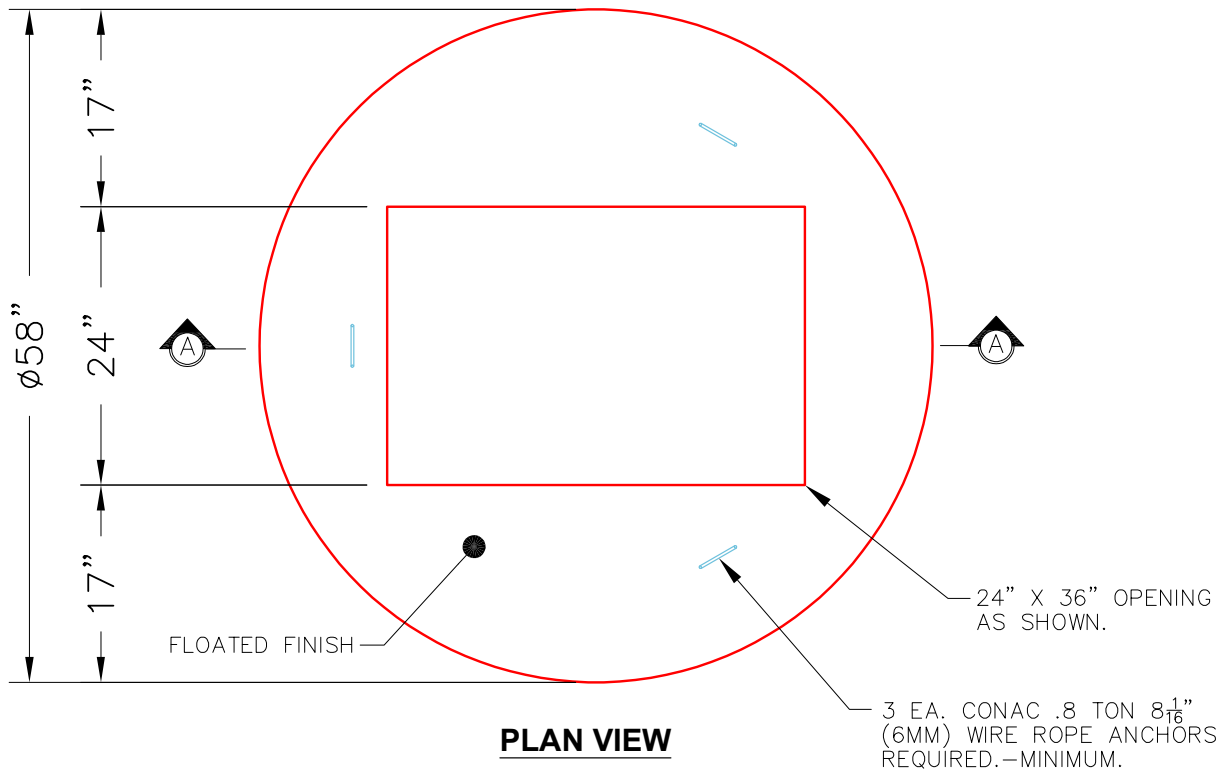

#### NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 5,000 PSI AT 28 DAYS.
3. REINFORCING: #4 BAR @ 10" O.C. E.W. (GRADE 60).

Coating (Int):  
Coating (Ext):

Seam Up: Flat  
Seam Dn: Flat

Wall Thickness: 5"

Height (Ext): 7"

Weight (Net): 1044 lb  
Volume (Net): 0.27cu.yd
