


Job Name: 25-2397 Sandy Springs Sec. 2
Job Location: Elizabethtown, KY 42701
Contractor: Dirt Works Unlimited, LLC.

Plant: 100
7/10/2026 2:51:50 PM

Tech: Jared - A
PC: Thomas Ryan



Structure ID: F

P1 MH048BA36

MH BASE

- P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x36" Hole - 12"
P1) 48" - MH BASE - 36"
1) CASTING - HOE 525 SET (F/G/H)
1) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 30
1) Hole - 32
3) MH Step ML-10-TDS-NCR - 10"

- 0 lb
1300 lb
3166 lb
442 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Notes: PLAN LABEL: F
1. HOE 525 SET (F/G/H) PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.




Structure Total: 4908 lb

Rim: 692.1' Rim to Invert: 4.26' Slack: 0.12' Sump: 3' Step Position: 135°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	687.84'	0°	0"	24" HDPE	27.8"	Hole 30	30"	32.406"	1.1"	0"
Invert 2	687.84'	270°	136.659"	24" RCP B WALL	30"	Hole 32	32"	35.027"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

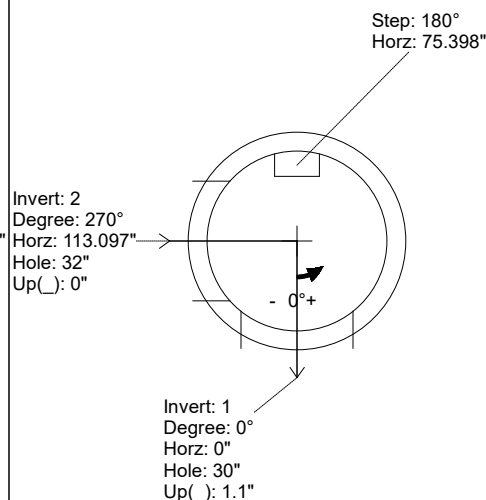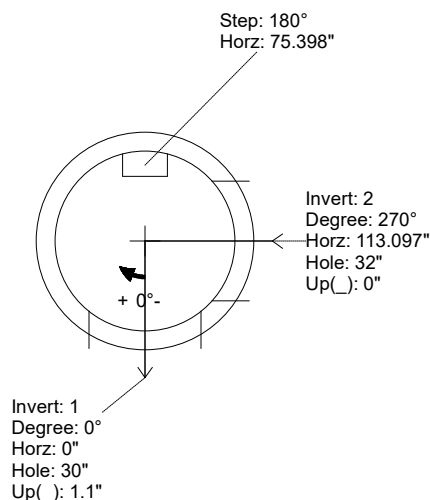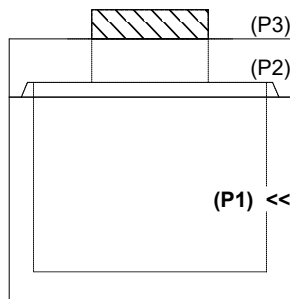

INSIDE WALL DIMENSIONS

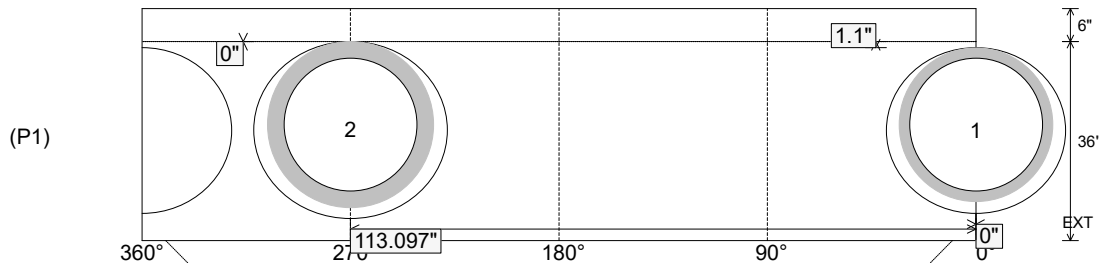

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 36"
Height (Ext): 42"

Weight (Net): 3166 lb
Volume (Net): 0.81cu.yd
