

Job Name: 25-2397 Sandy Springs Sec. 2
Job Location: Elizabethtown, KY 42701
Contractor: Dirt Works Unlimited, LLC.

Plant: 100

7/9/2026 2:52:13 PM

Tech: Jared - A

PC: Thomas Ryan



Structure ID: L


P2 MH060LD08-24X36RECT

MH FLAT TOP w/24"x36" Hole

- P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 60" - MH FLAT TOP w/24"x36" Hole - 8"
P1) 60" - MH BASE Custom Ht - 47"
1) CASTING - HOE 525 SET (F/G/H)
1) 60" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 44
1) Hole - 38
1) Hole - 26
4) MH Step ML-10-TDS-NCR - 10"

- 0 lb
2153 lb
5913 lb
442 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
- Structure Notes:
PLAN LABEL: L
1. HOE 525 SET (F/G/H) PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

Structure Total: 8508 lb

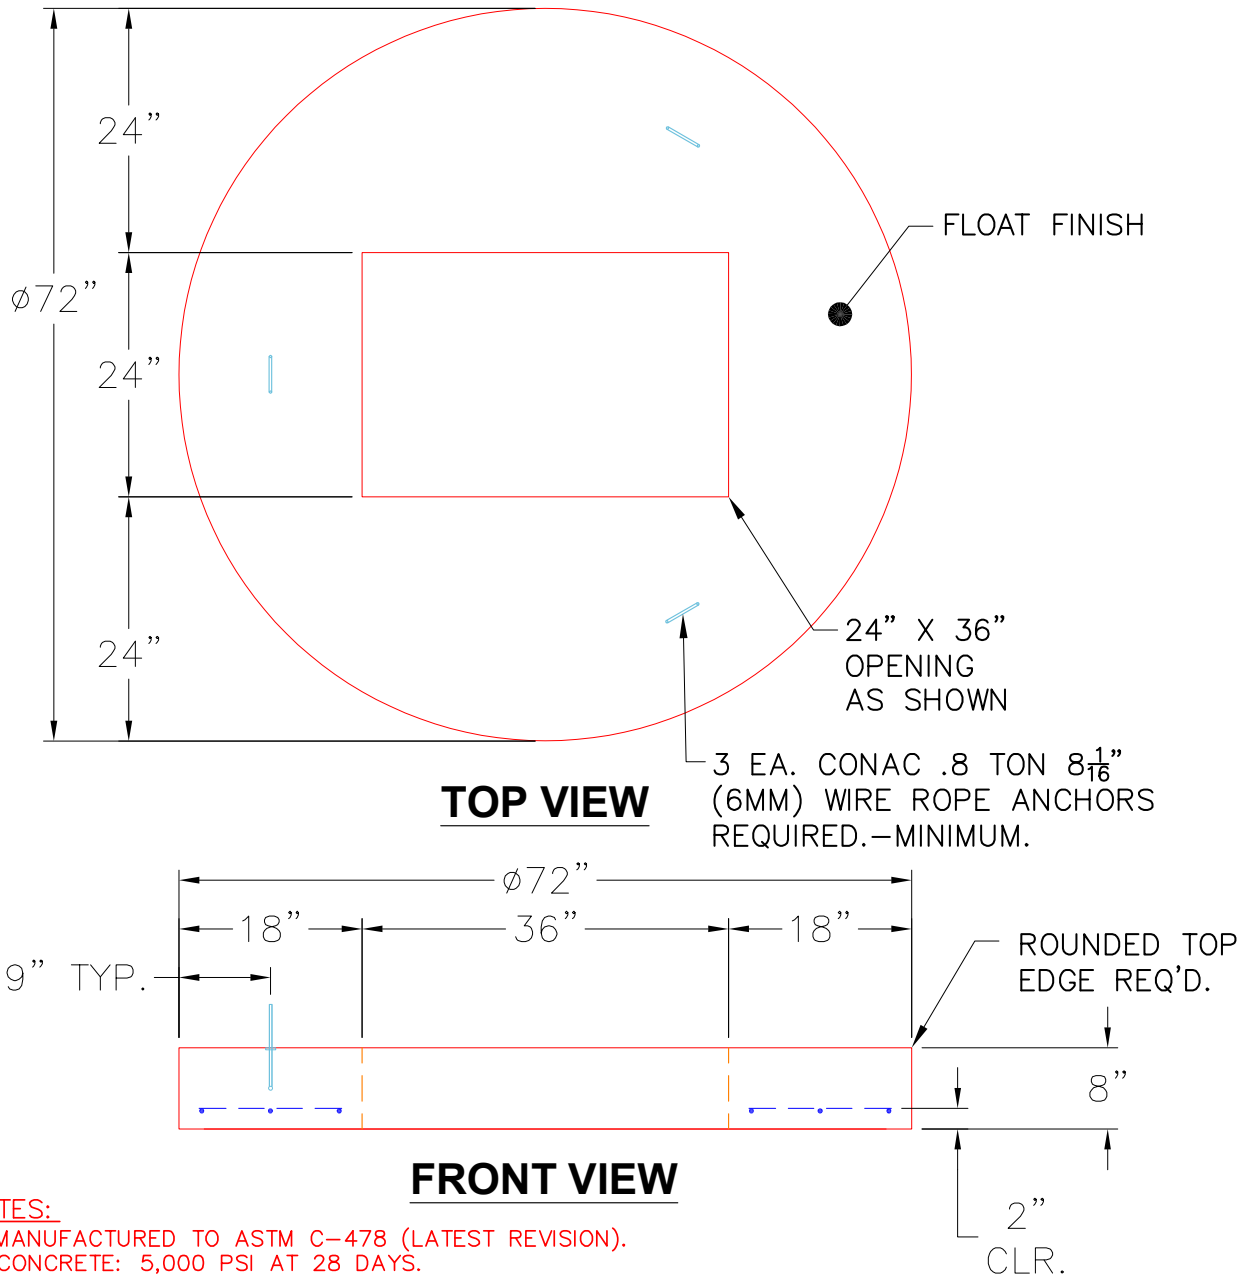

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 6"

Height (Ext): 8"

Weight (Net): 2153 lb
Volume (Net): 0.55cu.yd
