

Job Name: 25-2397 Sandy Springs Sec. 2
Job Location: Elizabethtown, KY 42701
Contractor: Dirt Works Unlimited, LLC.

Plant: 100

7/9/2026 2:52:14 PM

Tech: Jared - A

PC: Thomas Ryan



Structure ID: Q

P2 MH072LD08S

MH FLAT TOP SPEC. HT. (8") w/24"x36" Hole

P3) 24" x 36" - CASTING HEIGHT - 6"

P2) 72" - MH FLAT TOP SPEC. HT. (8") w/24"x36" Hole - 8"

P1) 72" - MH BASE - 54"

1) CASTING - HOE 525 SET (F/G/H)

1) 72" - Conseal CS-102 1.00"

1) 24" x 36" - Conseal CS-102 1.00"

1) DOGHOUSE INVRTD - 54"x51"

1) Hole - 50

4) MH Step ML-10-TDS-NCR - 10"

0 lb Structure Notes:

3319 lb PLAN LABEL: Q

8816 lb

442 lb

0 lb

0 lb

0 lb

0 lb

0 lb



Structure Total:

12578 lb

1. HOE 525 SET (F/G/H) PROVIDED BY ICAST.
 2. PER ASTM C478 SPECIFICATIONS.
 3. CONCRETE = 4,000 PSI AT 28 DAYS.
 4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .18)
 - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: PER ASTM A615 (GRADE 60)
- AS SHOWN BELOW.

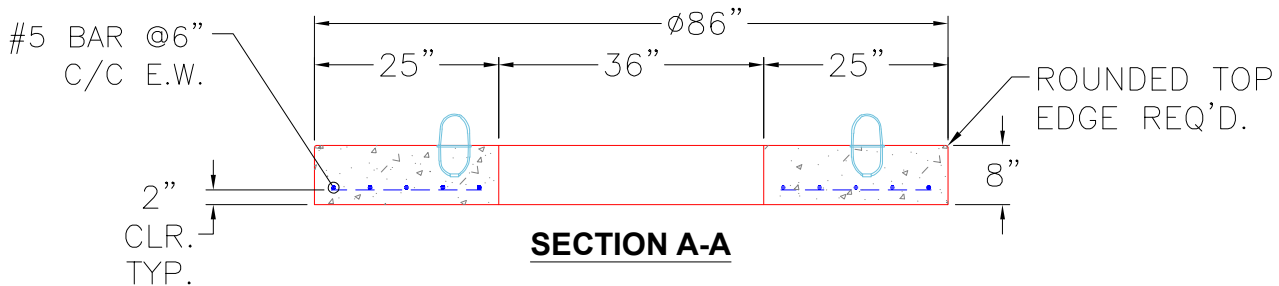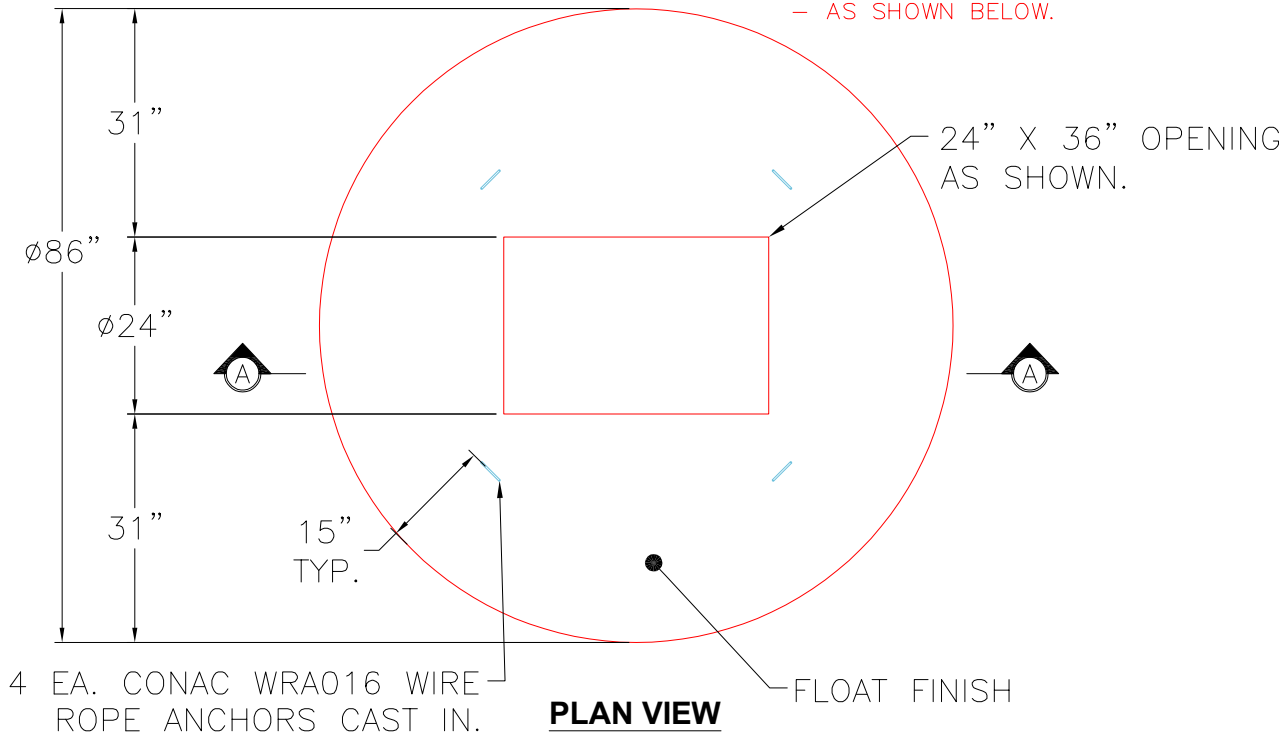

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 7"

Height (Ext): 8"

Weight (Net): 3319 lb
Volume (Net): 0.85cu.yd
