

Job Name: 25-2397 Sandy Springs Sec. 2
Job Location: Elizabethtown, KY 42701
Contractor: Dirt Works Unlimited, LLC.

Plant: 100

7/9/2026 2:52:15 PM

Tech: Jared - A

PC: Thomas Ryan



Structure ID: W



P2 MH048LD07-24X36RECT

MH FLAT TOP w/24"x36" Hole

- P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x36" Hole - 7"
P1) 48" - MH BASE Custom Ht - 31"
1) CASTING - HOE 525 SET (F/G/H)
1) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) DOGHOUSE INVRTD - 30"x30"
1) Hole - 20
1) Hole - 24
2) MH Step ML-10-TDS-NCR - 10"

- 0 lb
1044 lb
2792 lb
442 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
- Structure Notes:**
PLAN LABEL: W
1. HOE 525 SET (F/G/H) PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 4278 lb

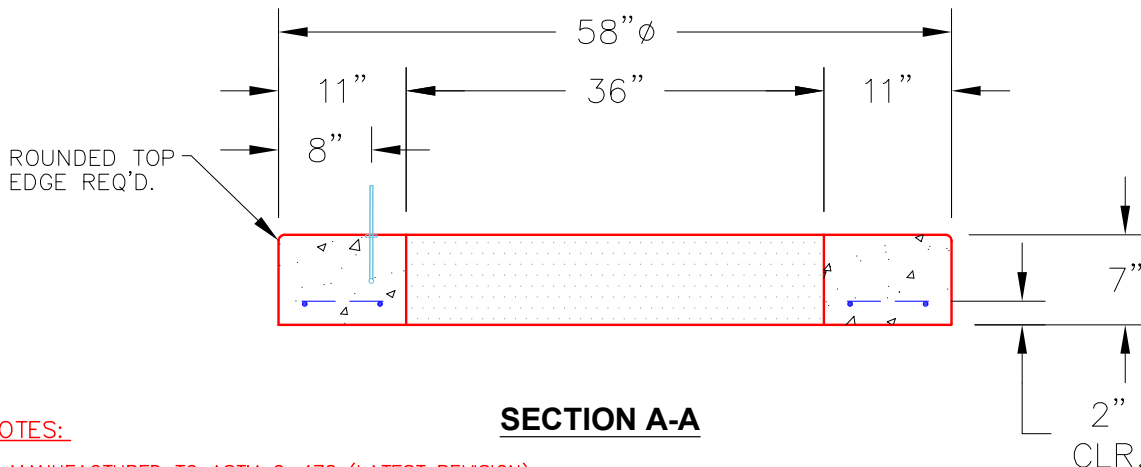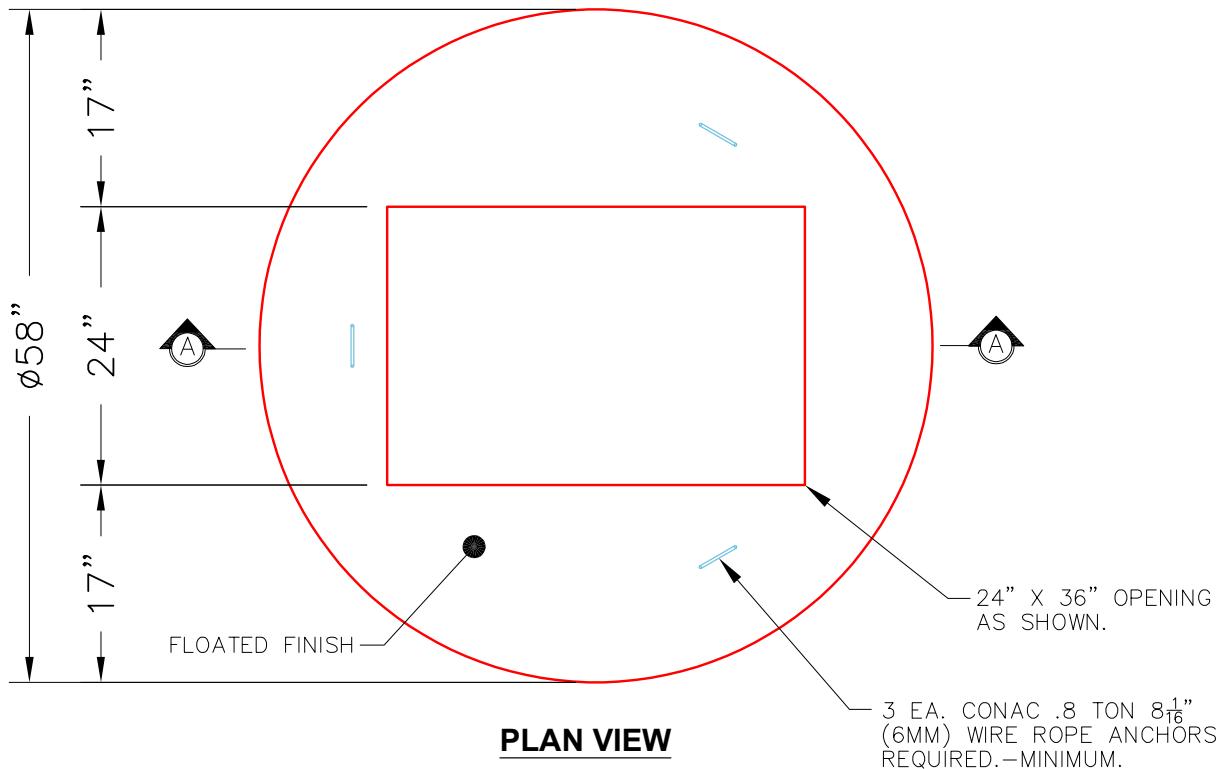

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 5,000 PSI AT 28 DAYS.
3. REINFORCING: #4 BAR @ 10" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 5"

Height (Ext): 7"

Weight (Net): 1044 lb
Volume (Net): 0.27cu.yd
