


Job Name: 25-2397B - Sandy Springs Section 2 Sanitary Job Location: Elizabethtown, KY 42701 Contractor: Gary Clifford	Plant: 100	Tech: J. Horsley	
	5/27/2026 2:56:18 PM	PC: T. Lewis	

Structure ID: MH 2


P3 GR4

GRADE RING F/F


P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING F/F - 4" P2) 48" - ECC CONE w/ 24" HOLE F/G - 42" P1) 48" - MH BASE T/n - 30" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 DD (DBL Bands) 6) MH Step ML-10-TDS-NCR - 10"	0 lb 270 lb 3200 lb 3282 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 8474 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: (1) #3 HOOP CENTERED (GRADE 60)
--	---	---

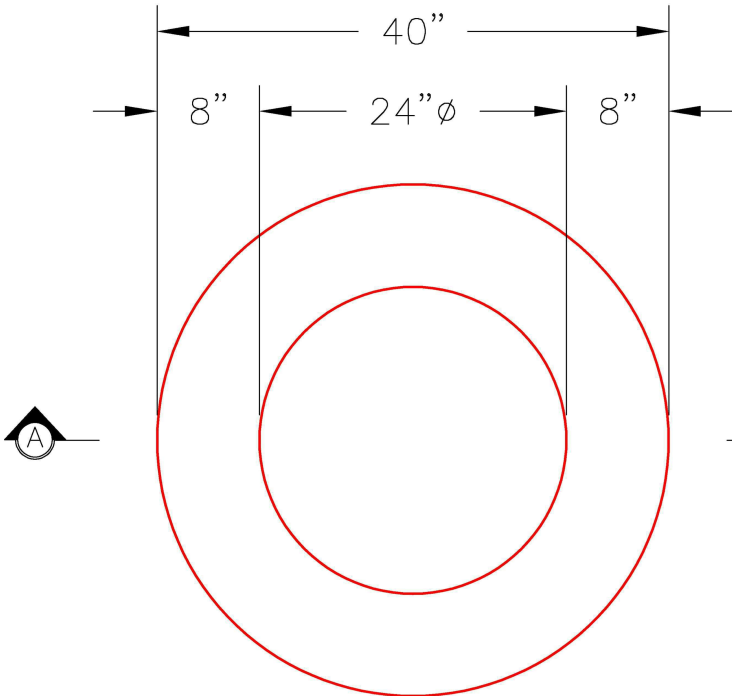

PLAN VIEW



ISOMETRIC VIEW

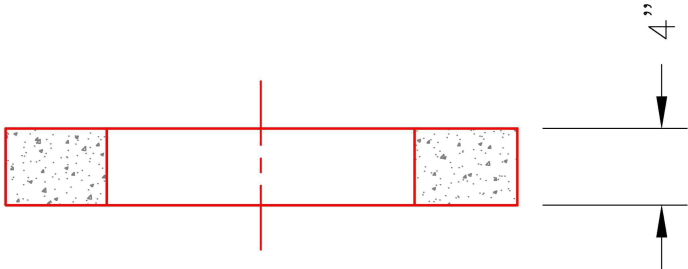

SECTION A-A

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 4"	Weight (Net): 270 lb Volume (Net): 0.07cu.yd
----------------------------------	--------------------------------	--------------------	------------------	---
