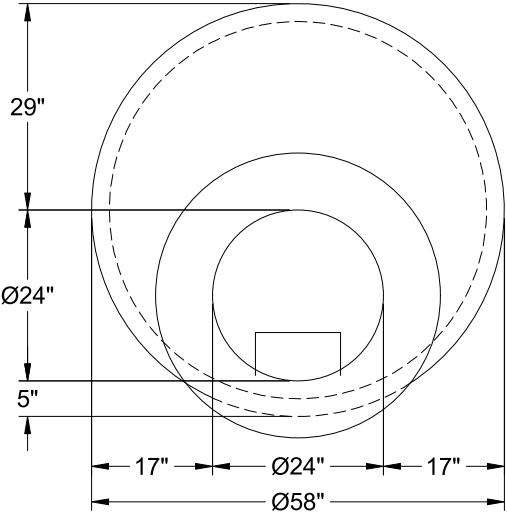



Job Name: 25-2397B - Sandy Springs Section 2 Sanitary Job Location: Elizabethtown, KY 42701 Contractor: Gary Clifford		Plant: 100 5/27/2026 2:56:18 PM	Tech: J. Horsley PC: T. Lewis	
Structure ID: MH 3				
P2 MH048CN30		ECC CONE w/ 24" HOLE F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING F/F - 4" P2) 48" - ECC CONE w/ 24" HOLE F/G - 30" P1) 48" - MH BASE T/n - 24" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 DD (DBL Bands) 4) MH Step ML-10-TDS-NCR - 10"		0 lb 270 lb 2050 lb 2863 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 6905 lb	<u>Structure Notes:</u> 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS REQUIRED 5. HOE MC-315 FRAME & COVER "SANITARY" SUPPLIED BY ICAST	
				
 48" - ECC CONE w/ 24" HOLE F/G - 30" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 2050 lb Volume (Net): 0.41cu.yd
