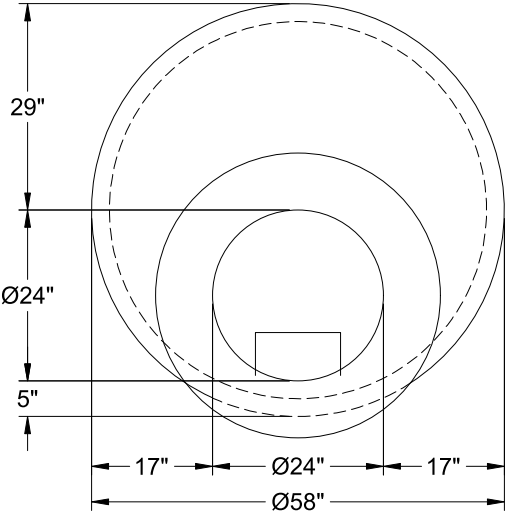



Job Name: 25-2422 - Woodland Springs Section 3 (Sanitary) Job Location: Clarksville, TN Contractor: Byard Construction, LLC		Plant: 100 5/14/2026 2:17:25 PM	Tech: Jared - A PC: A. Chambers	
Structure ID: A-1				
P4 MH048CN30CDARED		ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G		
P5) 24" - CASTING HEIGHT - 6" P4) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" P3) 48" - MH RISER w/ConBlock-CDA Red T/G - 72" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 72" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE CONBLOCK CDA RED 1) CASTING - JBS 1155 F/C SANITARY 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 17) MH Step ML-10-TDS-NCR - 10"		0 lb 1961 lb 5030 lb 5030 lb 3330 lb 1440 lb 0 lb 0 lb 0 lb 250 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 17057 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. CONBLOCK CDA RED ADMIXTURE REQUIRED 5. STEPS REQUIRED 6. JBS 1155 FRAME & COVER "SANITARY" SUPPLIED BY ICAST	
				
48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" - (P4) 				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 1961 lb Volume (Net): 0.5cu.yd
