




Job Name: 25-2422 - Woodland Springs Section 3 (Sanitary) Job Location: Clarksville, TN Contractor: Byard Construction, LLC					Plant: 100 5/14/2026 2:16:58 PM		Tech: Jared - A PC: A. Chambers				
Structure ID: A-10											
P2 MH048RS24CDARED			MH RISER w/ConBlock-CDA Red T/G								
P4) 24" - CASTING HEIGHT - 6" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 24" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE CONBLOCK CDA RED 1) CASTING - JBS 1155 F/C SANITARY 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 2) PSX - 8QRS-S NYLO 7) MH Step ML-10-TDS-NCR - 10"					0 lb 1961 lb 1677 lb 3336 lb 1440 lb 0 lb 0 lb 0 lb 250 lb 0 lb 0 lb 8 lb 13 lb 0 lb ----- 8685 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. CONBLOCK CDA RED ADMIXTURE REQUIRED 5. STEPS AT 180 DEGREES 6. JBS 1155 FRAME & COVER "SANITARY" SUPPLIED BY ICAST				
Rim: 469.8' Rim to Invert: 7.35' Slack: 0.2" Sump: 2" Step Position: 180°					Structure Total:						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

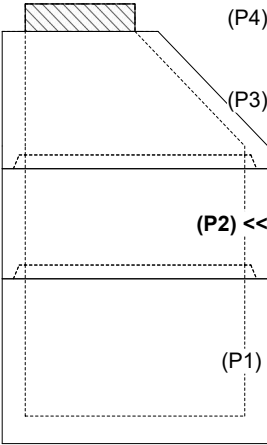

RIGHT-SIDE UP VIEW (int. dimensions)

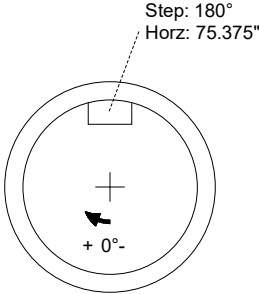

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 24" Height (Ext): 24"	Weight (Net): 1677 lb Volume (Net): 0.43cu.yd
----------------------------------	------------------------------------	--	--	--
