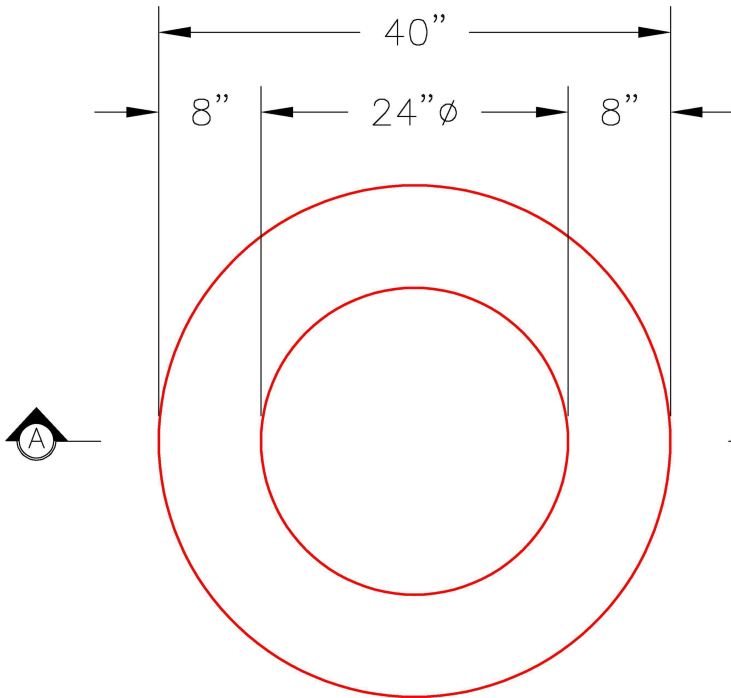

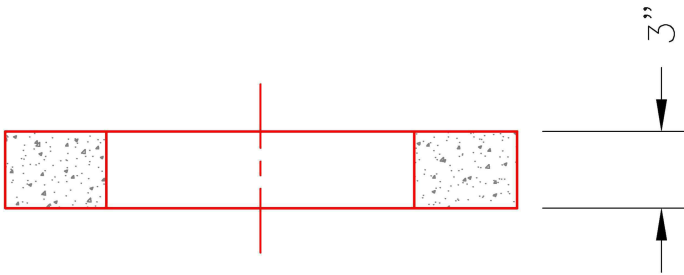


Job Name: 25-2422 - Woodland Springs Section 3 (Sanitary)		Plant: 100	Tech: Jared - A	
Job Location: Clarksville, TN		5/14/2026 2:17:27 PM	PC: A. Chambers	
Contractor: Byard Construction, LLC				
Structure ID: A-5				
P4 GR3CDARED		GRADE RING w/ConBlock-CDA Red F/F		
P5) 24" - CASTING HEIGHT - 6" P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 3" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42" P2) 48" - MH RISER SPECIAL w/ConBlock-CDA Red T/G - 72" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 36" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE CONBLOCK CDA RED 1) CASTING - JBS 1155 F/C SANITARY 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) PSX - 8QRS DD 13) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 3116 lb 5009 lb 3749 lb 1440 lb 0 lb 0 lb 0 lb 250 lb 0 lb 0 lb 0 lb 16 lb 6 lb 0 lb ----- Structure Total: 13789 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: (1) #3 HOOP CENTERED (GRADE 60) 4. CONBLOCK CDA RED ADMIXTURE REQUIRED	
 PLAN VIEW  ISOMETRIC VIEW  SECTION A-A				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 3"	Weight (Net): 202 lb Volume (Net): 0.05cu.yd
