



Job Name: 25-2471 - Texas Roadhouse Job Location: Danville, KY Contractor: McCain Bros Excavating LLC					Plant: 100 6/12/2026 3:42:51 PM		Tech: Jared - F PC: M. Sullivan				
Structure ID: 1											
P4 MH048RS24 MH RISER T/G											
P7) 24" - CASTING HEIGHT - 7" P6) 24" - GRADE RING F/F - 4" P5) 48" - ECC CONE w/ 24" HOLE F/G - 24" P4) 48" - MH RISER T/G - 24" P3) 60" - MH Transition Slab 48" Hole T/G - 13" P2) 60" - MH RISER T/F - 72" P1) 60" - P.I.P. BY OTHERS - BTM SLAB F/n - 0" 2) 60" - Conseal CS-202 1.00" 2) 48" - Conseal CS-202 1.00" 2) DOGHOUSE - 40"x42" 1) Hole - 30 10) MH Step ML-10-TDS-NCR - 10"						0 lb 270 lb 1550 lb 1677 lb 1928 lb 5413 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 10838 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. (7" TALL CASTING BY OTHERS) REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12). - RISER/WALLS (As .12) - TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18)			
Rim: 1036.1' Rim to Invert: 11.6' Slack: 0.2" Sump: 5" Step Position: 90°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

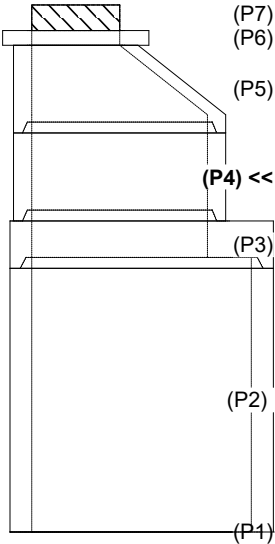


(P7)
(P6)
(P5)
(P4) <<
(P3)
(P2)
(P1)

RIGHT-SIDE UP VIEW (int. dimensions)



Step: 90°
Horz: 37.75"
+ 0°

INSIDE WALL DIMENSIONS



(P4)

0° 90° 180° 270° 360°

EXT
24"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 24" Height (Ext): 24"	Weight (Net): 1677 lb Volume (Net): 0.43cu.yd
----------------------------------	------------------------------------	--	--	--
